

0644RARE0302ND1SW-V2
44MM 5M X 3M CORNER LOG CABIN.

BEFORE YOU START PLEASE READ INSTRUCTIONS CAREFULLY

- Check the pack and make sure you have all the items listed in the parts list provided.
- When you are ready to start, make sure you have the right tools at hand (not supplied - see the equipment list on next page).
- Ensure you have enough time to build the product to ensure the building is water tight.

LOCATION FOR YOUR GARDEN BUILDING

A minimum of 600mm should be left around the perimeter of your garden building to allow access for maintenance, annual treatment and to allow air flow around the building.

Where possible you should avoid placing your garden building underneath large trees to prevent the tree causing damage to the building.

TIMBER

As with all natural materials, timber can be affected during various weather conditions. For the duration of heavy or extended periods of rain, swelling of the wood panels may occur. Warping of the wood may also occur during excessive dry spells due to an interior moisture loss. Unfortunately, these processes cannot be avoided but can be helped. It is suggested that the outdoor building is sprayed with water during extended periods of warm sunshine and sheltered as much as possible during rain or snow.

Once your garden building has been installed it will need to be treated within 14 days (weather permitting) and annually to prevent the timber from deteriorating and to waterproof it. This is required to maintain the anti-rot guarantee.

Log Cabins/Insulated Garden Rooms - Are supplied untreated and require a preservative and waterproofing treatment.

BUILDING A BASE

When thinking about where the building and where the base is going to be constructed: Ensure that there will be access to all sides for maintenance work and annual treatment.

Ensure the base is level and is built on firm ground, to prevent movement. Refer to the contents page for the base dimensions. The base should be slightly smaller than the external measurement of the building, i.e. The cladding should overlap the base, creating a run off for water. It is also recommended that the floor be at least 25mm above the surrounding ground level to avoid flooding.

TYPES OF BASE

- Concrete 75mm laid on top of 75mm hard-core.
- Slabs laid on 50mm of sharp sand.
- Wooden base - Levelled / on posts / ground screws.

Whilst all products manufactured are made to the highest standards of safety and in the case of children's products independently tested to EN71 level, we cannot accept responsibility for your safety whilst erecting or using this product.



x2 All buildings should be erected by two adults



Winter = High Moisture = Expansion
 Summer = Low Moisture = Contraction



2mm Drill bit

For ease of assembly, you **MUST** pilot drill all screw holes and ensure all screw heads are countersunk.




CAUTION
 Every effort has been made during the manufacturing process to eliminate the prospect of splinters on rough surfaces of the timber. You are strongly advised to wear gloves when working with or handling rough sawn timber.



For ease of assembly use a rubber mallet to fit the log boards. Do NOT use a heavy hammer.



Ensure to measure and check before cutting boards.



It is advisable to use a hand saw when cutting roof and floor boards.



To ensure log boards are even, use a spirit level to check each layer has been installed correctly.

Screws & Nails



Bolts



To identify the fixings required for each step use a measuring tape.

**REGISTER FOR YOUR
 ANTI-ROT
 GUARANTEE TODAY**

PLEASE SCAN HERE:

In all instances for assistance with your product, please contact us via our customer portal: <https://www.mgplistics.co.uk/>.

Mercia Garden Products Limited,
 Sutton On Trent,
 Newark,
 Nottinghamshire,
 NG23 6QN



TO DO LIST

- Find a suitable location to build *(see front cover for further information)*.
- Build a base *(see front cover for further information)*.
- Check the base is flat, level, clear of debris and has 60cm clearance on all sides.
- Check you have the required equipment / tools.
- Check you have all the product items listed *(if you have missing or damaged parts please scan the QR code below to visit our online customer portal)*
- Install the product as per the step by step instructions within this pack.
- Prepare the product ready for treatment (This may include sanding).
- Apply a preserving and a waterproofing treatment within 14 days *(weather permitting)* of installation.
- Register for your anti rot guarantee *(scan the QR below)*.
- Tidy the build area and dispose of any remaining parts responsibly.
- Maintain your building *(see the manufacturers recommendations at the back of this pack)*.

EQUIPMENT LIST

- Hammer
- Mallet
- Flat Head Screwdriver
- Drill
- Drill Bit Set
- Phillips and Slotted Bit Sets
- Tape Measure
- Hand Saw
- Spirit Level
- Ladders/Steps
- Stanley Knife/Cutting Tool
- Sand Paper
- Gloves
- Silicone (For Windows Only)
- Wood Filler (Optional)
- Timber Preservative Treatment
- Timber Water Proofing Treatment
- Treatment Mixing Stick
- Paint Brush/Sprayer/Roller

NEED EXTRA SUPPORT

If you are unsure that your base preparation will be suitable, please contact us via our customer portal to discuss this further.

Alternatively, you can visit our website or MGP Logistics Online Portal for some further sheducation.

Website:

<https://www.merciagardenproducts.co.uk/sheducation>

MGP Logistics Online Portal:

<https://www.mgplogistics.co.uk/>

Here you will find plenty of useful information that'll help with most pre-installation and maintenance queries.

PLEASE SCAN HERE:



ANY QUESTIONS?

Scan the QR code to contact us via our customer portal.

NOTES

Before assembly
please make sure you have a
suitable base ready to erect your
building



MADE IN GREAT BRITAIN

PLEASE SCAN HERE:



ANY QUESTIONS?

Scan the QR code to
contact us via our customer
portal.


Tip: Labelling your parts, using a pencil and masking tape,
may help you to identify them easier when you need them.

NO.1 STARTER BOARD


Overall Dimensions: Width = 5098mm
Depth = 3168mm
Height = 2742mm

Base Dimensions: Width = 4818mm
Depth = 2818mm

Left Handed

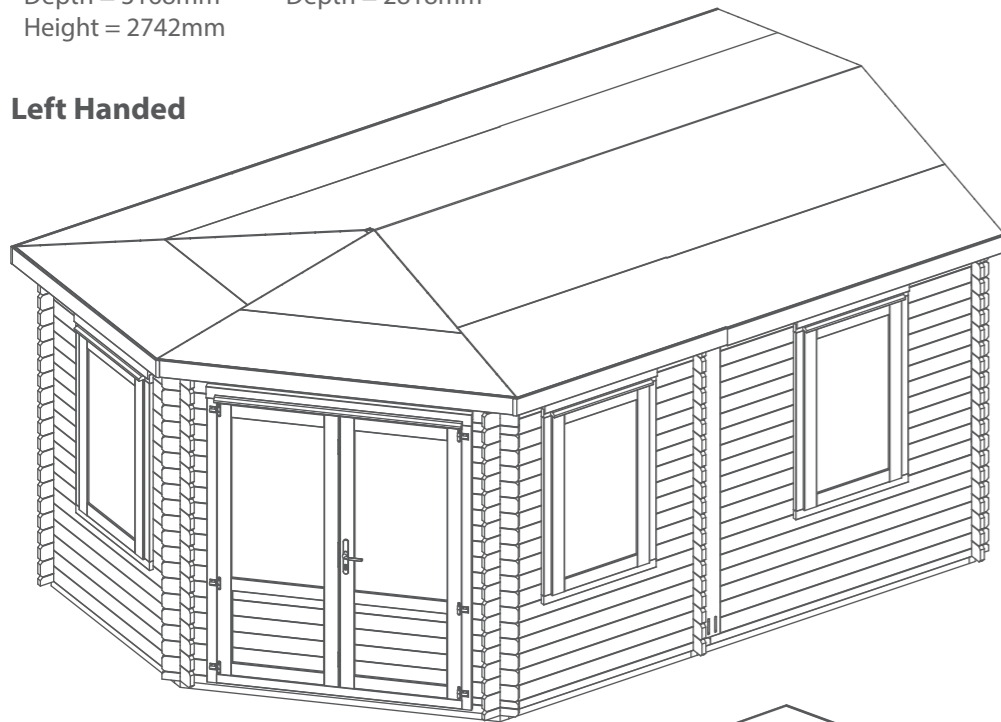

Right Handed

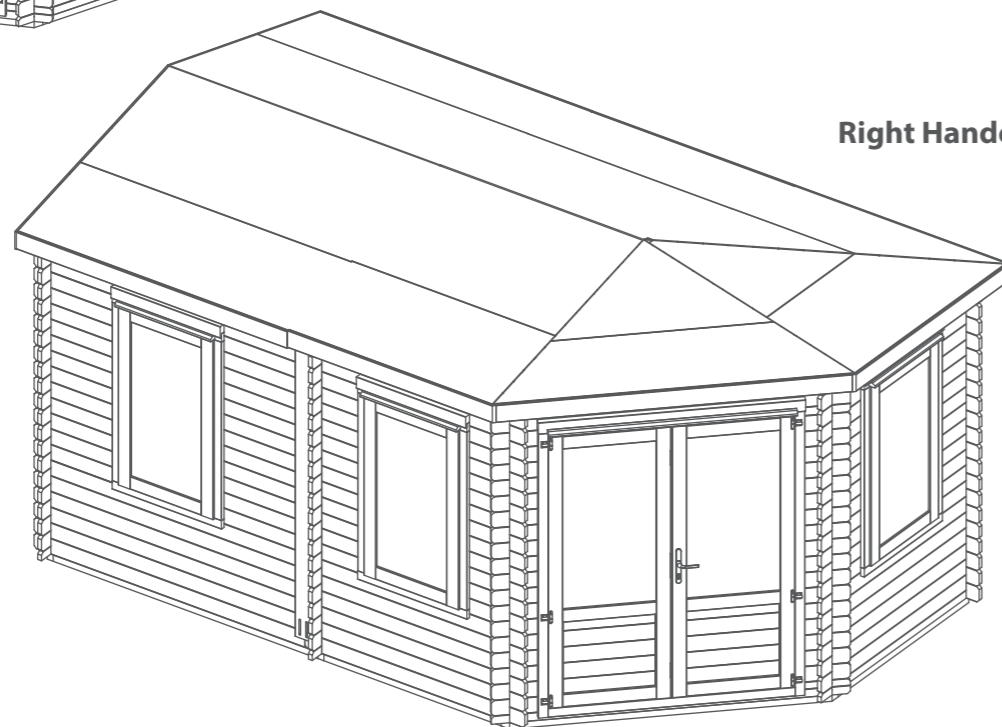

****All components and the nail bag from 3m x 3m corner cabin (0644CSNE0303HGDD2SW-V1) will be required to construct the 5m x 3m corner lodge. These components are shown in the 3m x 3m corner cabin instructions.****

5x3 Log Boards Contents:

- 

74 Starter Board - 44x66x232mm QTY 2 (Right handed only)
LB44RT66-B-232mm
- 

75 Starter Board - 44x66x2000mm QTY 2 (Left handed only)
LB44RT66-B-2000mm
- 

76 Log Board - 44x120x2000mm QTY 27
LB44-B-2000mm
- 

77 Log Board - 44x120x232mm QTY 38
LB44-B-232mm
- 

78 Log Board - 44x120x625mm QTY 12
LB44-B-625mm
- 

79 Log Board - 44x120x625mm QTY 12
LB44-C-625mm
- 


80 Log Board - 44x120x2000mm QTY 1
LB44-BD-2000mm (1 x Window Notch cut out)
- 


81 Finisher Board - 44x66x2000mm QTY 2 (Right handed only)
LB44-BH66-2000mm (66mm height board)
- 


82 Finisher Board - 44x80x880mm QTY 4
LB44RG80-C-880mm
- 


83 Finisher Board - 44x80x70mm QTY 2
LB44RG80-C-70mm


5x3 Fixing Kit Contents:

- 

84 **Roof Purlin - 45x120x3522mm QTY 1**
F45120-AE-3522mm
- 

85 **Bearer - 44x58x1884mm QTY 11**
F4458-1884mm-PT
- 

86 **Floor Board - 16x121x2726mm QTY 19***
MB16-2726mm
- 

87 **Roof Board - 16x121x2000mm QTY 32***
MB16-2000mm
- 

88 **Double Storm Brace - 16x120x2110mm QTY 4**
S16120-2110mm

**This part will be longer than needed and requires cutting to size when used. This will be explained when required within the instruction step.*

Note: one piece may be required to be cut into multiple different sizes. Do not dispose of off-cuts until the building is fully constructed as they may be needed in another step.

Please note;

The components you have been provided with will allow you to construct your cabin to be either left handed or right handed, however not all components are needed for both.


Depending if you construct your cabin to be left handed or right handed, you will have some parts left over that are not needed for your cabin.


Contents note:


The components listed below are featured in both contents lists for the 3m x 3m Corner Cabin (0644CSNE0303HGDD2SW) as well as the 5m x 3m Corner Lodge.


The component numbers listed below are the same component numbers as listed in the 3m x 3m Corner Cabin instructions, some numbers may be out of chronological order or skipped to satisfy this.


Please see the **total combined quantity required** for the 5m x 3m Corner Lodge (3m x 3m Corner + 3m x 2m Pack B) listed next to the components below.


- 


4 **Log Board - 44x120x3000mm QTY 1 - Combined Total Required x 40**
LB44-A-3000mm
- 


21 **Finisher Board - 44x66x3000mm QTY 1 - Combined Total Required x 2**
LB44-AH66-3000mm (64mm high board)
- 


26 **Gable QTY 1 - Combined Total Required x 2**
AI-0644LOGC3-G-V1
- 


29 **Roof Truss A- 40x140x1604mm QTY 6 - Combined Total Required x 11**
AI-06LOGC3RTA-V1 (2 x 76 deg parallel cuts)
- 

37 **Bearer - 44x58x2818mm QTY 2 - Combined Total Required x 3**
F4458-2818mm-PT
- 

48 **Fascia - 16x120x2000mm QTY 2* - Combined Total Required x 4**
S16120-2000mm
- 

51 **Closure Trim - 16x28x2400mm (approx length) QTY 4 - Combined Total Required x 14**
S1628-2400mm
- 


52 **Storm Brace - 44x27x2000mm QTY 4 - Combined Total Required x 12**
F2744-2000mm
- 

54 **Felt**
- 

55 **2mm Spacer QTY 5 - Combined Total Required x 10**
PI-07-0208 (20x100x2mm)


Window Contents:

68



Window QTY 1
Combined Total Required x 3
 AI-06LOGDGSW702X1264-V1

69




Window Frame QTY 1
Combined Total Required x 3
 AI-0644DGWF808X1417-V1

70



Rain Guard - 28x44x710mm QTY 1 - Combined Total Required x 3
 RG2844-710mm

71

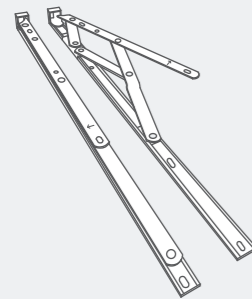

Friction Hinge Pair - QTY 1 - Combined Total Required x 3 pairs
 PI-07-0236 (Pair)

72



Window Handle QTY 1 - Combined Total Required x 3
 PI-07-0235

73



6mm Spacer QTY 5 - Combined Total Required x 10
 PI-07-0238 (20x100x6mm)

Screw Pack.

There may be extra screws present in the pack.



PLEASE SCAN HERE:



Missing parts?

Scan the QR code to visit our customer portal where you can quickly raise any missing or damaged parts and get a replacement sent out ASAP.




Pre-assembly

***Please note:**

Each board interlocks at either end in a staggered pattern.

Before securing ensure that the boards are fitted properly in their respective tongue's and groove's.

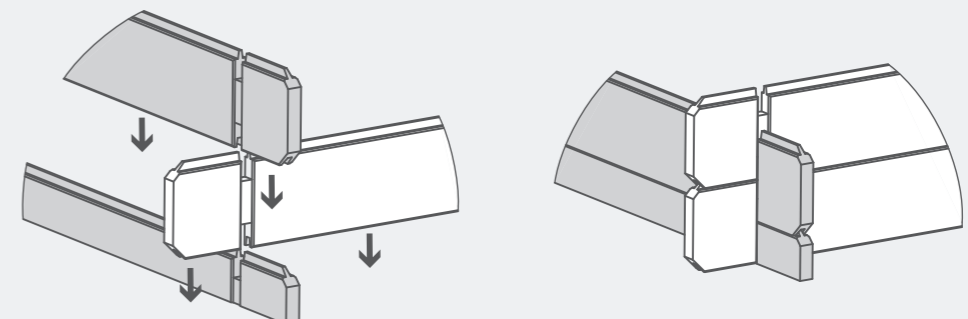

Pre - Assembly

*Please note

To construct the 5m x 3m Corner Lodge, **all components from the 3m x 3m Corner Cabin (0634CSNE0303HGDD2SW) will be required as well as all components from this set of instructions.**

Components for the 3m x 3m Corner Cabin can be found in the contents of the 3m x 3m Corner Cabin instructions.

****DO NOT CONSTRUCT USING THE 3M X 3M CORNER CABIN INSTRUCTIONS IF YOU ARE CONSTRUCTING THE 5M X 3M CORNER LODGE.****

Step 1

- Parts Needed - No. 37 QTY 1
- No. 38 QTY 1
- No. 43 QTY 1
- No. 44 QTY 1
- No. 45 QTY 1

Lay the bearers (No. 37, 38, 43, 44 & 45) onto a firm and level base (*free from areas where standing water can collect*) ensuring the bearers are flat and level and the ends are flush, as shown.



Ensure to lay the bearers so the widest face (58mm) is positioned on the flat, and the smaller face (44mm) is positioned as the height, as shown.

Fix the bearers together using 2x90mm screws per corner.

Once secured, ensure the bearers are square by measuring from corner to corner, making sure the measurements are equal. If the bearers are not aligned equally, unscrew, adjust and re-align accordingly.

10x90mm Screws

Important: Pre-drill before fixing screws.

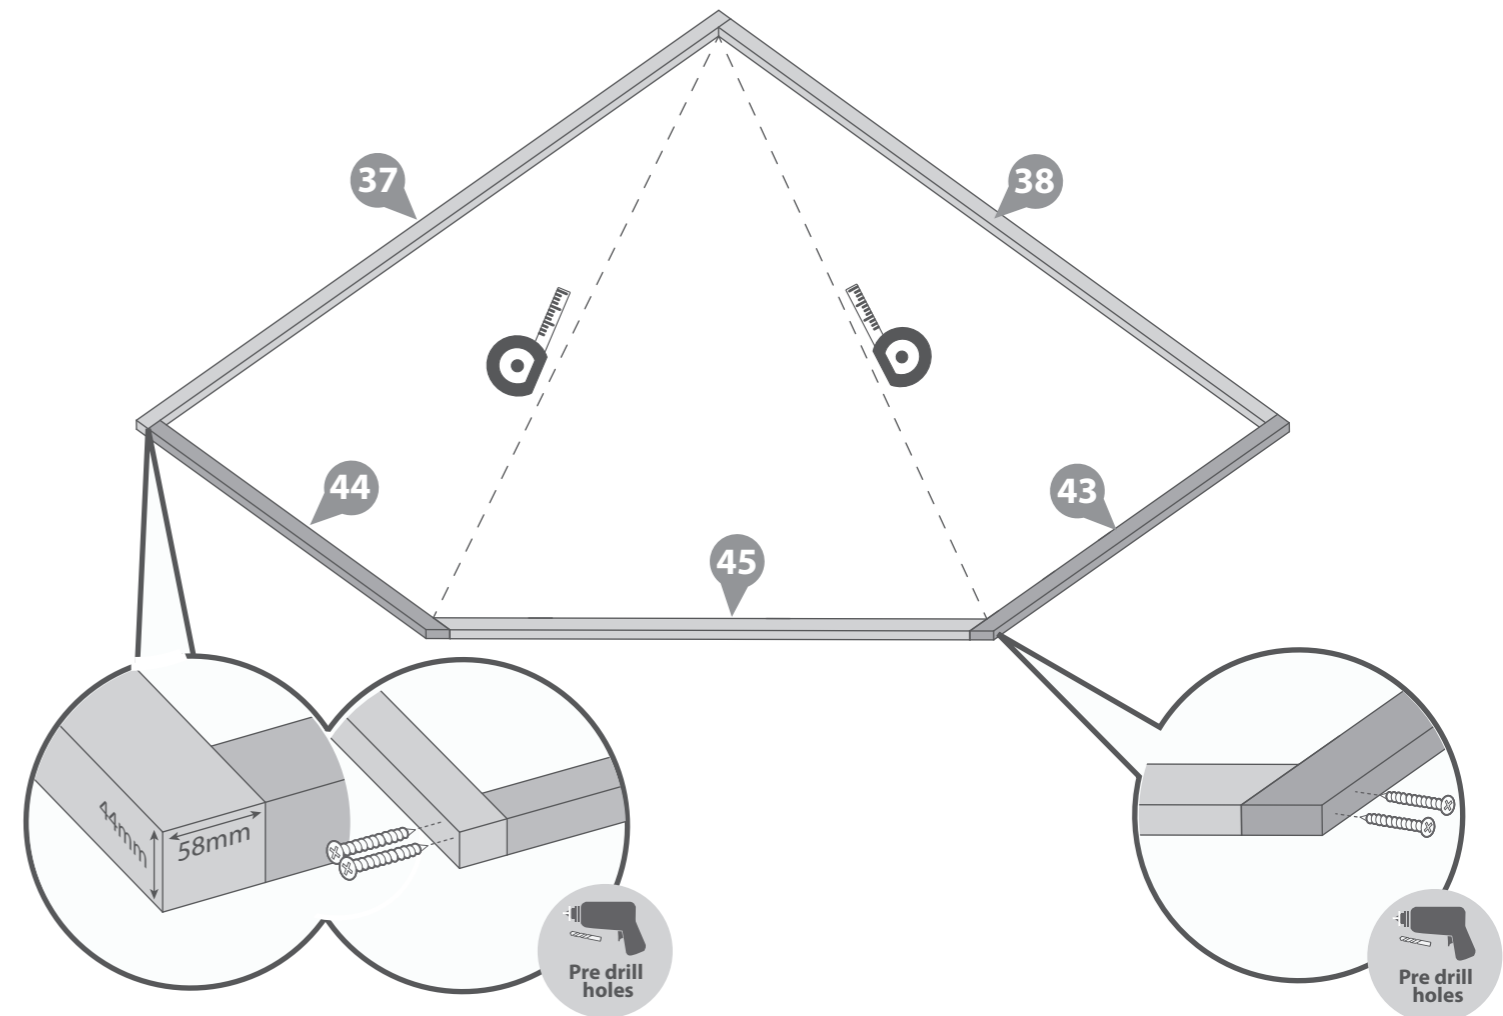

Step 2

- Parts Needed - No. 38 QTY 5**
No. 39 QTY 1
No. 40 QTY 1
No. 41 QTY 1
No. 42 QTY 1


Following the same method shown in the previous step, arrange the remaining bearers (**No. 38, 39, 40, 41 & 42**) inside the assembled frame, ensuring each piece is flush and level.

Ensure to lay the bearers so the widest face (58mm) is positioned on the flat, and the smaller face (44mm) is positioned as the height, as shown.

***Ensure there is an equal amount of space between each bearer.**

Secure each of the bearers in place by screwing through the outside framing into the framing behind using 2x90mm screws for each end of the bearer, as shown.

36x90mm Screws
Important: Pre-drill before fixing screws.

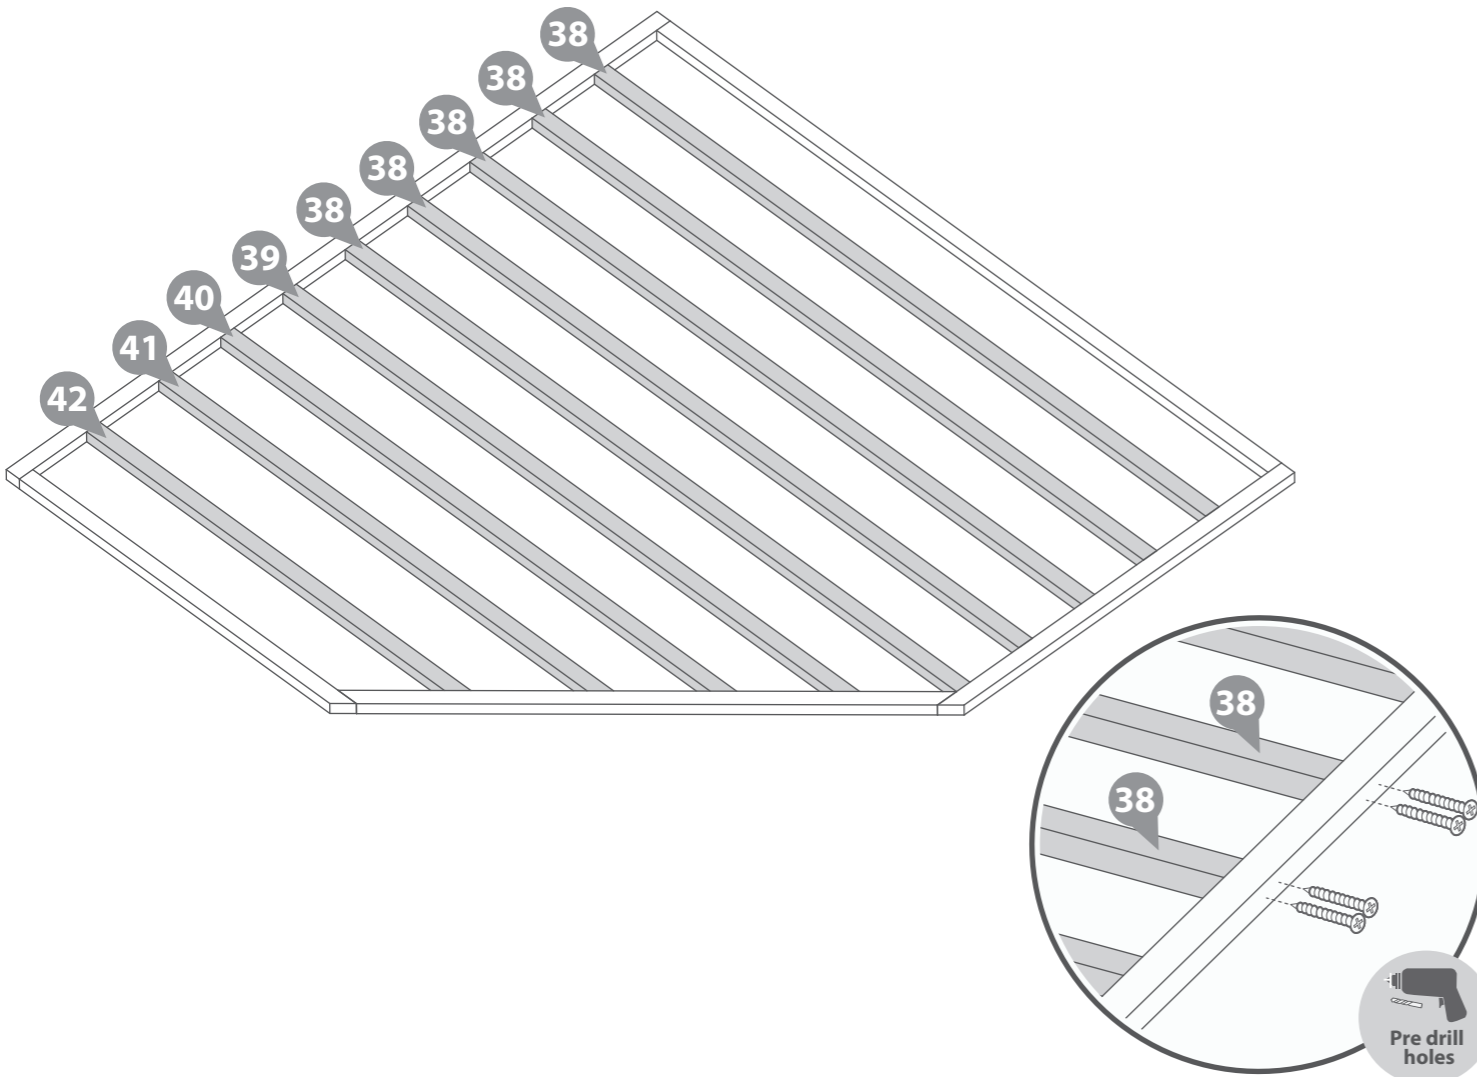

Step 3

- Parts Needed - No. 37 QTY 2**
No. 85 QTY 2



Lay the bearers (**No. 37 & 85**) onto a firm and level base (*free from areas where standing water can collect*) ensuring the bearers are flat and level and the ends are flush, as shown.

Ensure to lay the bearers so the widest face (58mm) is positioned on the flat, and the smaller face (44mm) is positioned as the height, as shown.

Fix the bearers together using 2x90mm screws per corner.

Once secured, ensure the bearers are square by measuring from corner to corner, making sure the measurements are equal. If the bearers are not aligned equally, unscrew, adjust and re-align accordingly.

8x90mm Screws
Important: Pre-drill before fixing screws.

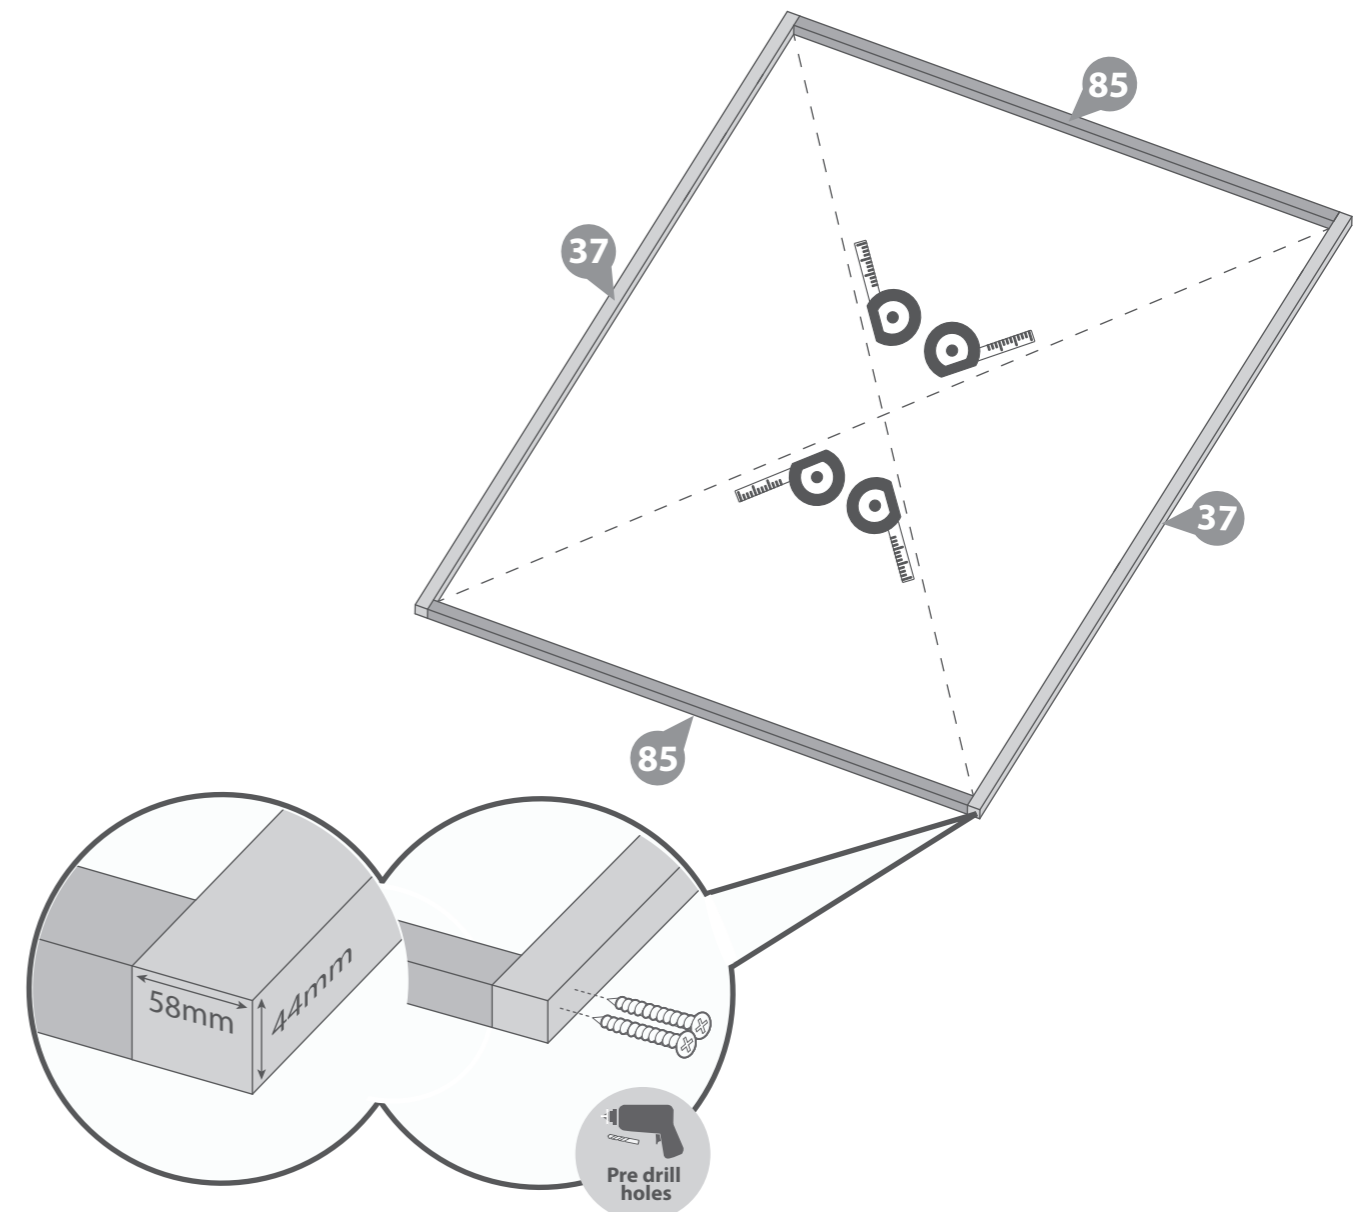

Step 4
Parts Needed - No. 85 QTY 9




Following the same method shown in the previous step, arrange the remaining bearers (No. 85) inside the assembled frame, ensuring each piece is flush and level.

Ensure to lay the bearers so the widest face (58mm) is positioned on the flat, and the smaller face (44mm) is positioned as the height, as shown.

***Ensure there is an equal amount of space between each bearer.**

Secure each of the bearers in place by screwing through the outside framing into the framing behind using 2x90mm screws for each end of the bearer, as shown.

36x90mm Screws
Important: Pre-drill before fixing screws.

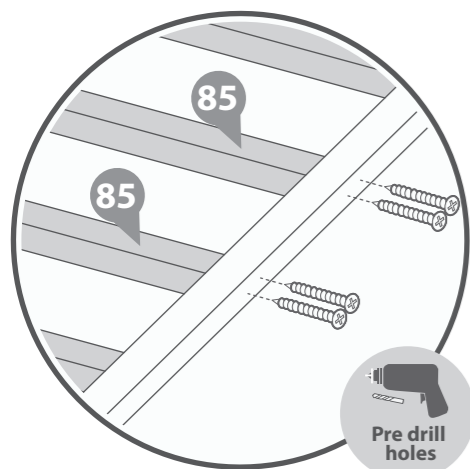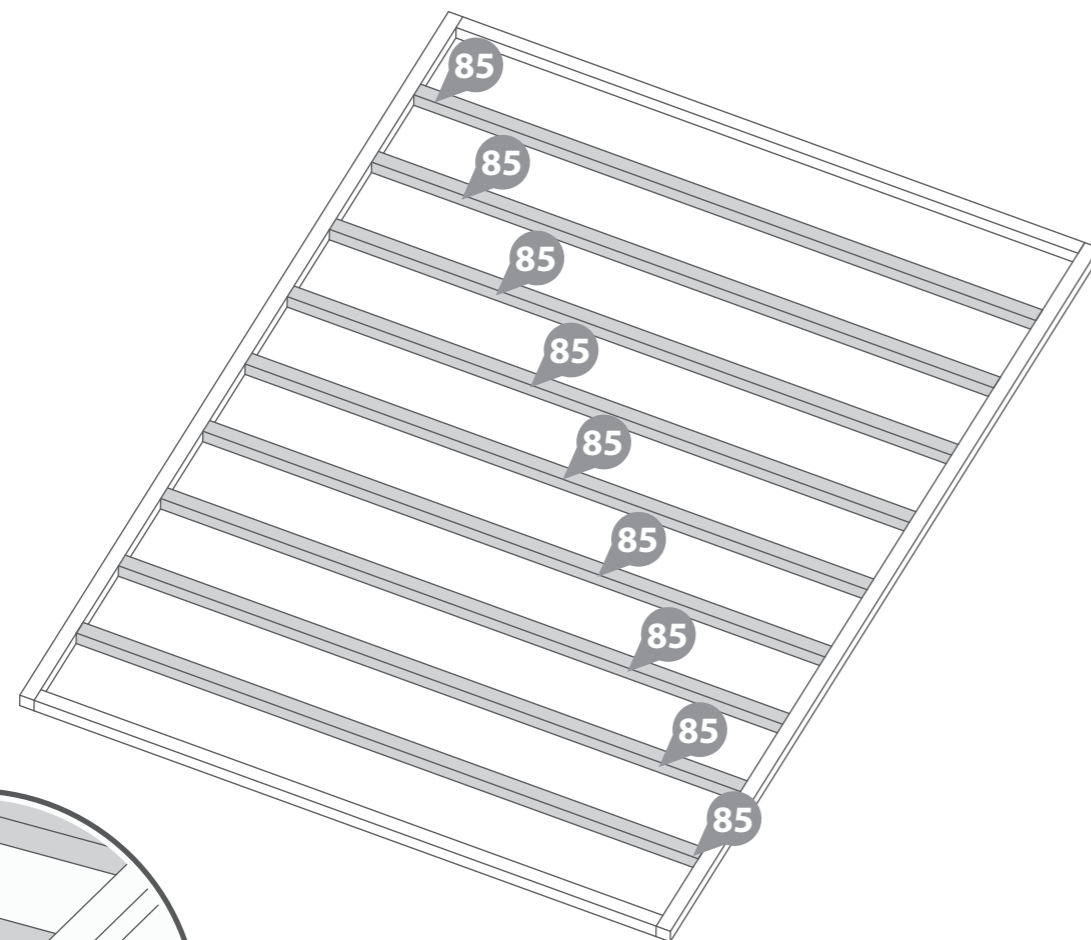


Step 5

**** Please Note: Your log cabin can be either Right Handed or Left Handed, dependant on your wants and needs (See Contents for image reference). Please ensure to construct your Log Cabin by following either the 'Left Handed' or 'Right Handed' instructions dependant on which side you choose.**


Align the two assembled bases together by the longest bearer as shown in the illustration.

Secure the base sections together using 10x90mm screws, ensuring to stagger the screws so they do not collide.


10x90mm Screws
Important: Pre-drill before fixing screws.



Left Handed

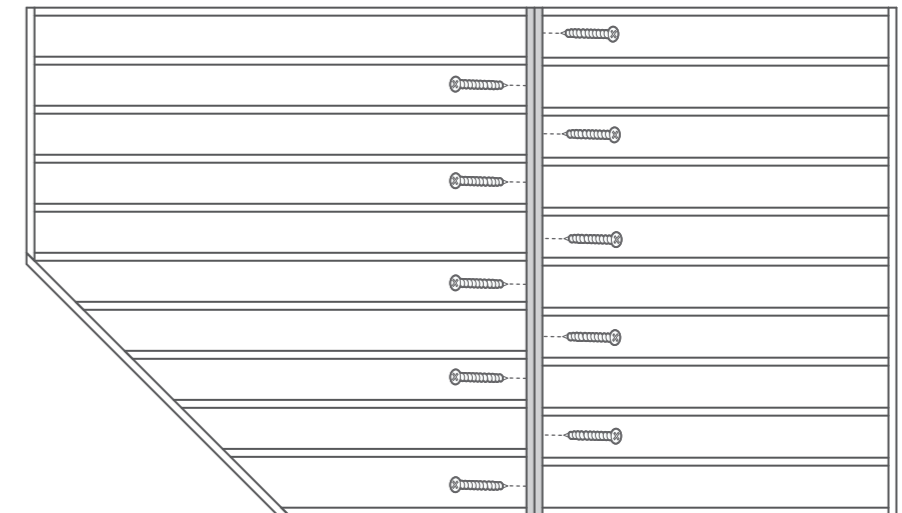

Right Handed

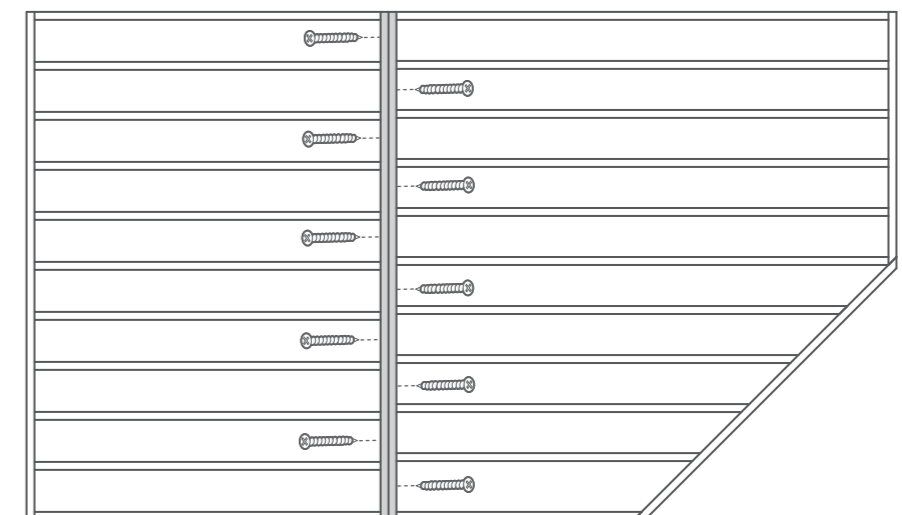

Step 6 - Left Handed

- Parts Needed -**
- | | |
|-------------|--------------|
| No. 1 QTY 1 | No. 7 QTY 1 |
| No. 2 QTY 1 | No. 75 QTY 2 |
| No. 3 QTY 1 | No. 77 QTY 2 |
| No. 4 QTY 1 | |

Place the starter boards (**No.1, 2, 3 & 75**) on to the assembled bearers and lightly position the first log boards (**No. 4, 7 & 77**) into the notches as shown.

Ensure the boards sit square on the base using the same method used in Step 1. Measure corner to corner, making sure the measurements are equal.

Once the boards are square, lift up the log boards (**No. 4, 7 & 77**) and fix the starter boards (**No.1, 2, 3 & 75**) in place by screwing through the notch into the bearer below, using 1x70mm screw per notch.


On either side, secure the Starter Board (**No. 75**) in place by screwing through the board at an angle into the adjacent starter board using 1x70mm screw per side, as shown.

Note: Use a mallet and a scrap piece of wood to gently persuade the log boards into place.

9x70mm Screws
Important: Pre-drill before fixing screws.



Left Handed

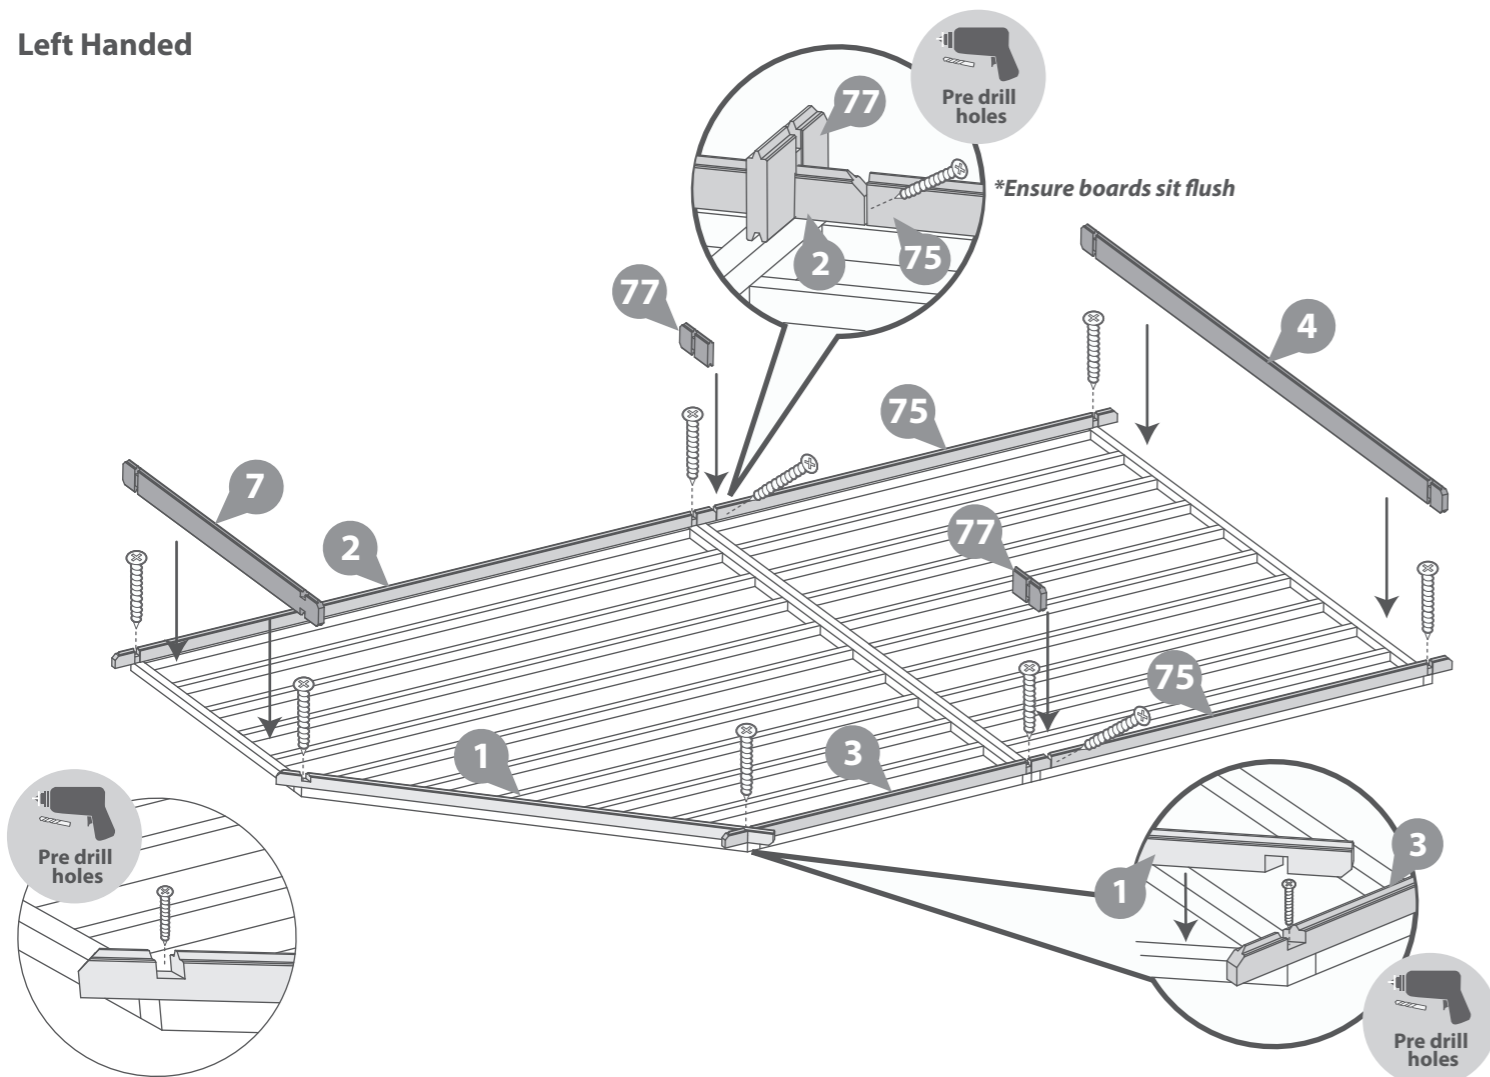

Step 6 - Right Handed

- Parts Needed -**
- | | |
|-------------|--------------|
| No. 1 QTY 1 | No. 7 QTY 1 |
| No. 2 QTY 1 | No. 74 QTY 2 |
| No. 3 QTY 1 | No. 76 QTY 2 |
| No. 4 QTY 1 | |

Place the starter boards (**No.1, 2, 3 & 74**) on to the assembled bearers and lightly position the first log boards (**No. 4, 7 & 76**) into the notches as shown.


Ensure the boards sit square on the base using the same method used in Step 1. Measure corner to corner, making sure the measurements are equal.

Once the boards are square, lift up the log boards (**No. 4, 7 & 76**) and fix the starter boards (**No.1, 2, 3 & 74**) in place by screwing through the notch into the bearer below, using 1x70mm screw per notch.


On either side, secure the Log Board (**No. 76**) in place by screwing through the board at an angle into the adjacent board using 1x70mm screw per side, as shown.

Note: Use a mallet and a scrap piece of wood to gently persuade the log boards into place.

9x70mm Screws
Important: Pre-drill before fixing screws.




Right Handed

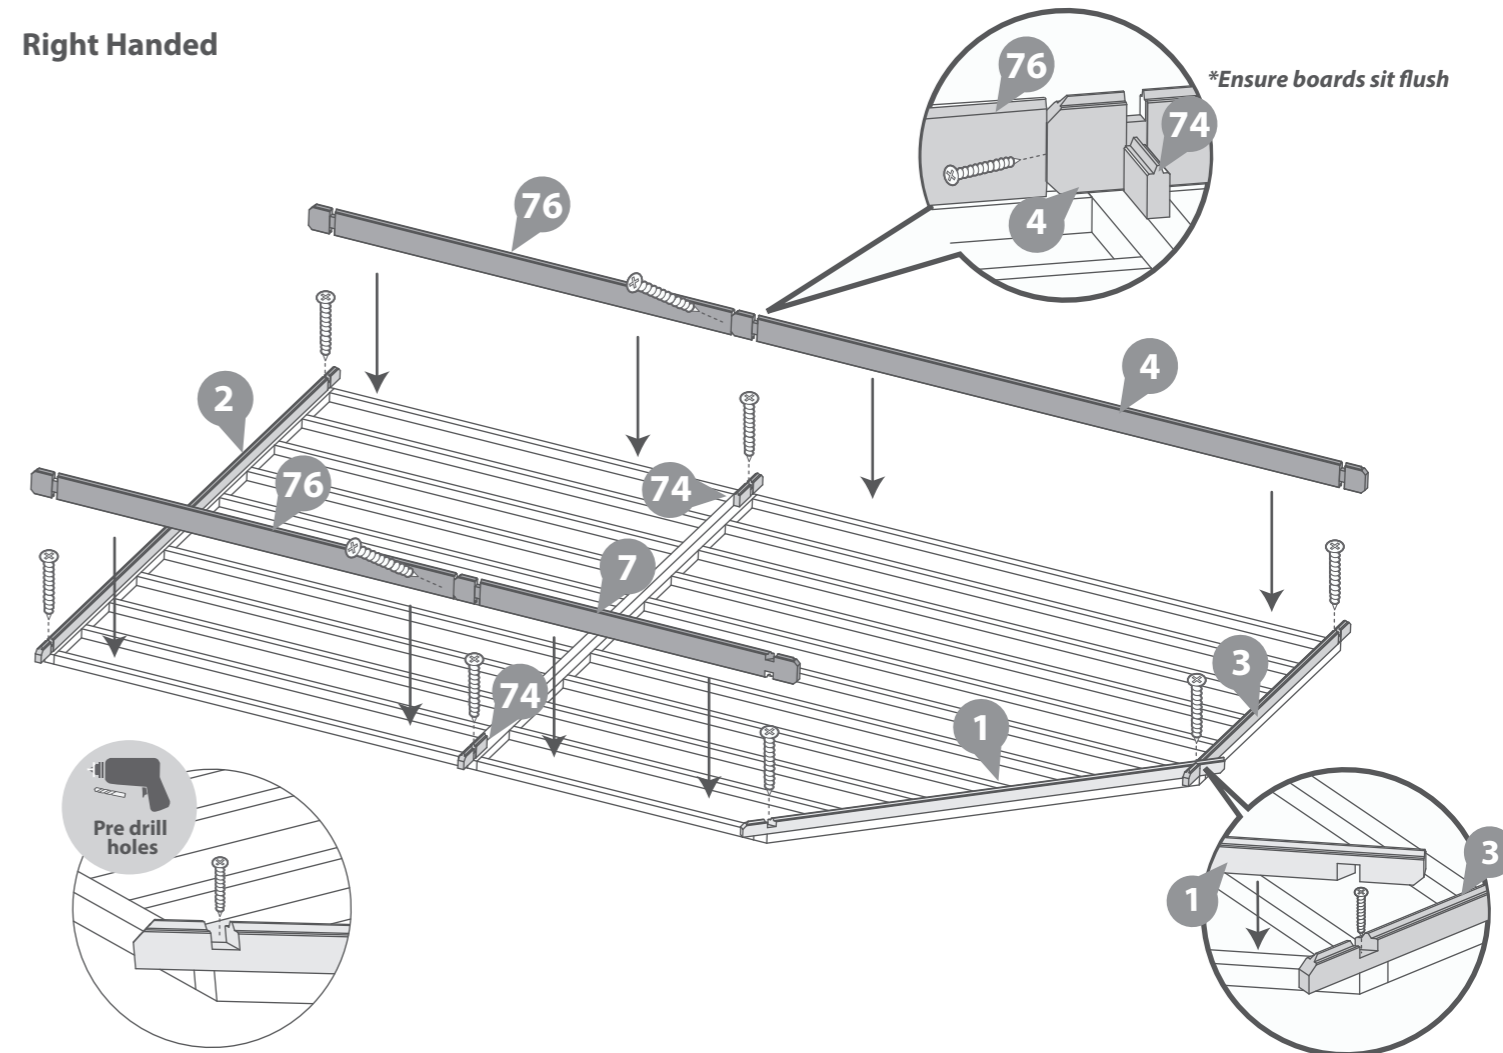

Step 7
Parts Needed - No. 6 QTY 1

Make the log cabin level by laying another board (**No. 6**) onto the right side of the cabin, as shown.



Secure the board in place by screwing through the notch using 1x70mm screw. Ensure to stagger the screw to avoid collision with the one below.

**Ensure that the boards are level and flush with each other as you lay each one.*


1x70mm Screws
Important: Pre-drill before fixing screws.




Rubber Mallet. Drill / Pre drill.




70mm screw

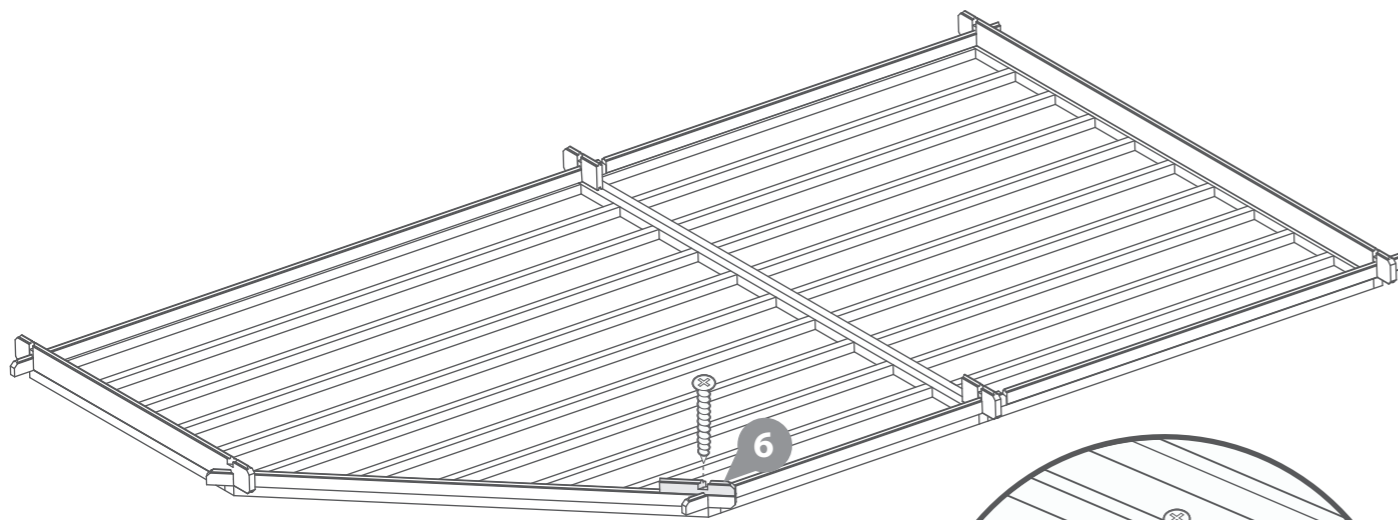

Left Handed

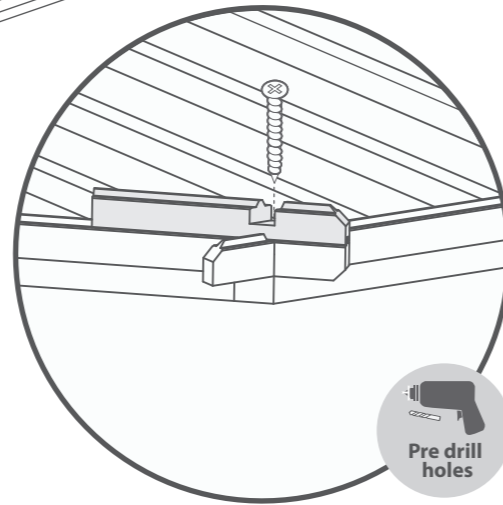


Pre drill holes

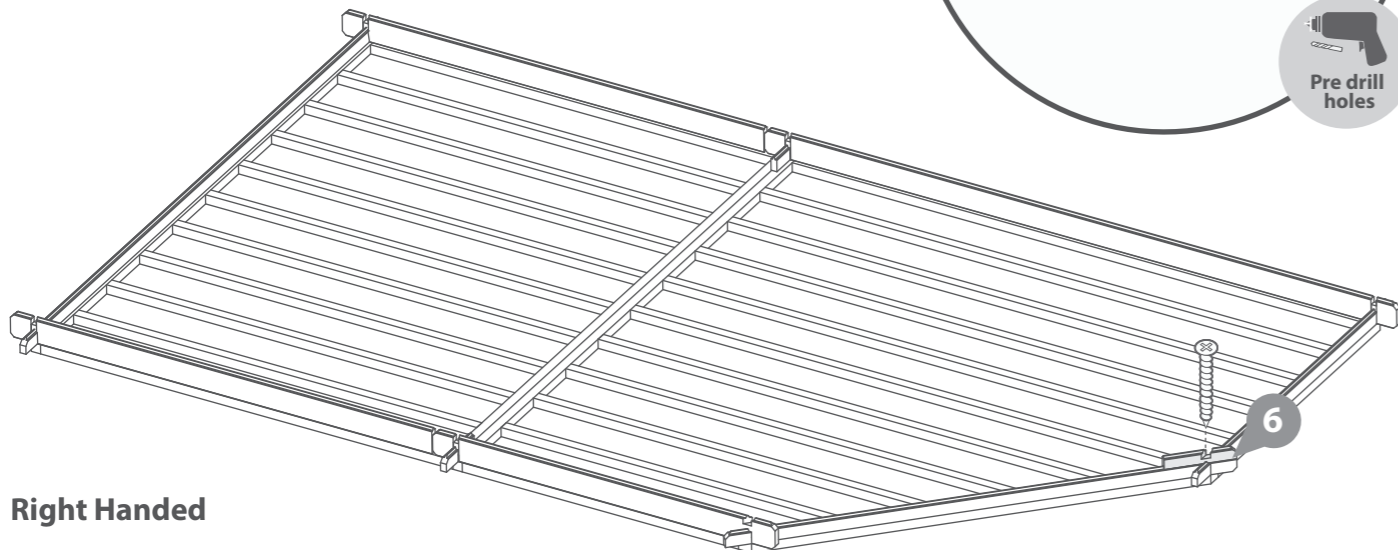

Right Handed

Step 8 - Left Handed

- Parts Needed -** No. 4 QTY 11 No. 10 QTY 6
 No. 7 QTY 5 No. 76 QTY 12
 No. 8 QTY 6 No. 77 QTY 12
 No. 9 QTY 6



Following the method shown in the illustration, lay the first 6 boards (**No. 4, 7, 8, 9, 10, 76 & 77**) off of the starter boards to create your first level.


**Ensure that the boards are level and flush with each other as you lay each one.*

Start by placing the front and back boards, interlocking them with the side boards. Then place the next side boards, interlocking with the front and back boards. Continue this method until you have placed **6 boards off of the starter boards on each side**, as shown.

Please note the right hand side of the door will be slightly higher. This will even out when the rest has been assembled.

Ensuring the boards (**No.76**) are level, flush and in line with the boards next to them, secure every other board in place by screwing through the side of the board at an angle into the end of the board next to it (**No. 4 & 8**), using 1x60mm screw per board.


6x60mm Screws
Important: Pre-drill before fixing screws.

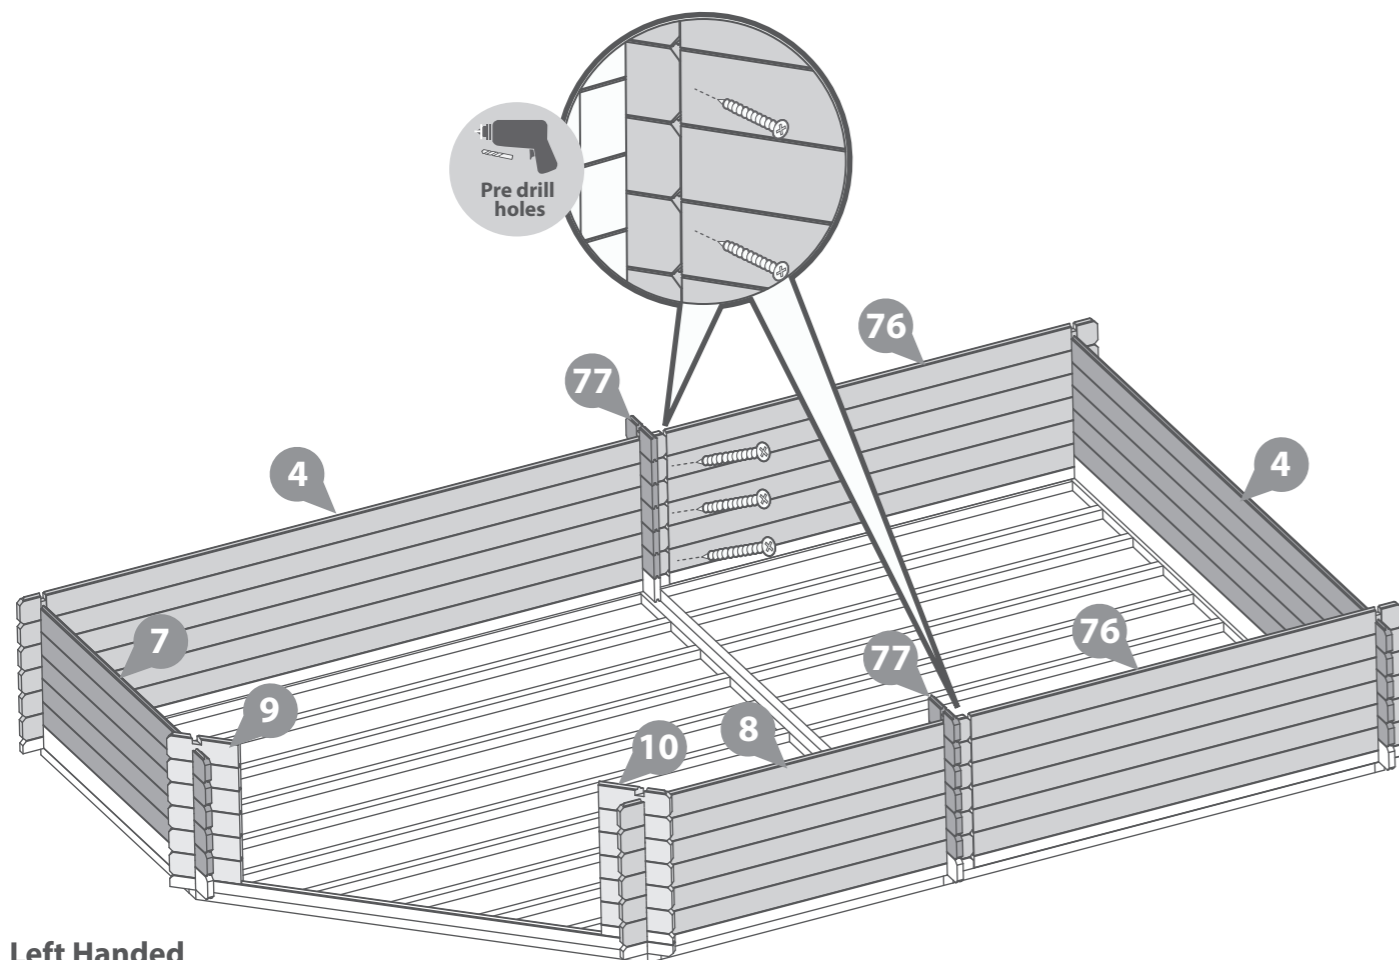

Left Handed

Step 8 - Right Handed

- Parts Needed -** No. 4 QTY 11 No. 10 QTY 6
 No. 7 QTY 5 No. 76 QTY 10
 No. 8 QTY 6 No. 77 QTY 12
 No. 9 QTY 6



Following the method shown in the illustration, lay the first 6 boards (**No. 4, 7, 8, 9, 10, 76 & 77**) off of the starter boards to create your first level.


**Ensure that the boards are level and flush with each other as you lay each one.*

Start by placing the front and back boards, interlocking them with the side boards. Then place the next side boards, interlocking with the front and back boards. Continue this method until you have placed **6 boards off of the starter boards on each side**, as shown.

Please note the right hand side of the door will be slightly higher. This will even out when the rest has been assembled.

Ensuring the boards (**No.76**) are level, flush and in line with the boards next to them, secure every other board in place by screwing through the side of the board at an angle into the end of the board next to it (**No. 4 & 7**), using 1x60mm screw per board.

6x60mm Screws
Important: Pre-drill before fixing screws.

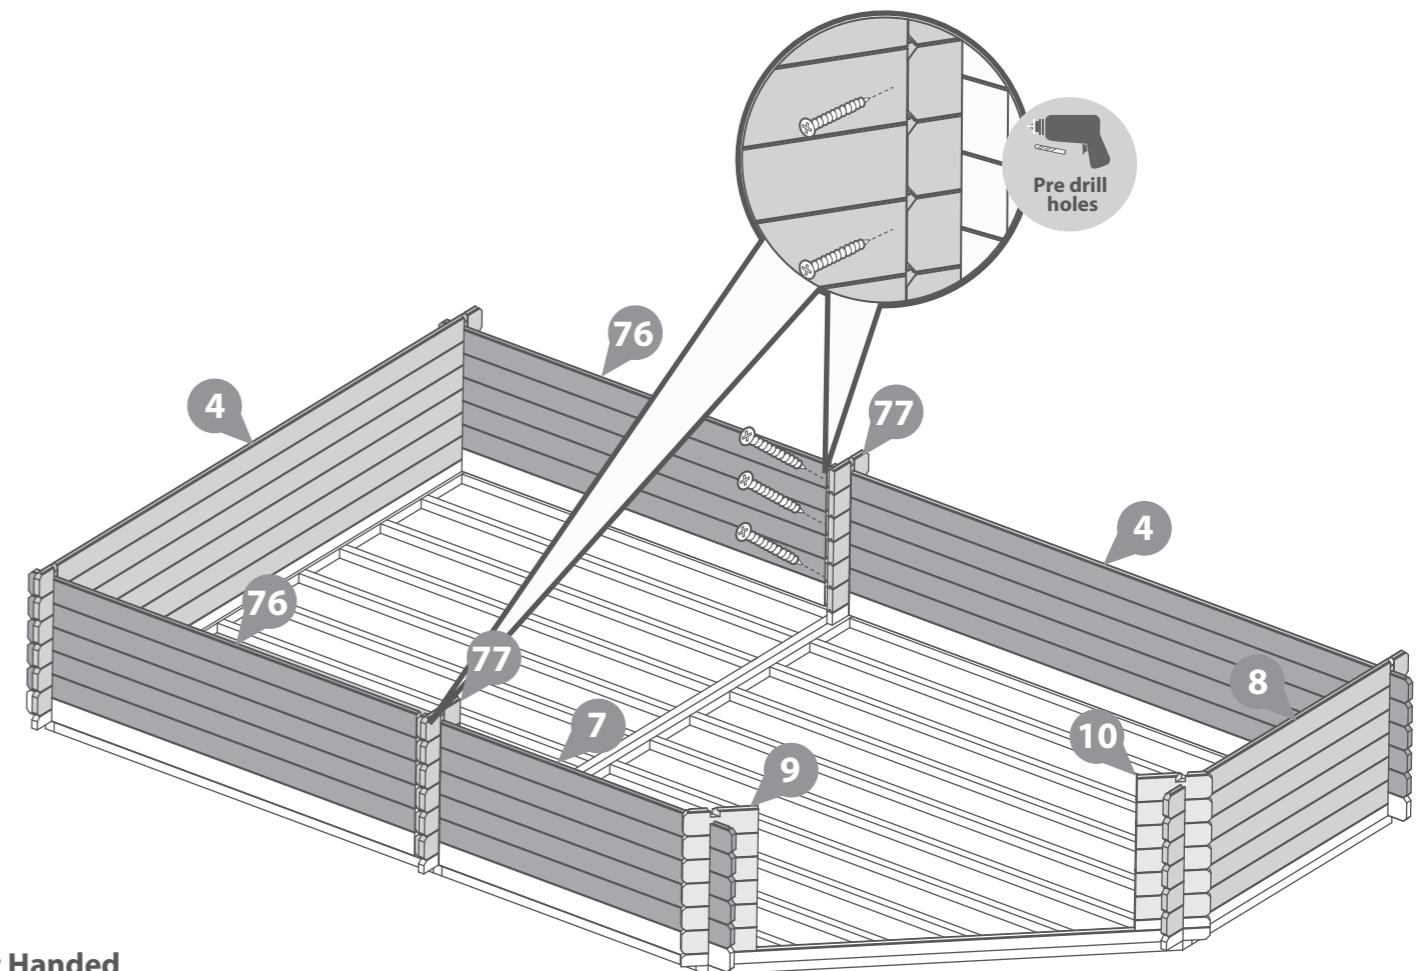

Right Handed

Step 9

- Parts Needed - No. 58 QTY 1**
- No. 59 QTY 1**
- No. 60 QTY 1**
- No. 61 QTY 1**

Arrange the left, right, top & bottom door frames (**No. 58, 59, 60 & 61**) onto a flat and level surface.

Secure the top and bottom frames to the uprights using 2x80mm screws per corner, ensuring the screws do **NOT** protrude through the front of the door framing.

8x80mm Screws


Important: Pre-drill before fixing screws.



Drill / Pre drill.



80mm screw

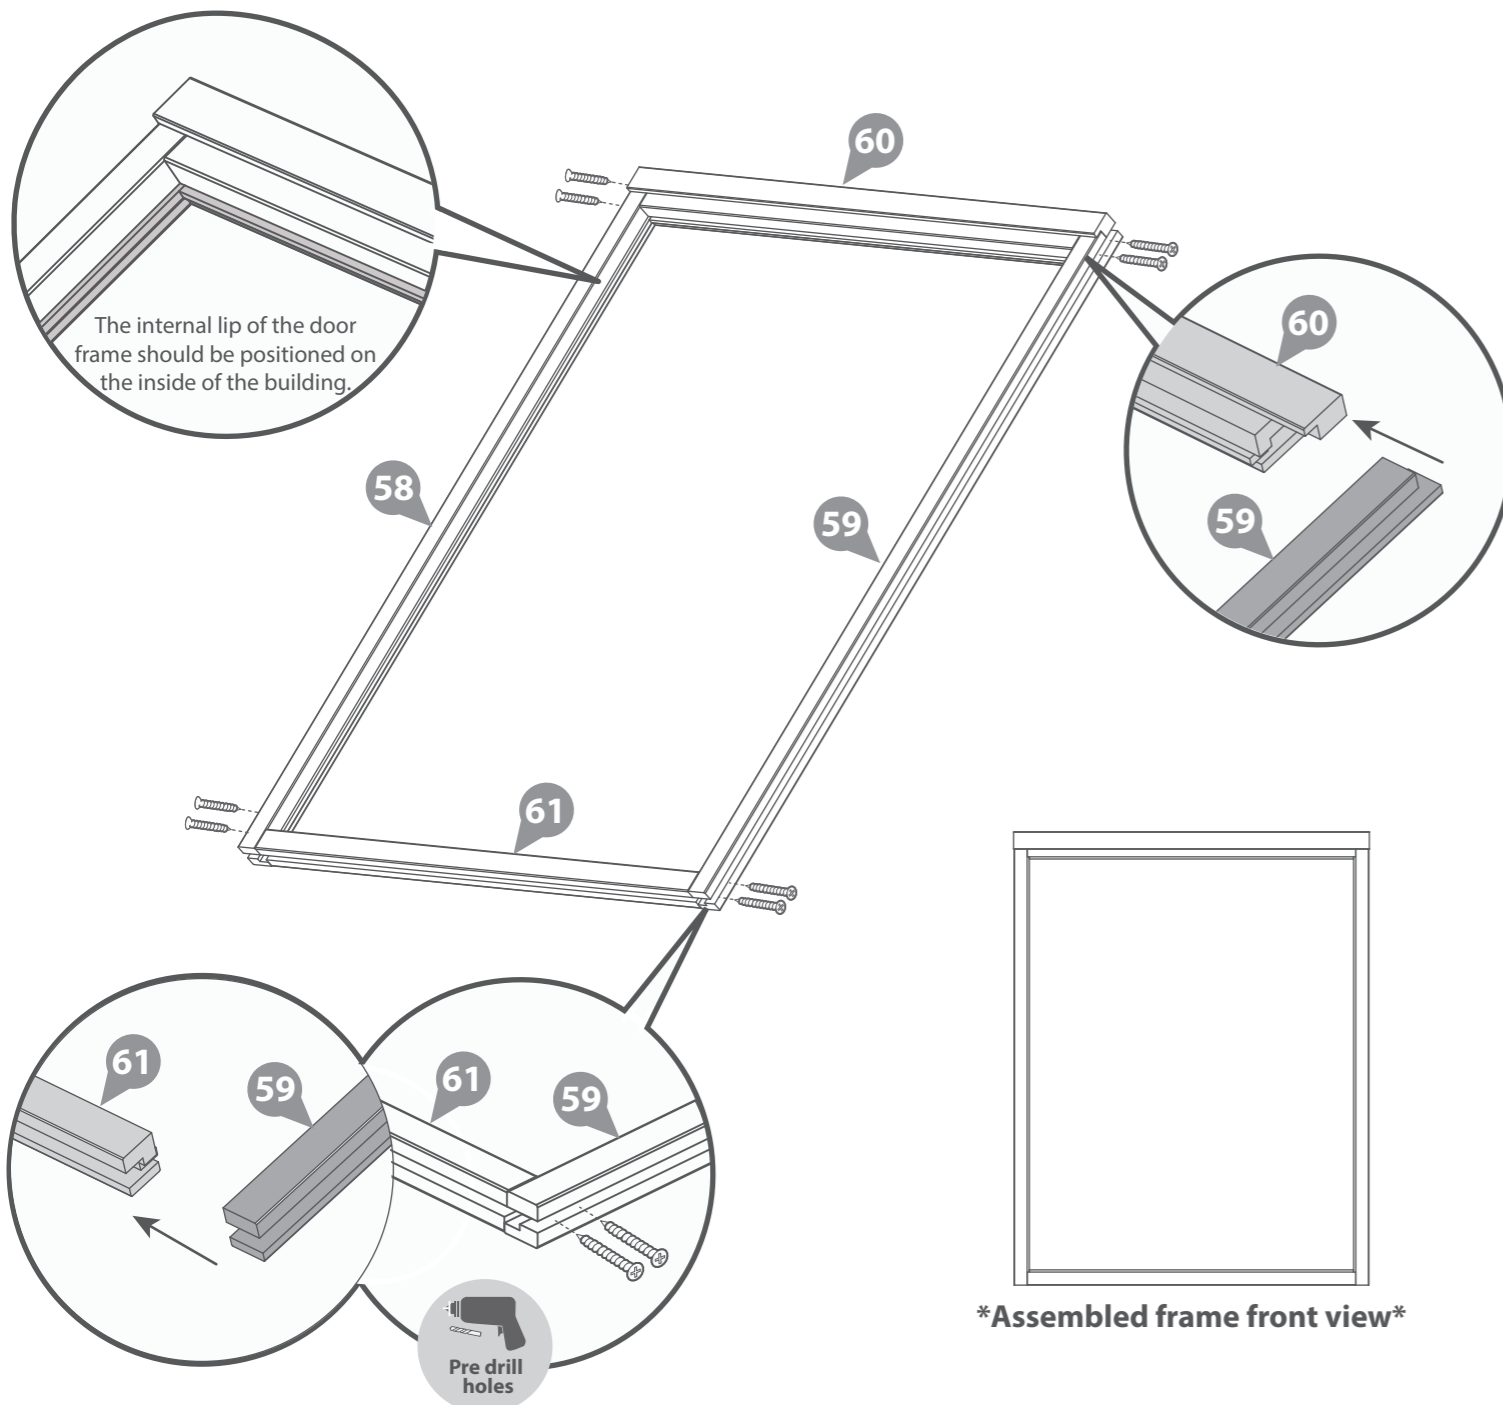

Assembled frame front view

Step 10

Parts Needed - No. 56 QTY 1
No. 57 QTY 1
No. 64 QTY 6

a The Adjustable Door Hinge (**No. 64**) comes in three parts.

Fasten parts **No. 64a** and **64b** of the Adjustable Door Hinge together by screwing part **64a** into **64b**, as shown in the illustration.

b Place the Master and Secondary Doors (**No. 56 & 57**) into the assembled double door frame, ensuring there is equal spacing on each side between the Doors and door frame.

Locate 3 x Adjustable Door Hinges (**No. 64c**) to each Door and fix in place using 3x30mm screws per hinge.

***Ensure the hinges are fitted to the external of the Doors so the doors open outwards from the log cabin.**

It is important to fit the Doors within the frames at this stage so that you can establish the position of the hinges.



c Fix 3 x Adjustable Door Hinges (**No. 64a&b**) onto each door frame using 4x30mm screws per hinge. Ensure the hinges on the Doors locate into the hinges on the door frame, and the Doors open & close freely without restriction.

***Please note: When fixing, screws may go through into the channel and not the framing. It is important to fit and locate the hinges at this point as the Doors are heavy and easier to locate when flat. Be aware that you may have to remove two screws on each hinge at a later point to correctly position your log boards.**

d Remove the Doors from the frame after fitting the hinges. Open the Doors and lift them off of the hinges attached to the frames. You do not need to unscrew the hinges to remove the Doors.

42x30mm Screw.


Important: Pre-drill before fixing screws.

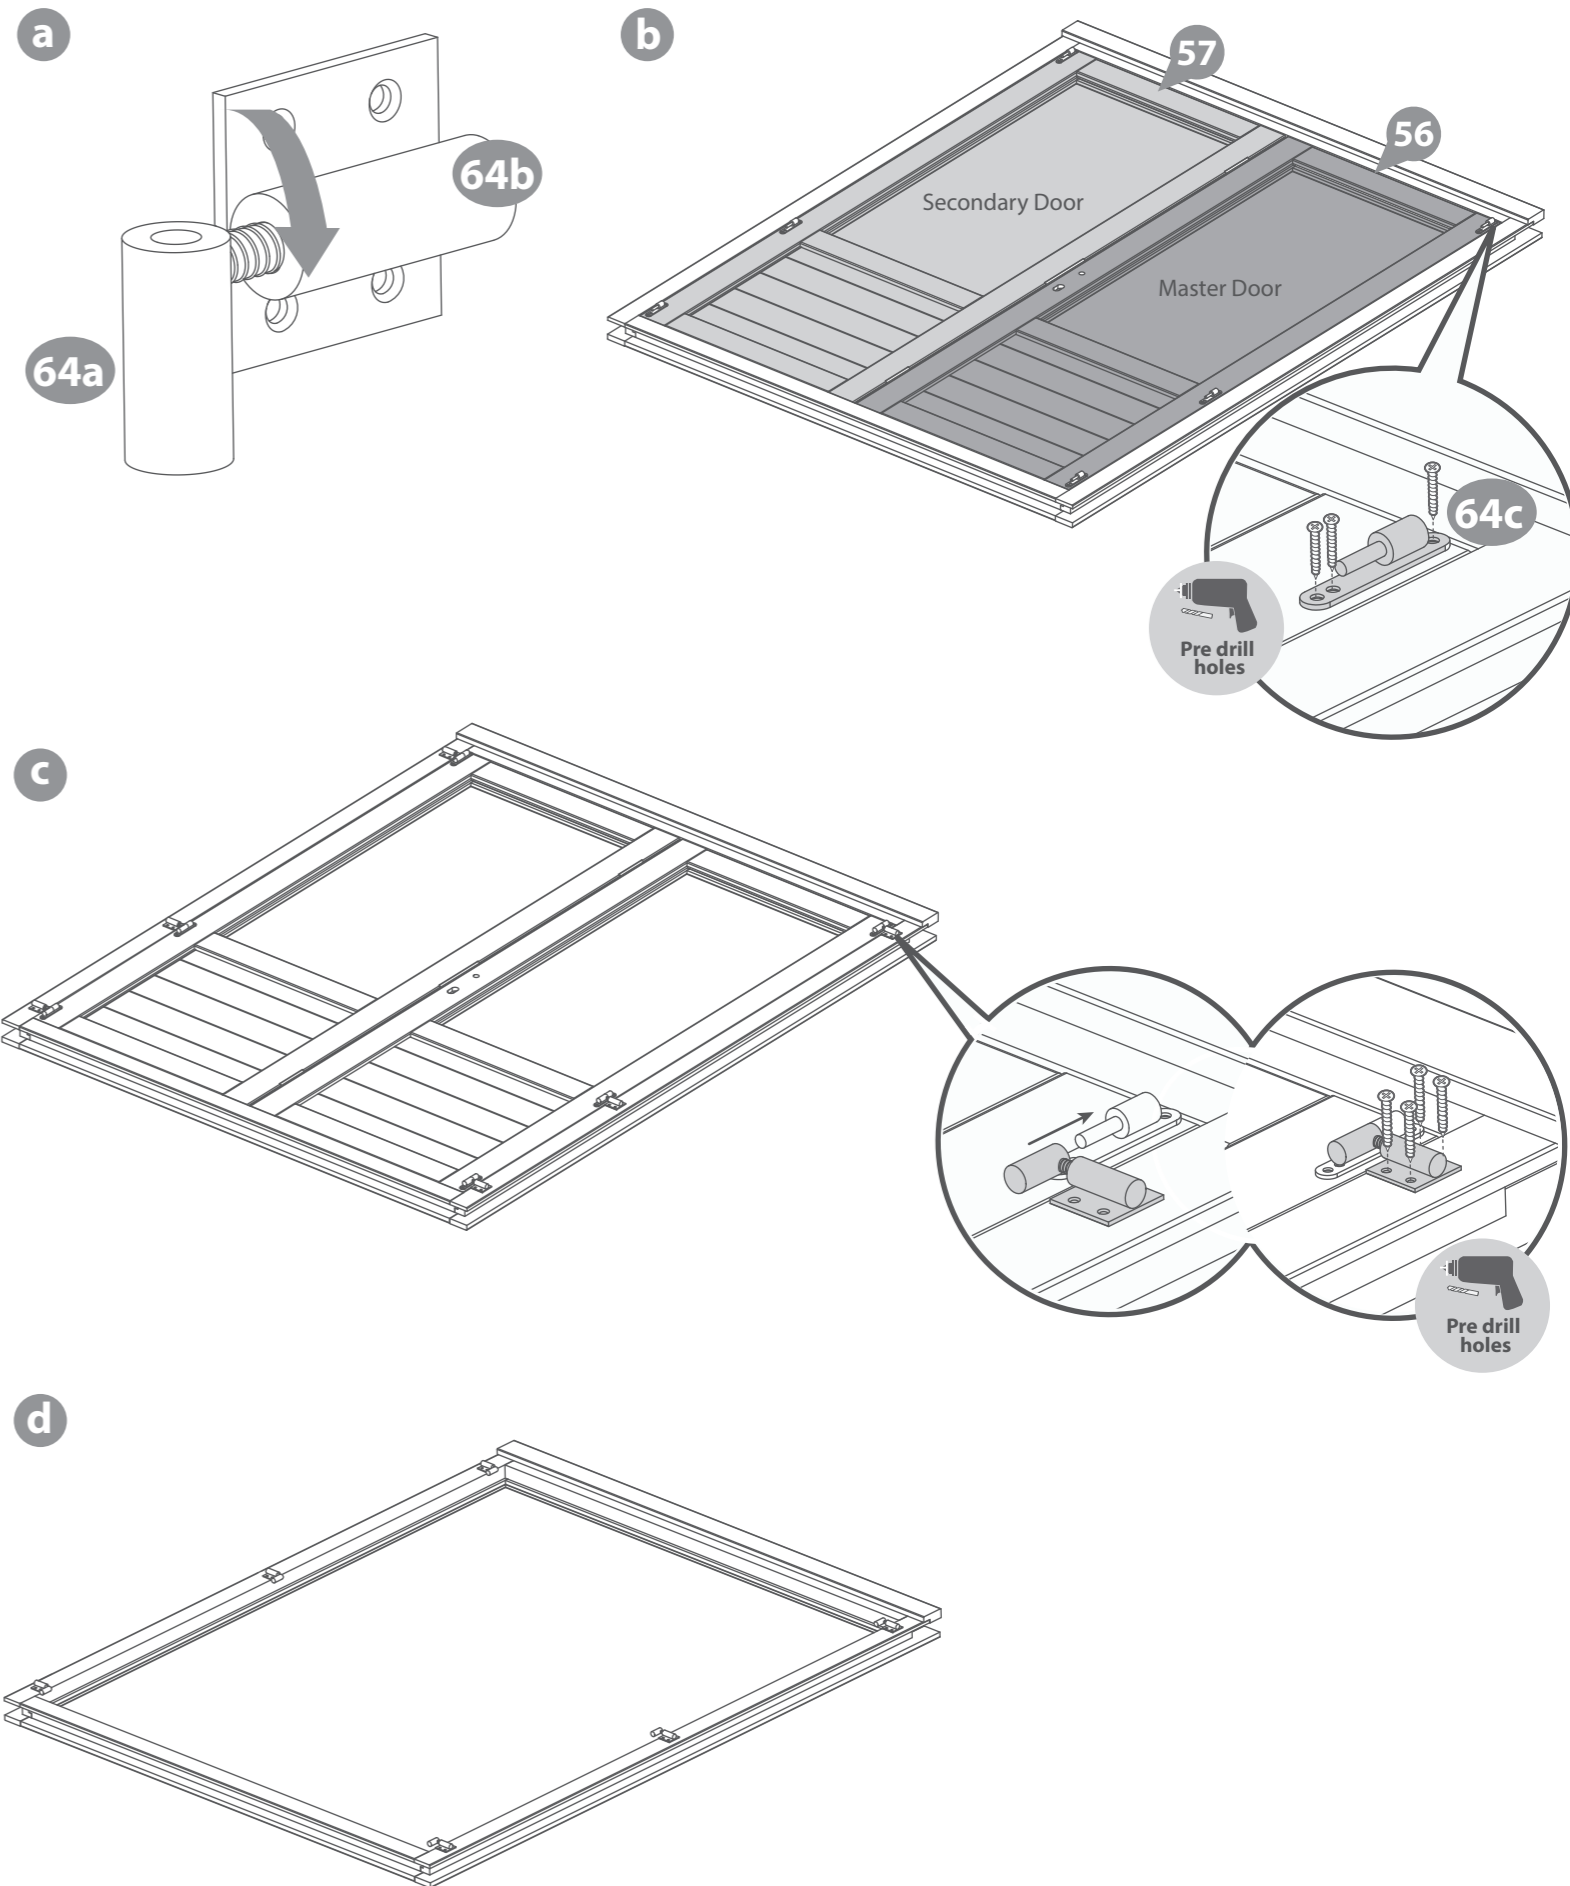

Step 11

To adjust and align your doors:

1. Lift up the doors to separate the two parts of the hinge.
2. Turn the rotating barrel (**No. 64a**) in / out to move the position of the doors either in or away from each other.
3. You can then place the door(s) back on to the hinge and check whether they require more / less adjustments, if further adjustments are required repeat number 2.

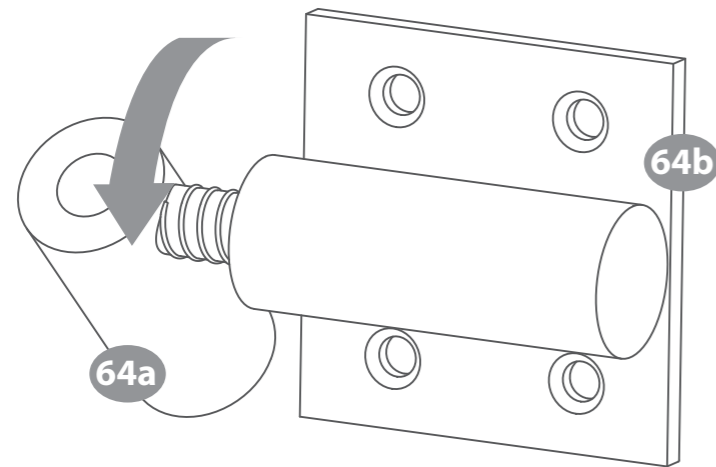


Step 12

Once you have laid 6 log boards (off of the starter board) up the door section, slide the assembled door frame over the boards, ensuring to rest the frame on top of the starter board. *If you have not yet assembled your door frame, please refer to steps 9-11.*




Rubber Mallet.

Left Handed

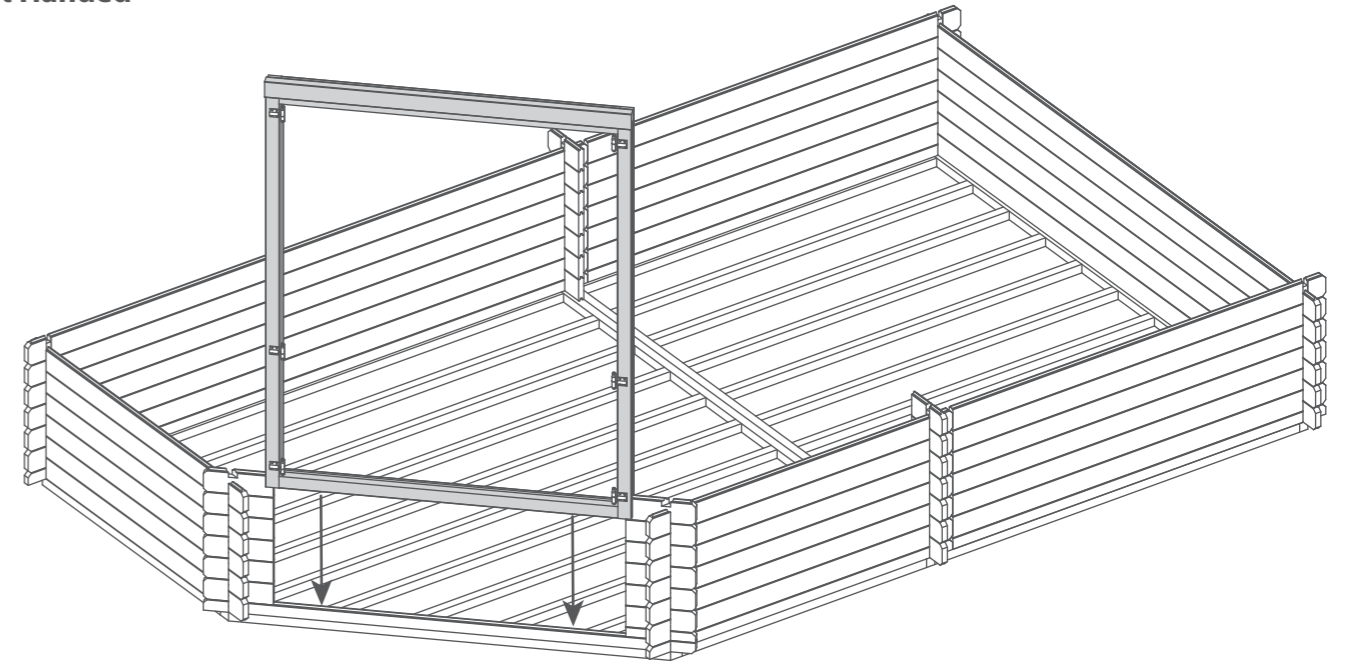


Right Handed

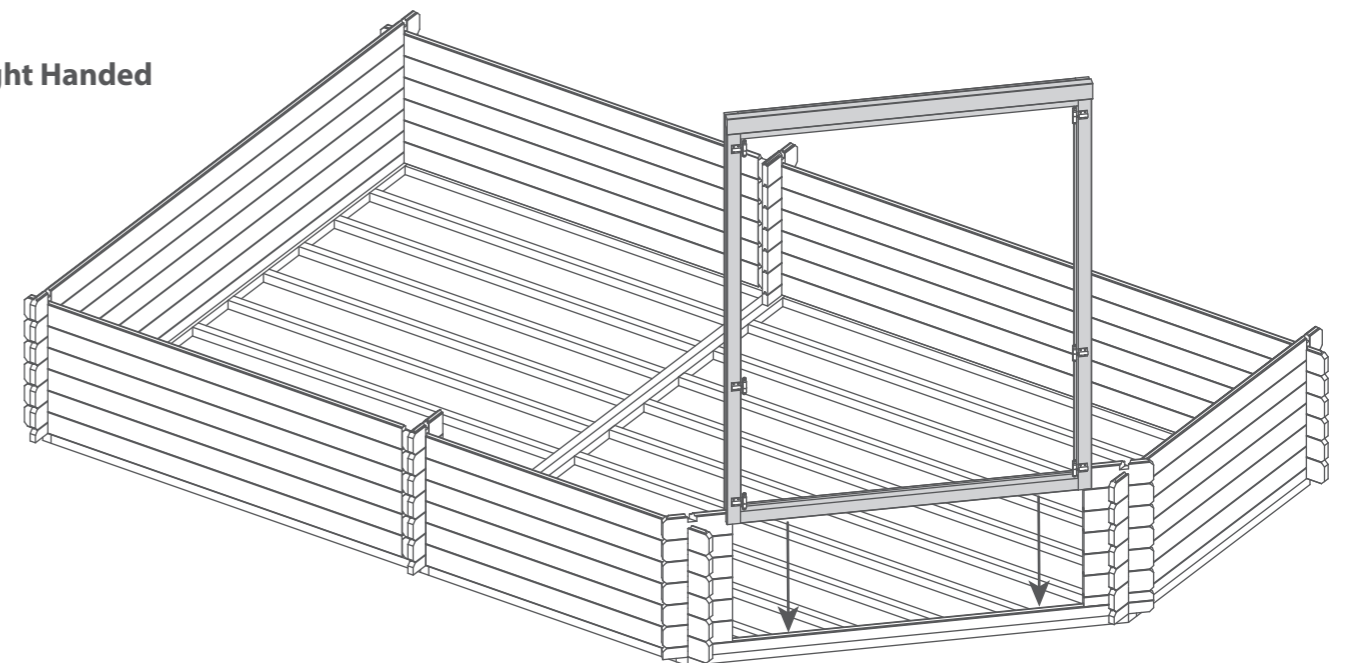

Step 13

- Parts Needed -**
- | | |
|---------------|---------------|
| No. 4 QTY 12 | No. 13 QTY 6 |
| No. 9 QTY 6 | No. 76 QTY 6 |
| No. 10 QTY 6 | No. 77 QTY 12 |
| No. 11 QTY 12 | No. 78 QTY 6 |
| No. 12 QTY 6 | No. 79 QTY 6 |



Following the method shown in the illustration, lay the next 6 boards (**No. 4, 9, 10, 11, 12, 13, 76, 77, 78 & 79**) on to the log cabin to create your second level.

***Ensure that the boards are level and flush with each other as you lay each one.**


Secure every other board (**No.76 & 79**) in place (Internally) by screwing through the side of the board at an angle into the end of the adjacent board using 1x60mm screw per board.

6x60mm Screws.



Important: Pre-drill before fixing screws.



Left Handed

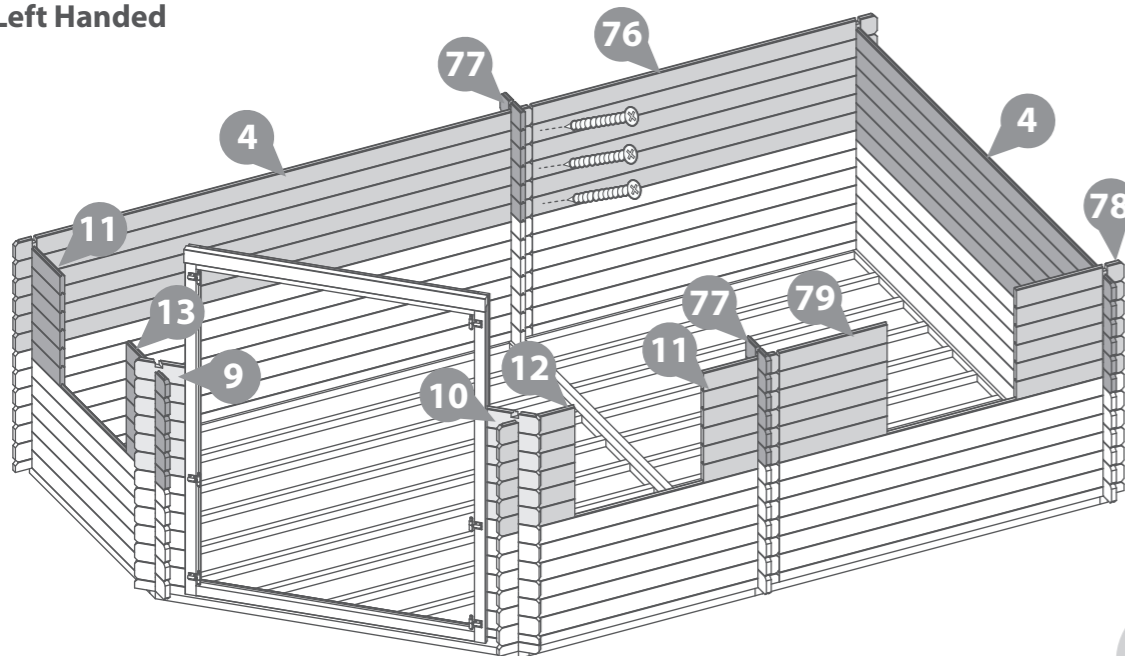

Right Handed

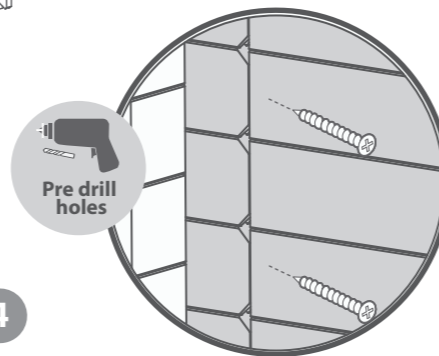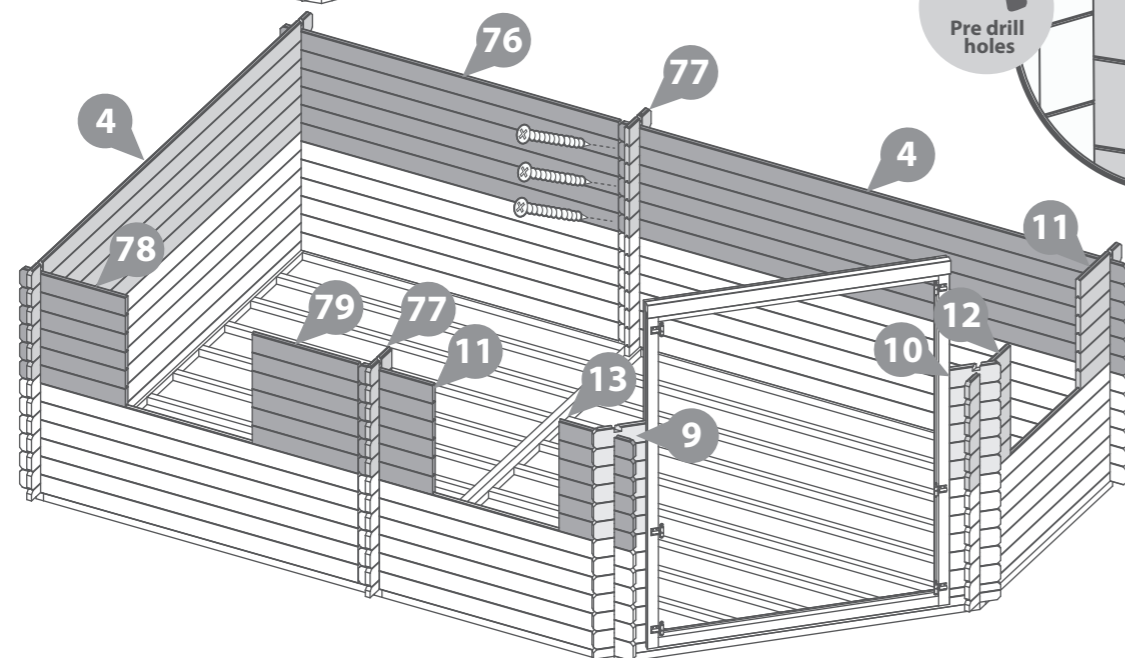

Step 14

- Parts Needed - No. 55 QTY 8**
No. 69 QTY 3
No. 71 QTY 3
No. 73 QTY 8

- a** Open the hinges (**No.71**) following the directional arrow given on the top of the hinge.
- b** Lay the assembled window frame (**No. 69**) on a flat and level surface.

Please note: The window can be hinged to open on either the left or the right, depending on where you position your hinges. Please decide which works best for you before fitting the hinges.

If you want your window to open on the left (from the inside), position the spacers / hinges to the right corners, and if you want your window to open on the right (from the inside), position the spacers / hinges in the left corners.

Place one 2mm spacer (**No. 55**) and one 6mm spacer (**No. 73**) flush together and position them flat onto the inside framing of your chosen hinge position, ensuring they are flush into the corner, as shown.

- c** Position one hinge (**No. 71**) inside the window frame at the top, butt up to the positioned spacers. Ensure the coloured corner cap is flush into the corner of the frame and the straight part of the hinge is flush to the top of the frame. Make sure the hinge opens outwards, away from the frame.

Secure in place using 3x30mm screws.

Repeat to fix the other hinge to the bottom of the frame and remove the spacers.


Use this method to locate and fix hinges to all three window frames.

18x30mm Screws.




Important: Pre-drill before fixing screws.



Drill / Pre drill.



30mm screw

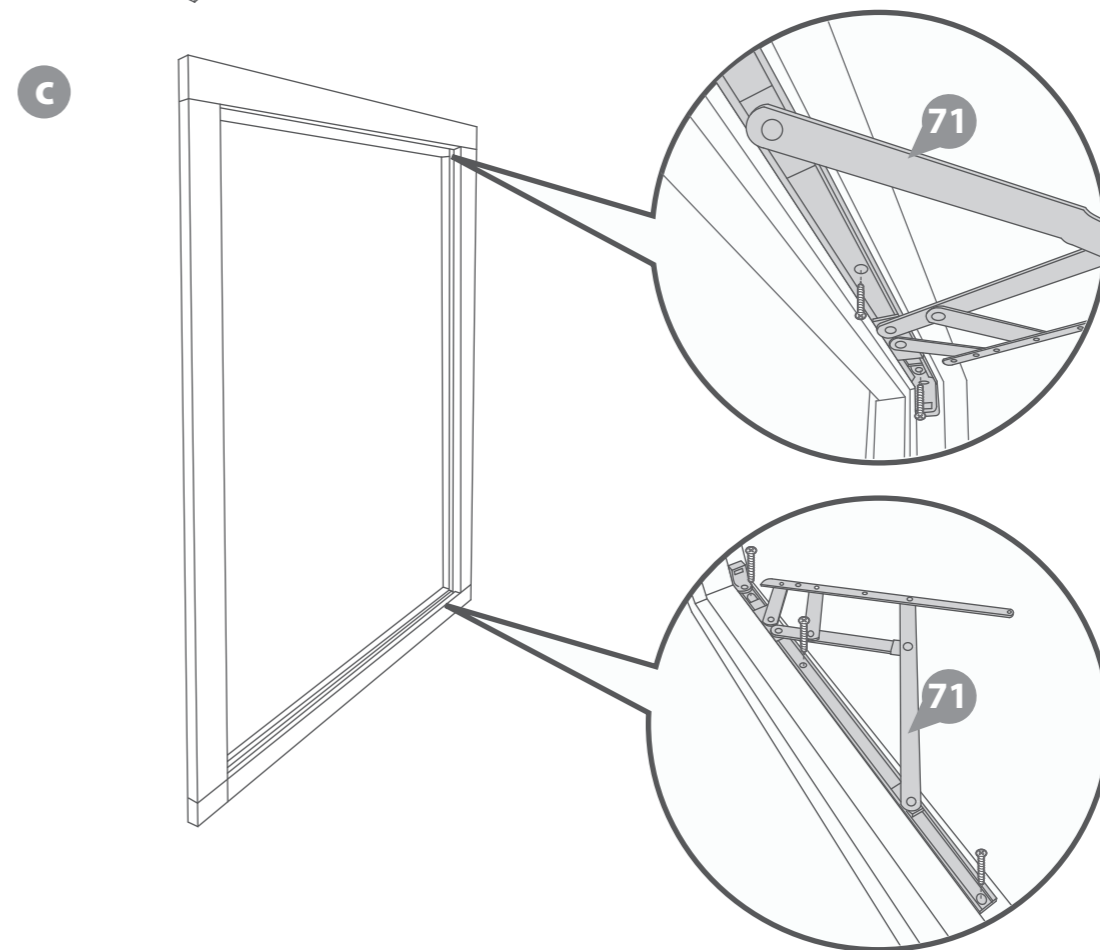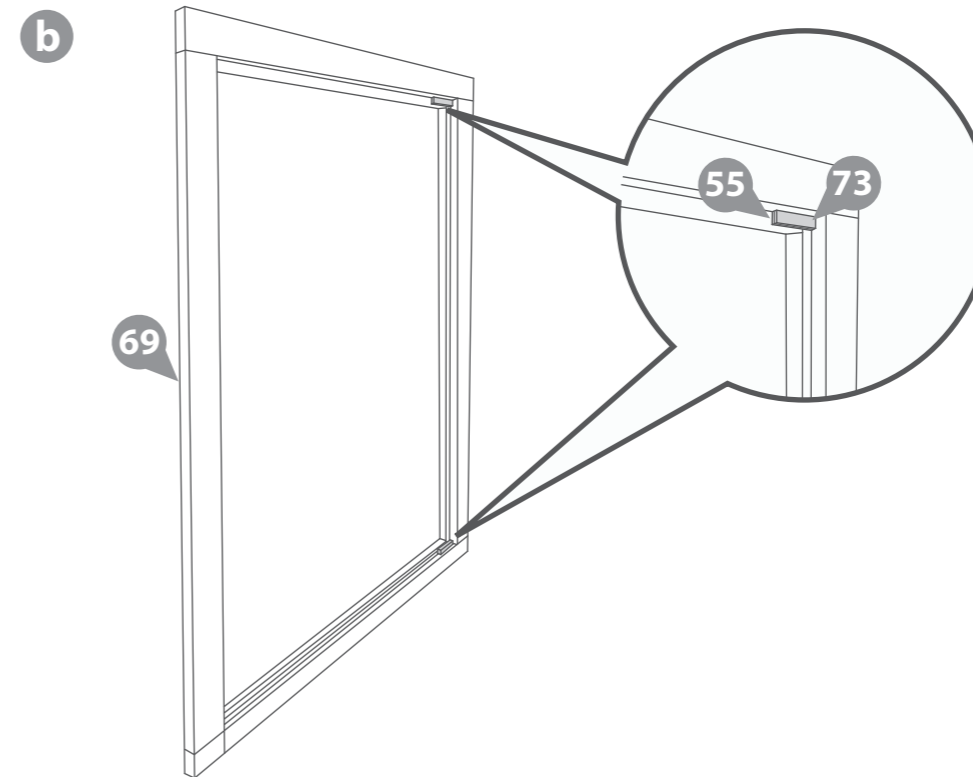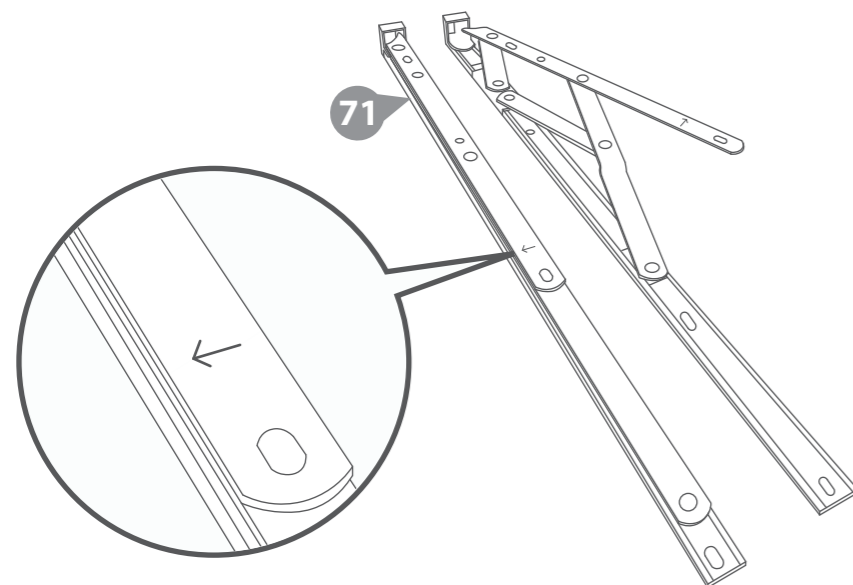

Step 15

Parts Needed - No. 68 QTY 3

- a** With the hinges (**No. 71**) open in the frame, locate the Window (**No. 68**) onto the bottom hinge, ensuring to position both the top and bottom hinge into the groove in the window, as shown.

Fix the hinge to the window using 3x30mm screws per hinge. Ensure the window is able to open and close without getting stuck on the frame.

- b** Once positioned, unscrew and remove the window from the hinges, ensuring to leave the hinges attached to the frame. This will make it easier to fit the window frame into the log cabin.


Use this method to assemble and remove the window from all three window frames.

18x30mm Screws.



Important: Pre-drill before fixing screws.



Drill / Pre drill.



30mm screw

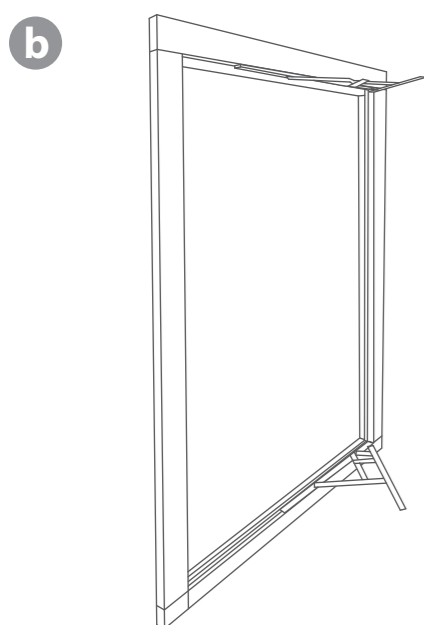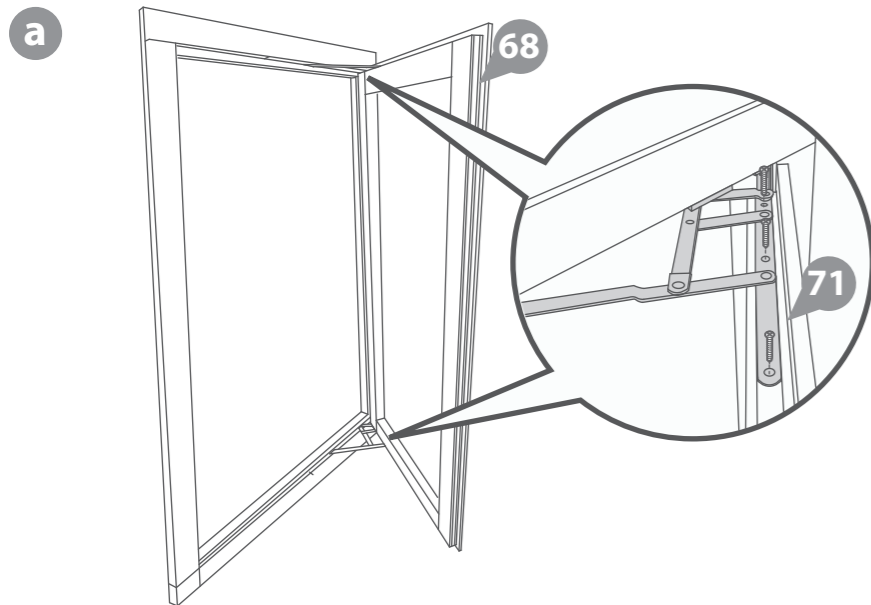

Step 16


Parts Needed - No. 69 QTY 3

Once you have laid 6 log boards up the window sections, slide the assembled Window frames (**No. 69**) over the boards, ensuring to rest the frame on top of the board below. *If you have not yet assembled your window frames, please refer to steps 14 & 15.*




Rubber Mallet.

Left Handed

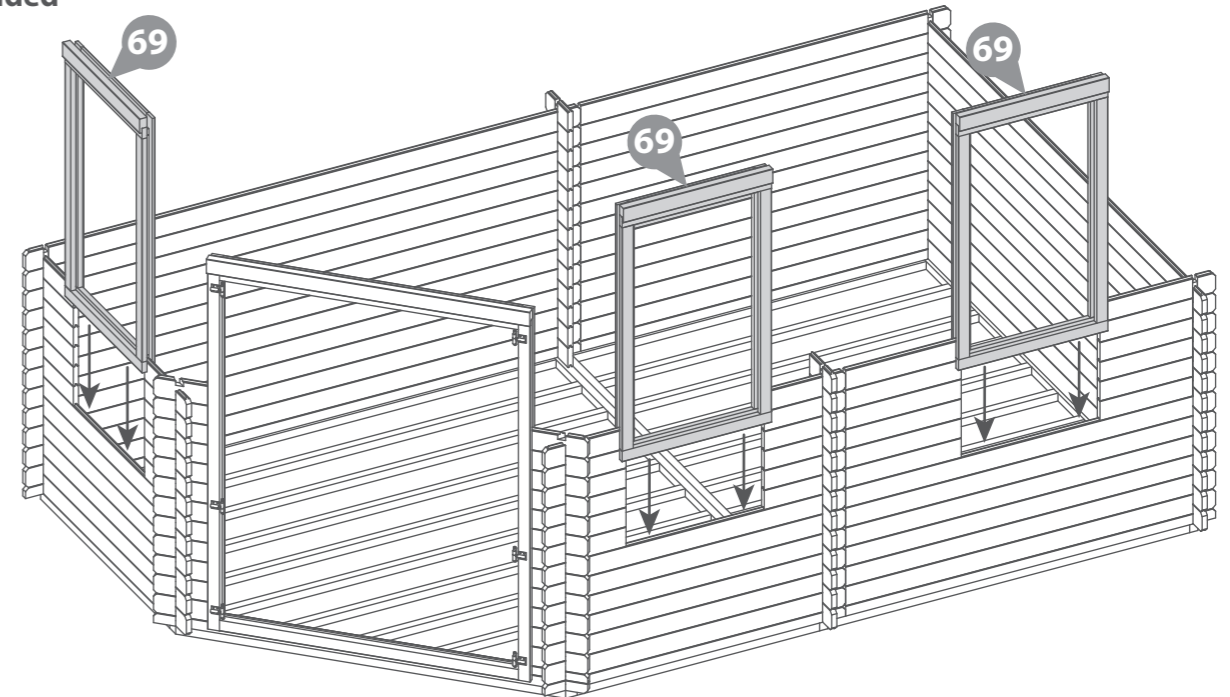


Right Handed

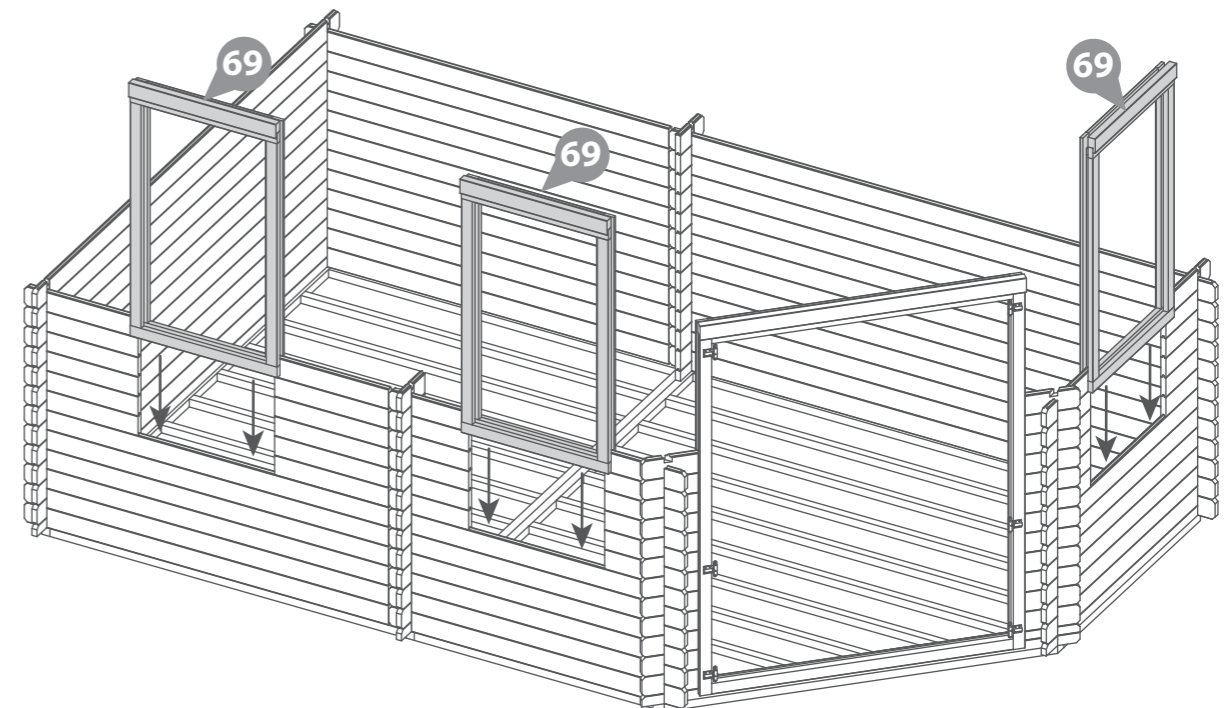

Step 17

- Parts Needed -**
- | | |
|---------------|---------------|
| No. 4 QTY 12 | No. 13 QTY 6 |
| No. 9 QTY 6 | No. 76 QTY 6 |
| No. 10 QTY 5 | No. 77 QTY 12 |
| No. 11 QTY 12 | No. 78 QTY 6 |
| No. 12 QTY 6 | No. 79 QTY 6 |



Following the method shown in the illustration, lay the next 6 boards (No. 4, 9, 10, 11, 12, 13, 76, 77, 78 & 79) to create your next level.

***Ensure that the boards are level and flush with each other as you lay each one.**

Secure every other board (No.76 & 79) in place (Internally) by screwing through the side of the board at an angle into the end of the adjacent board using 1x60mm screw per board.

6x60mm Screws.
Important: Pre-drill before fixing screws.




Step 18

- Parts Needed - No. 14 QTY 1**


Make the log cabin level by laying another board (No. 14) onto the right side of the cabin, as shown.

***Ensure that the boards are level and flush with each other as you lay each one.**




Rubber Mallet.


Left Handed

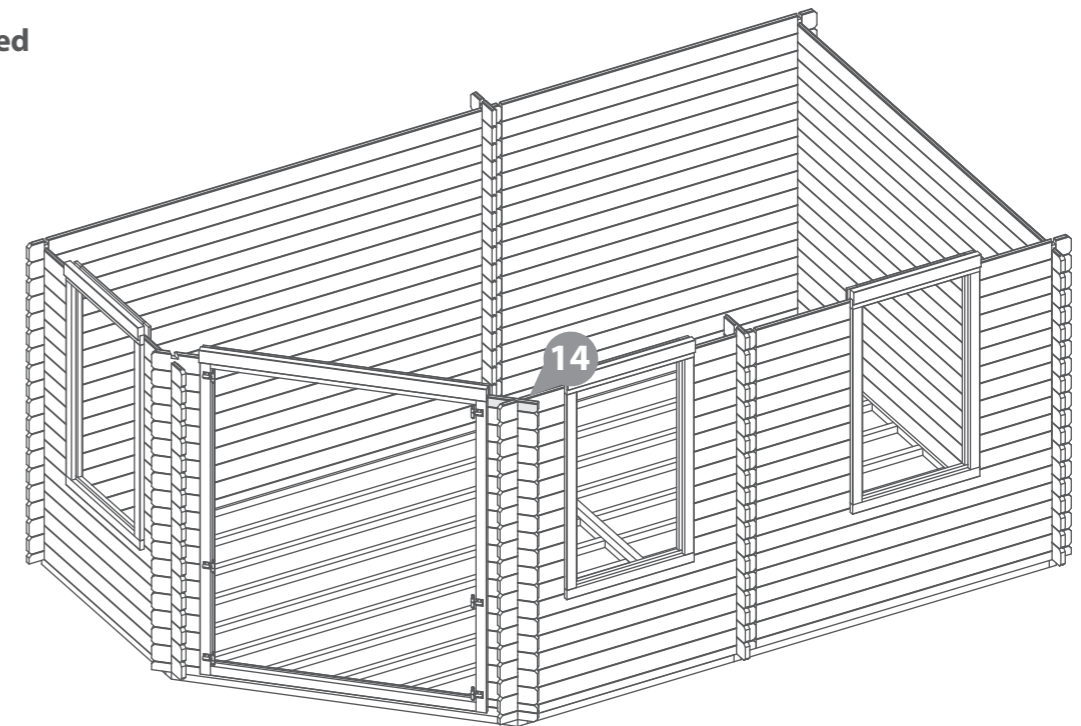


Right Handed

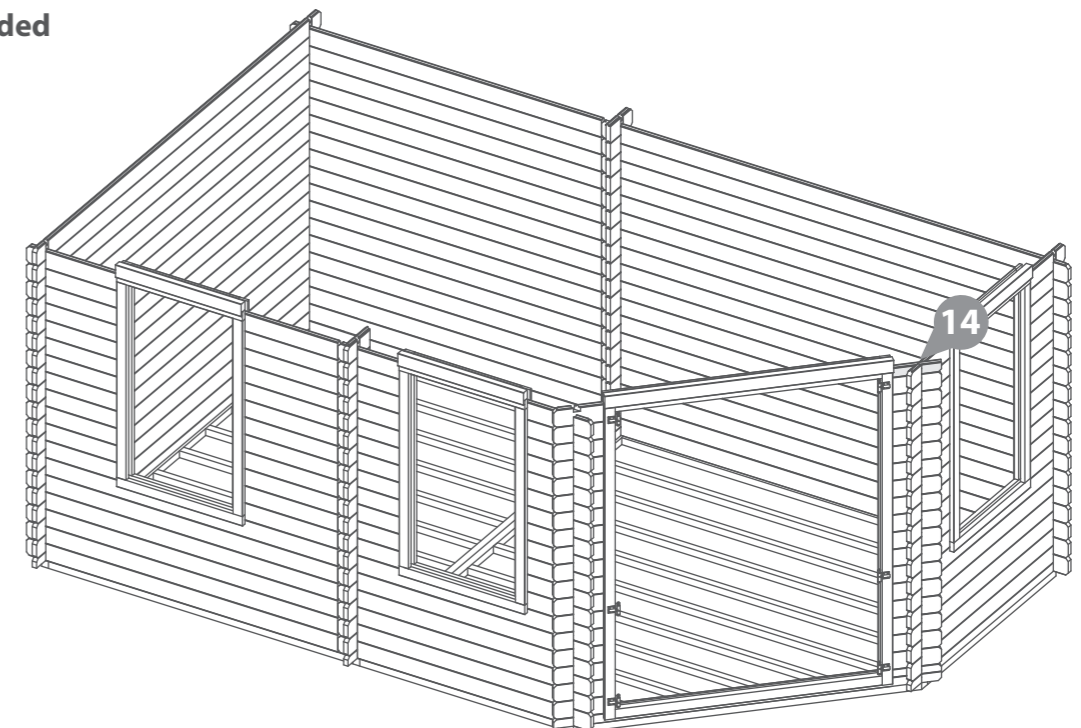

Left Handed

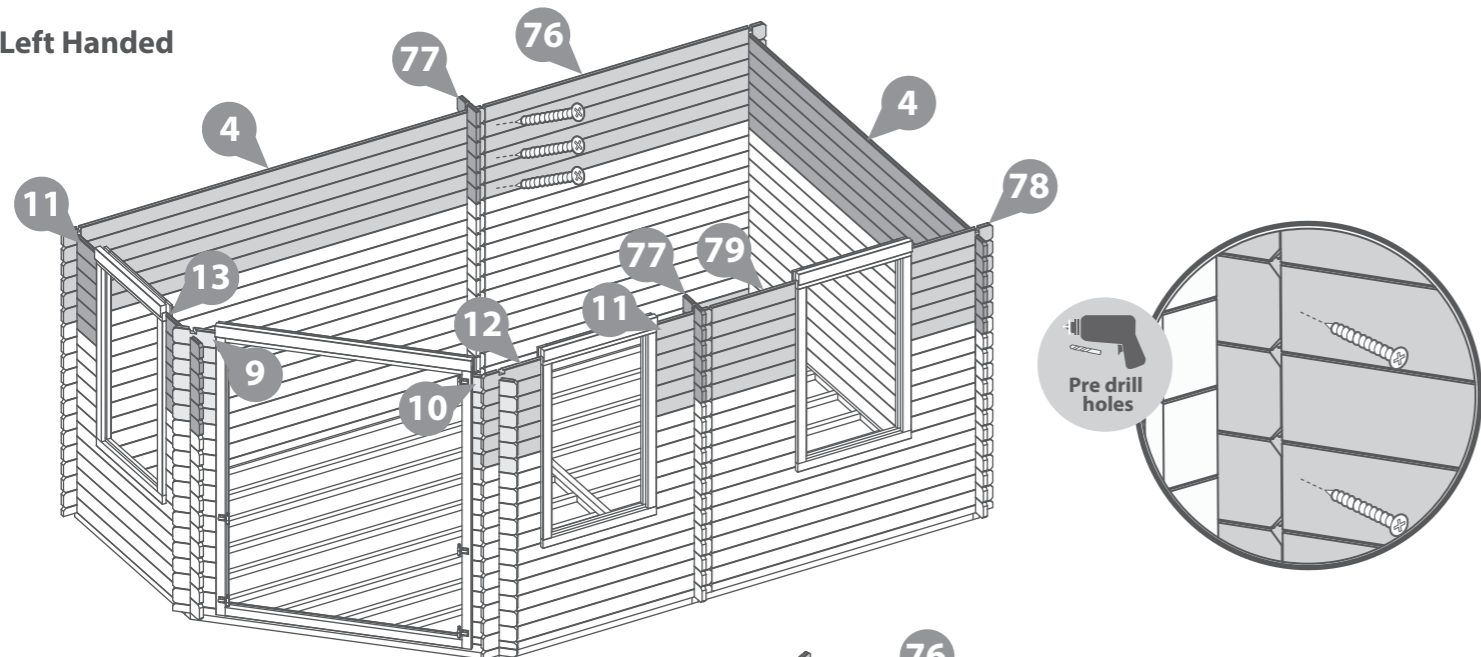


Right Handed

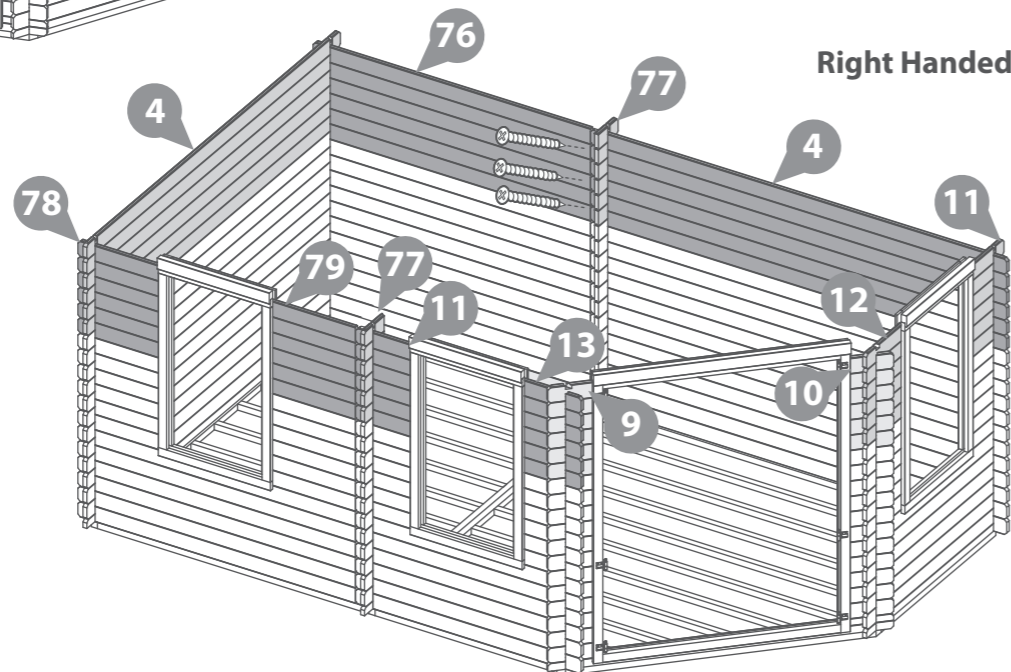

Step 19 - Left Handed

- Parts Needed - No. 4 QTY 3**
No. 15 QTY 1
No. 16 QTY 1
No. 17 QTY 1
No. 76 QTY 1
No. 80 QTY 1




Following the method shown in the illustration, lay the next layer of boards (**No. 4, 15, 16, 17, 76 & 80**) onto the log cabin.

**Ensure that the boards are level and flush with each other as you lay each one.*




Rubber Mallet.

Left Handed

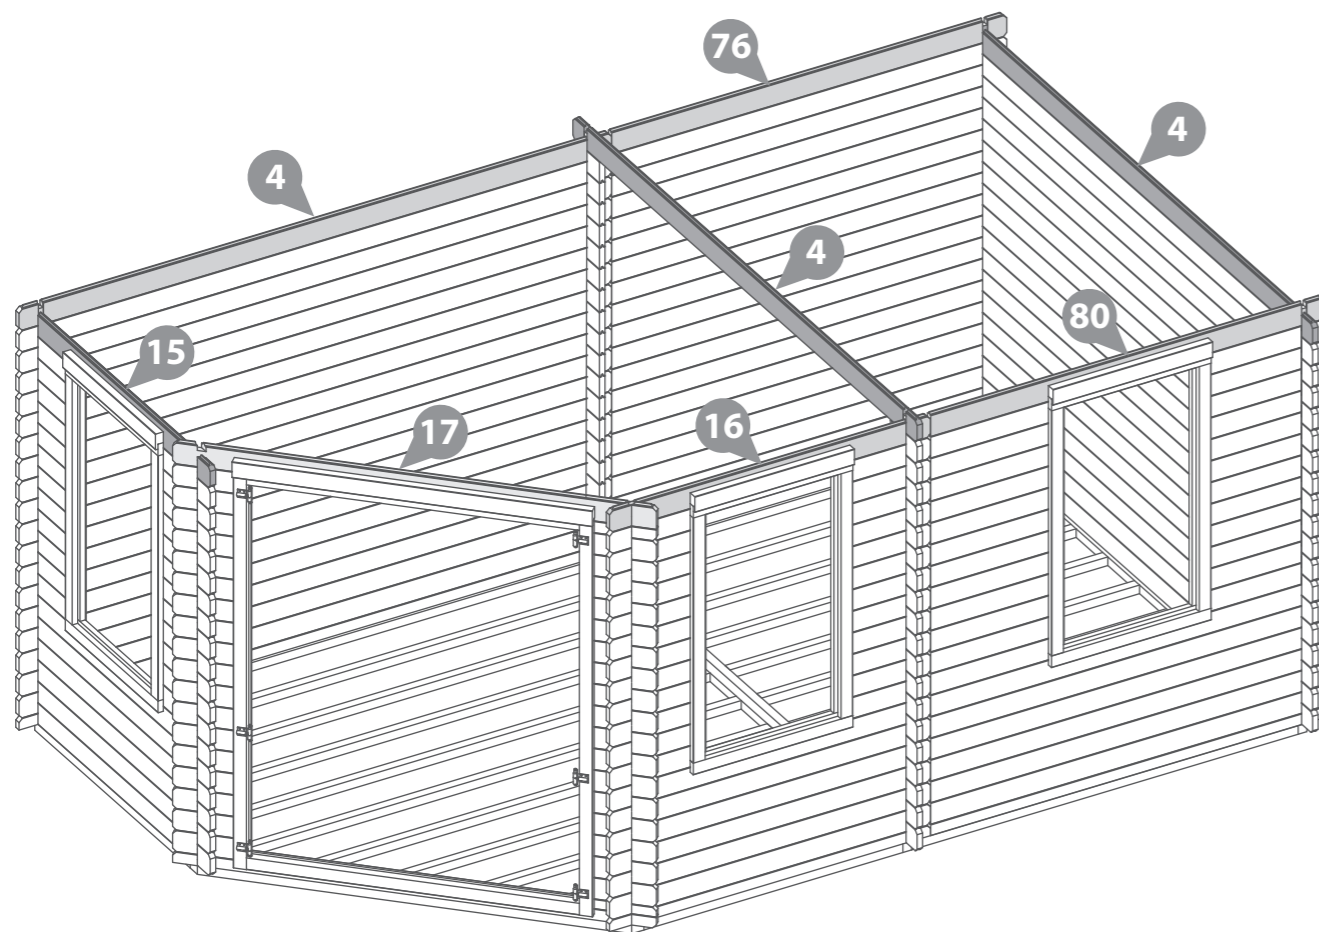

Step 19 - Right Handed

- Parts Needed - No. 4 QTY 2**
No. 15 QTY 1
No. 16 QTY 1
No. 17 QTY 1
No. 76 QTY 1
No. 77 QTY 2
No. 80 QTY 1




Following the method shown in the illustration, lay the next layer of boards (**No. 4, 15, 16, 17, 76, 77 & 80**) onto the log cabin.

**Ensure that the boards are level and flush with each other as you lay each one.*



Rubber Mallet.

Right Handed

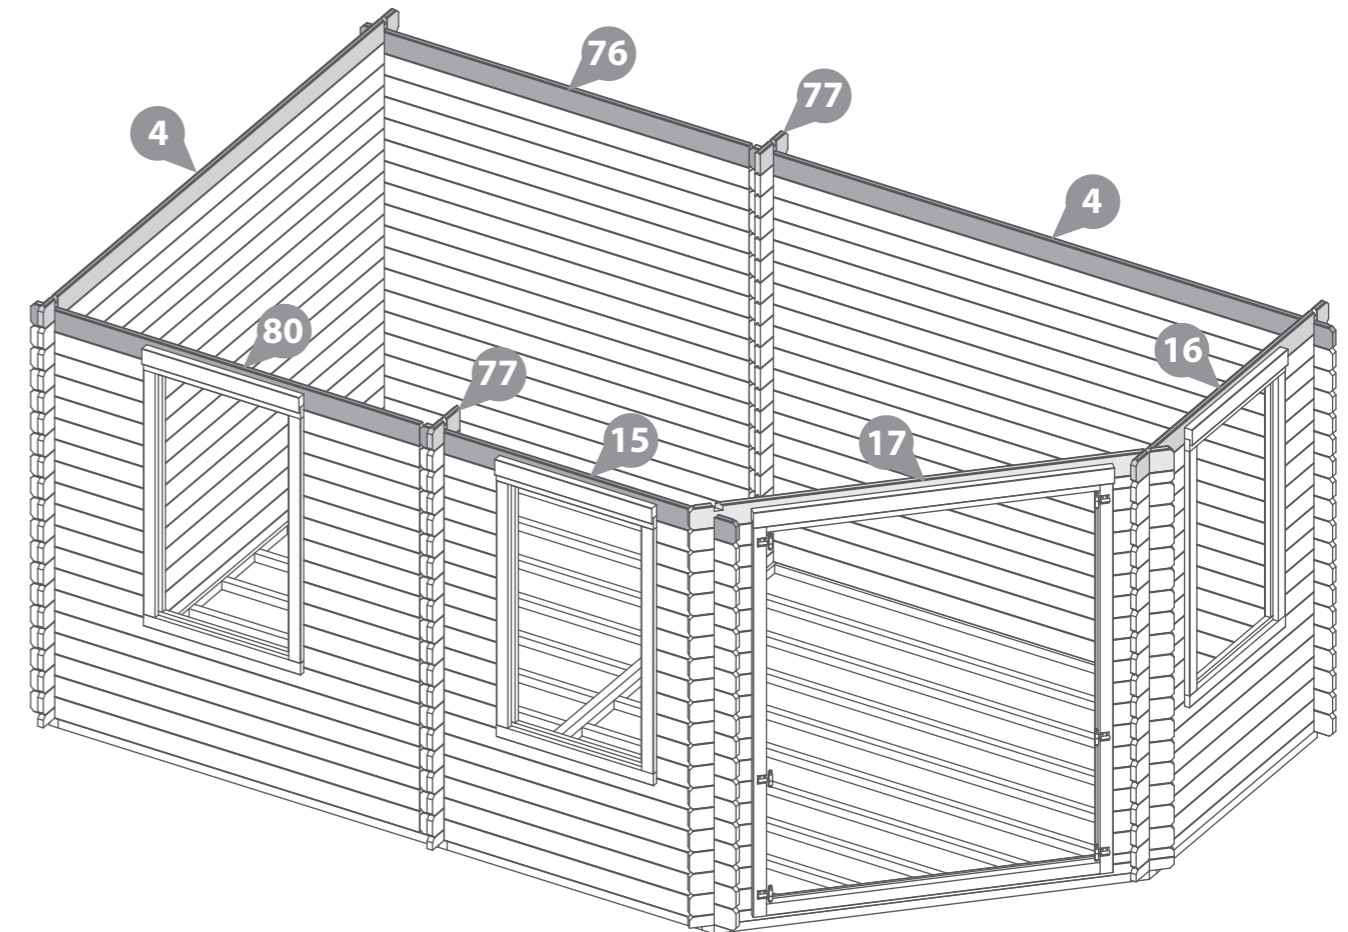

Step 20


**Parts Needed - No. 5 QTY 1
No. 19 QTY 1
No. 53 QTY 4**

Lay both Boards (**No. 5 & 19**) onto a flat and level surface and locate one Vent (**No. 53**) into each vent hole, as shown. Secure in place using 2x20mm screws per Vent.

Flip the Boards (**No. 5 & 19**) over and position the remaining Vents (**No. 53**) into the opposite side of the Vent holes. Fix in place using 2x20mm screws per vent.


On one side of each board, the vent will need to be slightly offset to an angle to ensure the screws do not collide.

8x20mm Screws.
Important: Pre-drill before fixing screws.

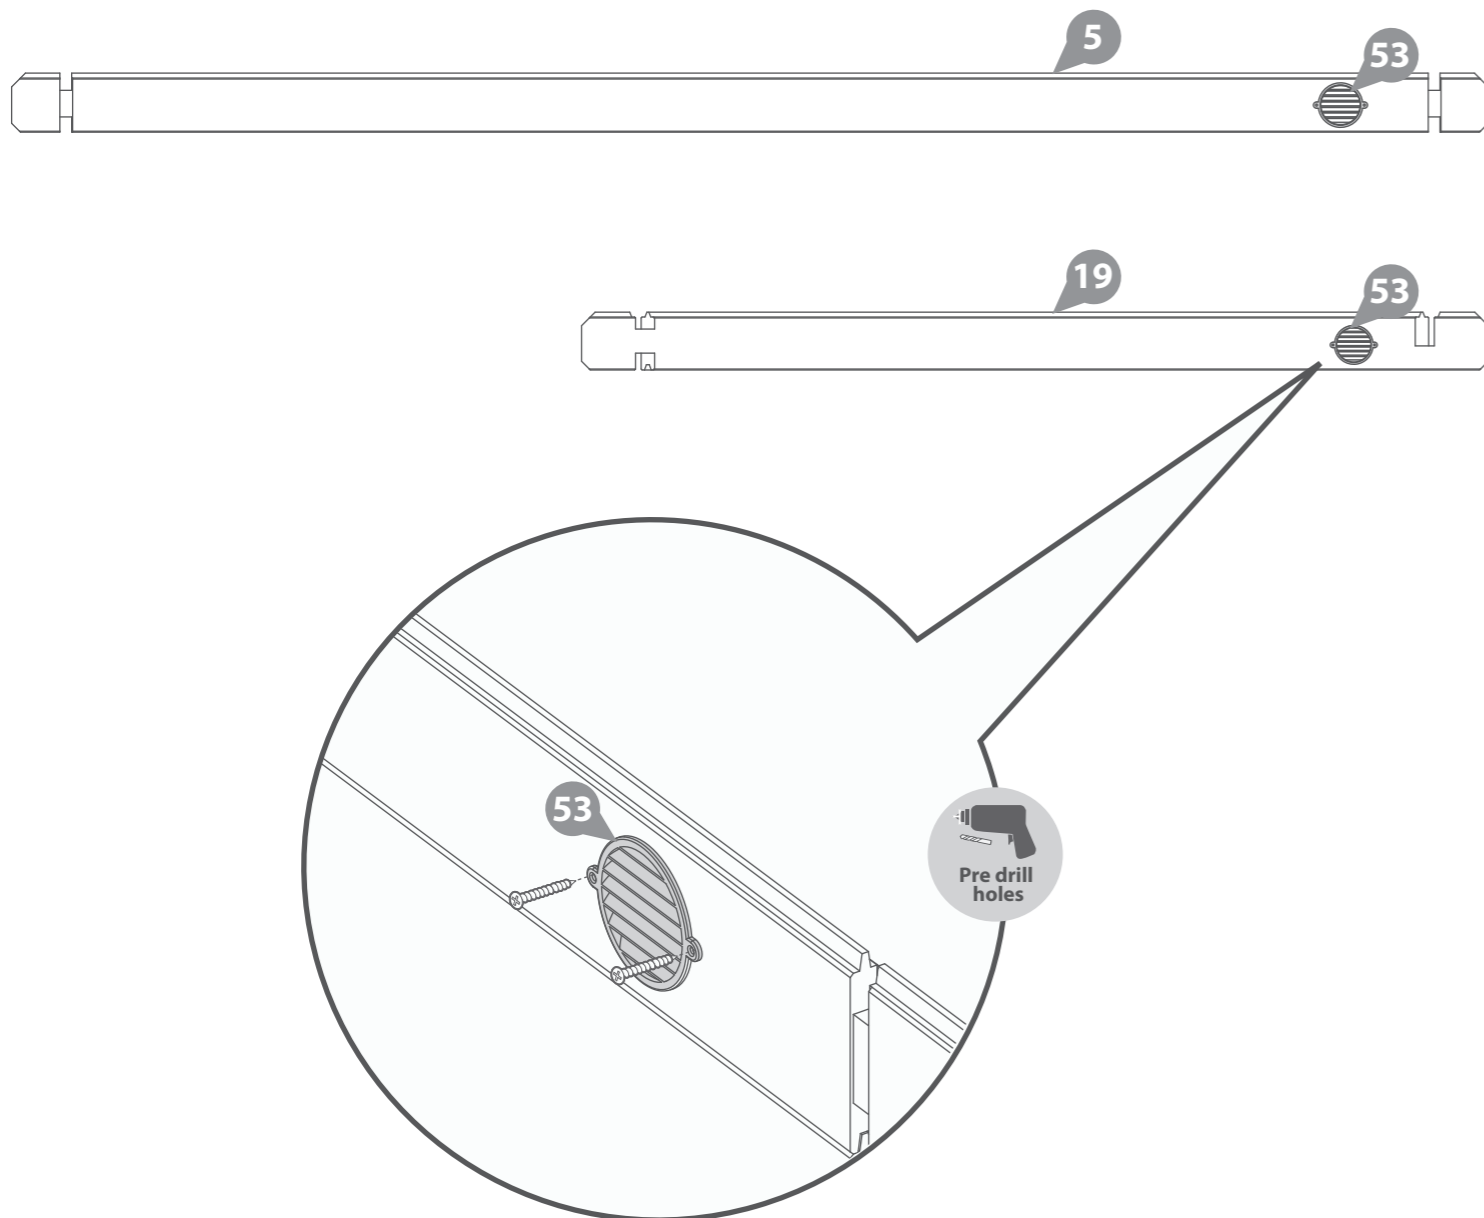

Step 21

**Parts Needed - No. 4 QTY 1 (Right handed QTY 2) No. 18 QTY 1
No. 5 QTY 1 No. 19 QTY 1
No. 7 QTY 1 No. 76 QTY 2**



Following the method shown in the illustration, lay the next layer of boards (**No. 4, 5, 7, 18, 19 & 76**) onto the log cabin.


***Ensure that the boards are level and flush with each other as you lay each one.**

Secure boards (**No.76**) in place (Internally) by screwing through the side of the board at an angle into the end of the adjacent board using 1x60mm screw per board.


2x60mm Screws.
Important: Pre-drill before fixing screws.




Left Handed

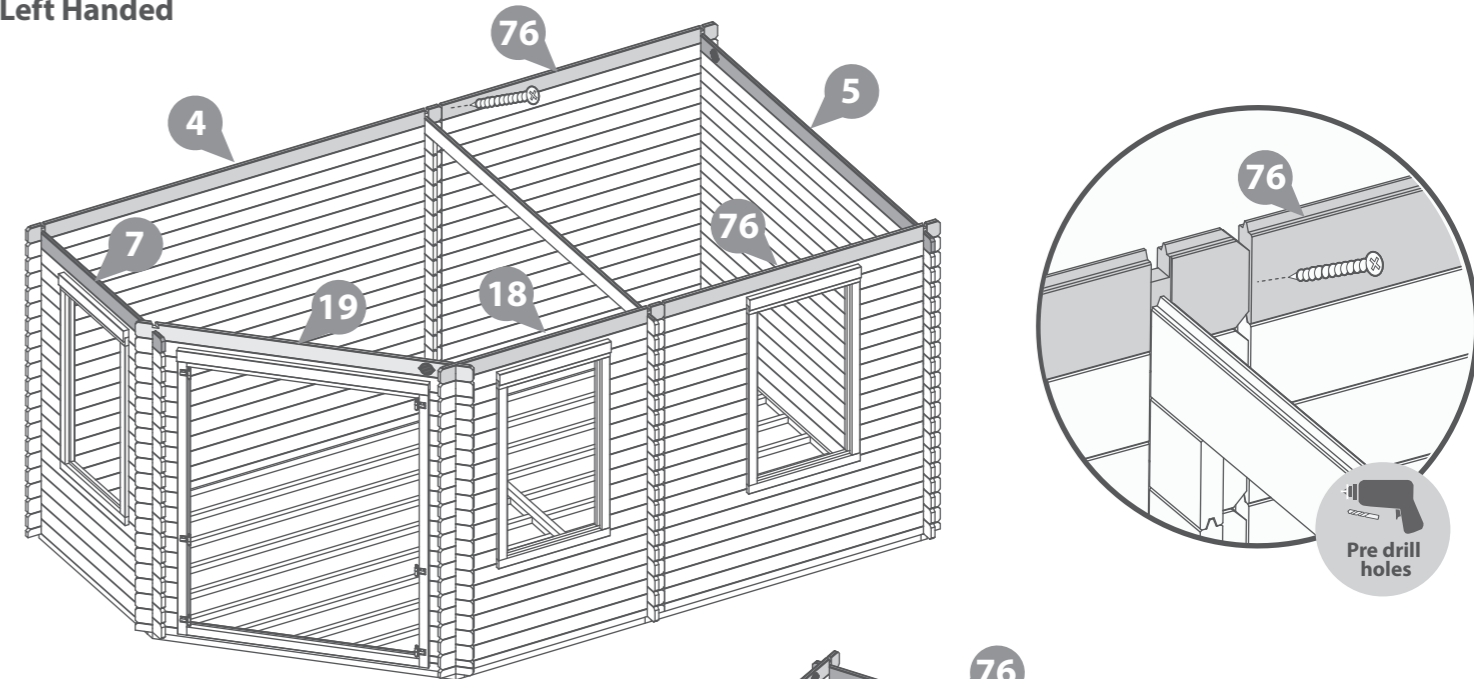

Right Handed

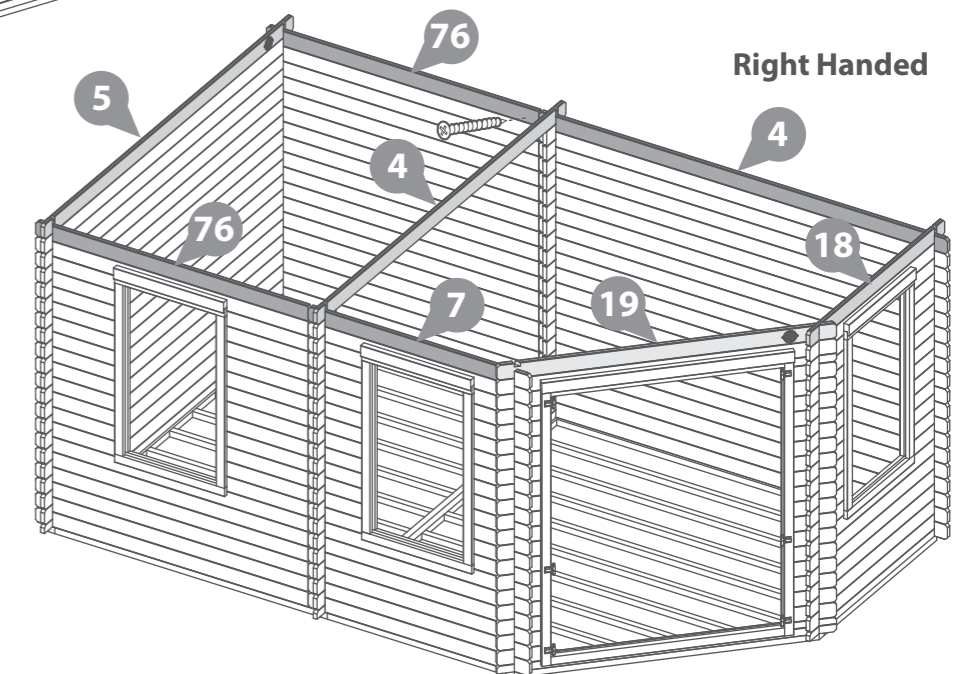

Step 22 - Left Handed
Parts Needed - No. 20 QTY 1
No. 21 QTY 2



Following the method shown in the illustration, lay the Finisher boards (**No. 20 & 21**) onto the log cabin.


***Ensure that the boards are level and flush with each other s you lay each one.**

Fix each board to the one below by screwing through the notch using 1x70mm screw per corner, as shown in the illustration.

6x70mm Screw.
Important: Pre-drill before fixing screws.



Step 22 - Right Handed
Parts Needed - No. 20 QTY 1
No. 21 QTY 1
No. 81 QTY 2



Following the method shown in the illustration, lay the Finisher boards (**No. 20, 21 & 81**) onto the log cabin.



***Ensure that the boards are level and flush with each other s you lay each one.**

Fix each board to the one below by screwing through the notch using 1x70mm screw per corner, as shown in the illustration.



6x70mm Screw.
Important: Pre-drill before fixing screws.



Left Handed

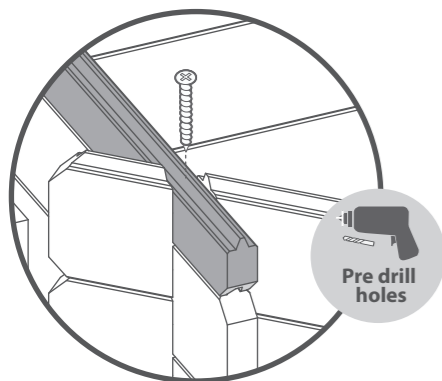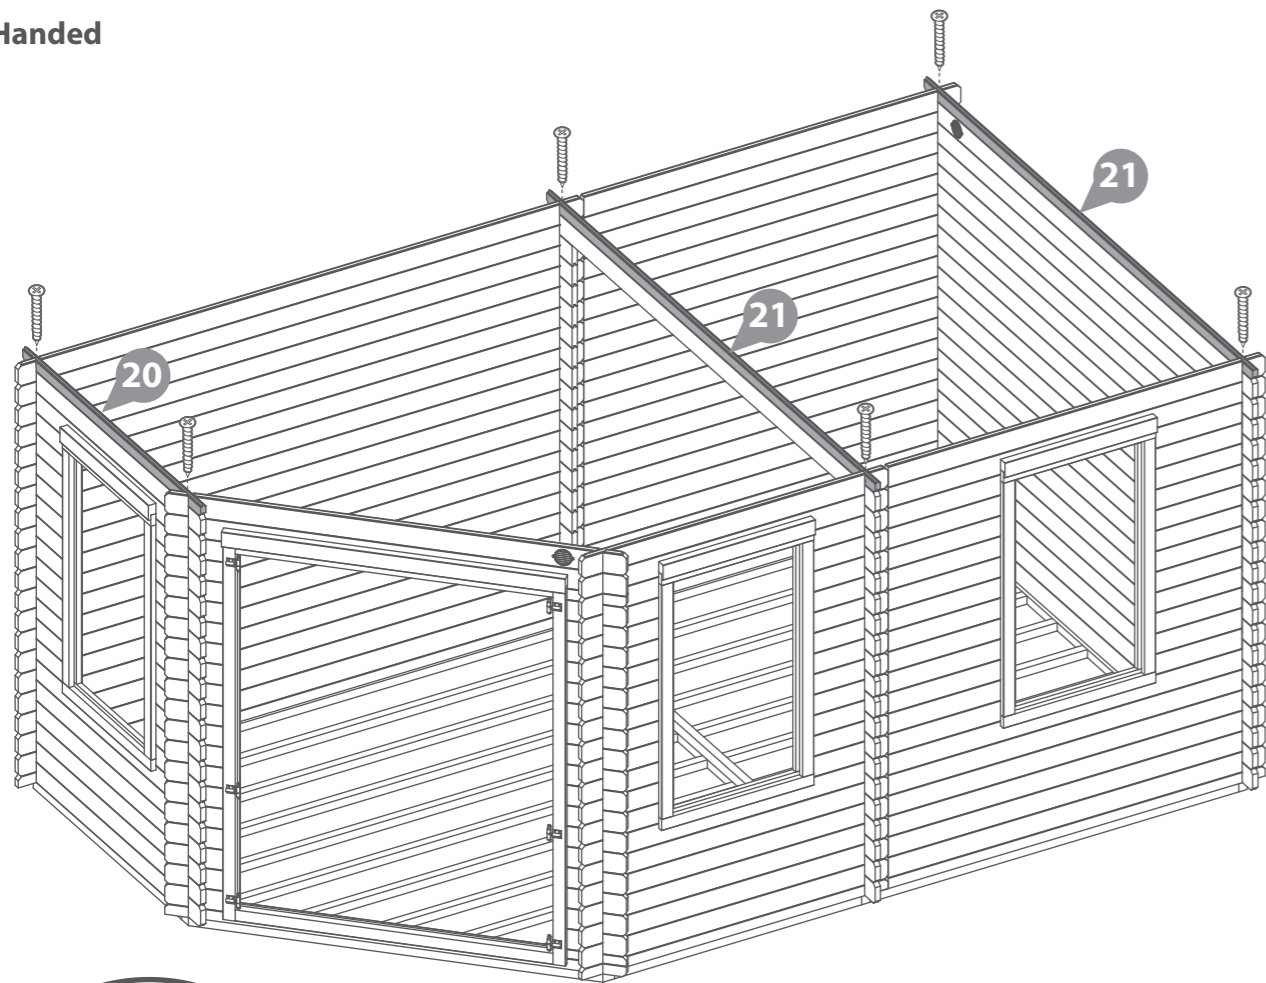

Right Handed

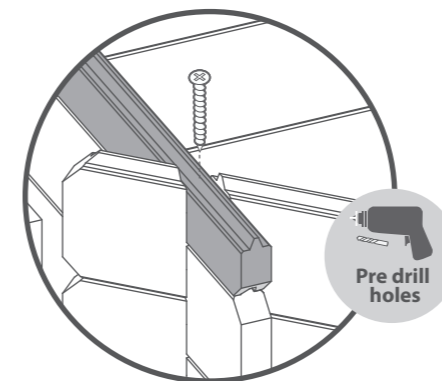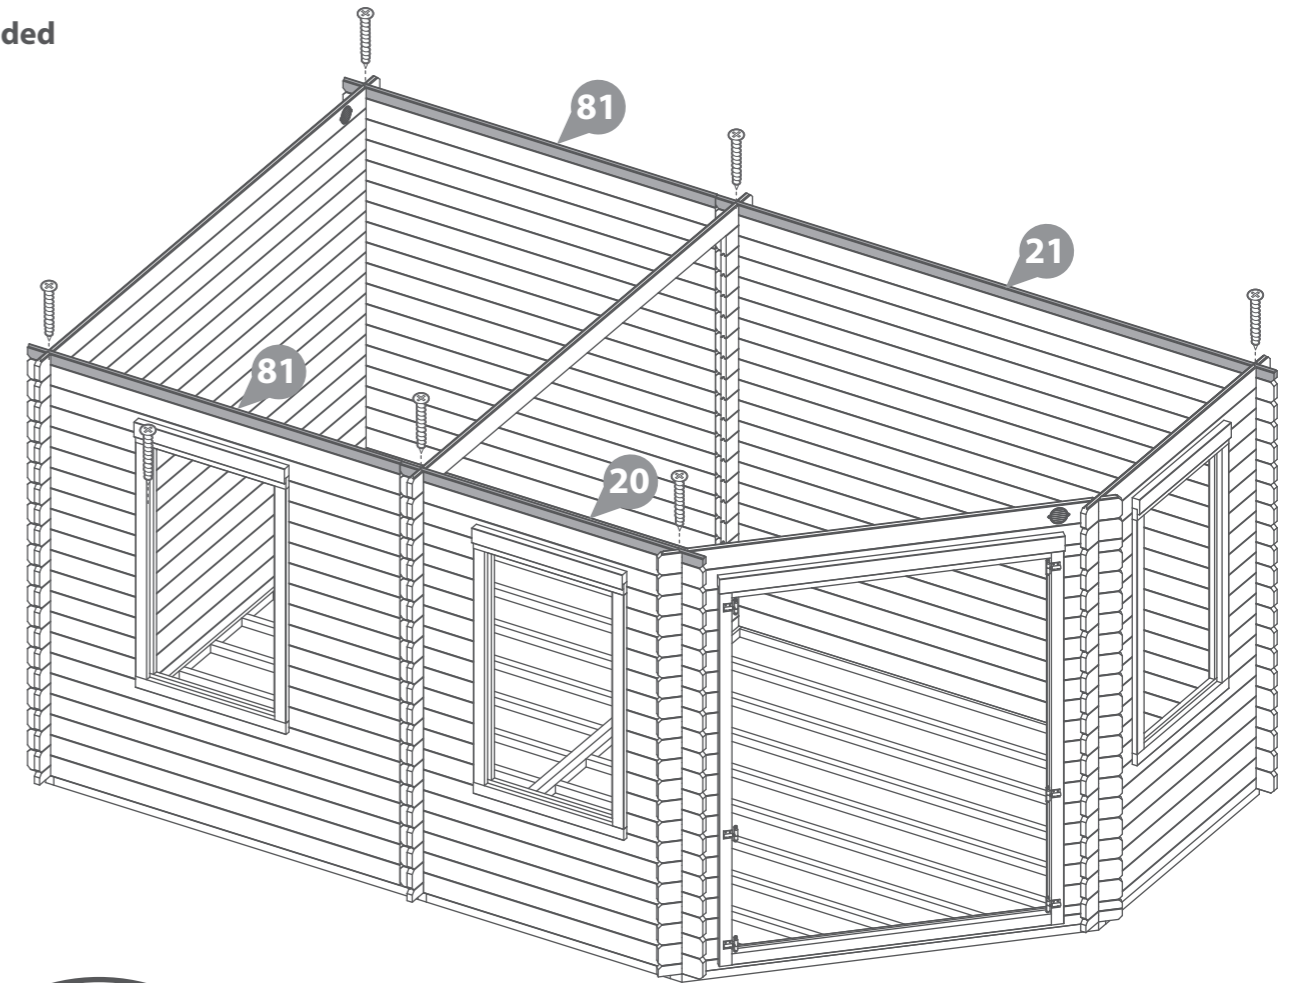

Step 23
Parts Needed - No. 88 QTY 4

Place the double storm braces (**No.88**) on either side of the log cabin, (externally and internally) ensuring to locate them centrally over where the middle log boards sit flush, as shown in the illustration.

***Ensure the storm braces are secured at the highest point possible on each side.**

The storm braces will need to be altered during the buildings life as the moisture content within the log boards changes. The boards will expand during periods of high moisture (Winter) and shrink during periods of low moisture (Summer.)

****Storm braces will help your building expand and contract properly.**




*****It is important that each bolt is tightened using a washer so as not to damage the log boards.**

Secure the double storm braces into position from the inside of the cabin using 4x90mm bolts per 2 storm braces (2 at the top, 2 at the bottom), making sure the washer & nut are tightened from the outside of the log cabin. Ensure the bolts go through both the internal and external double storm brace.


8x90mm Bolts
Important: Pre-drill before fixing screws.



Left Handed

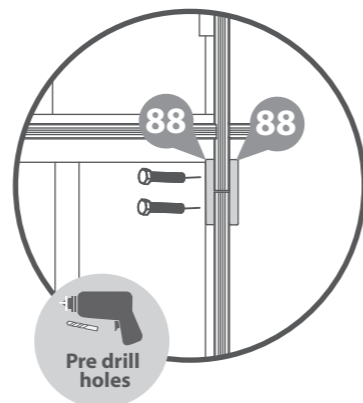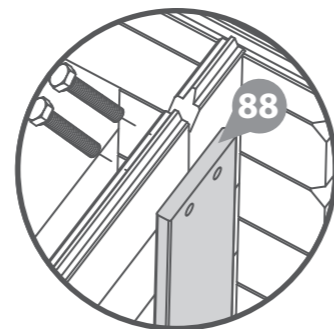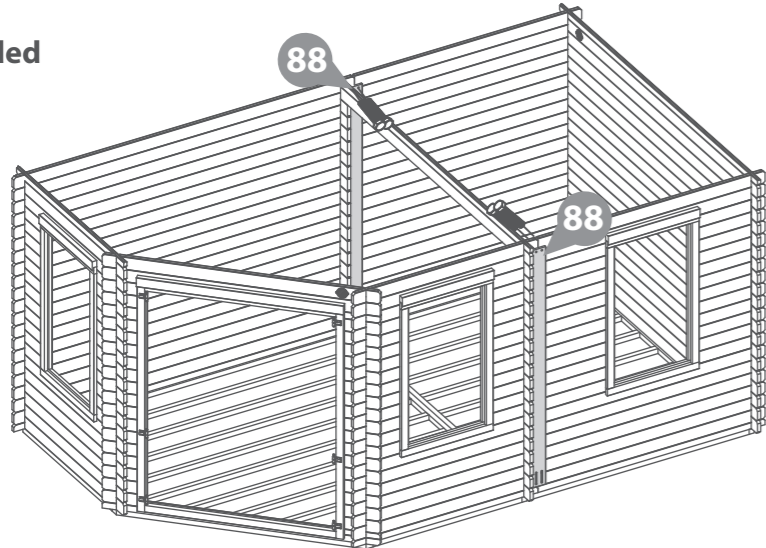

Right Handed

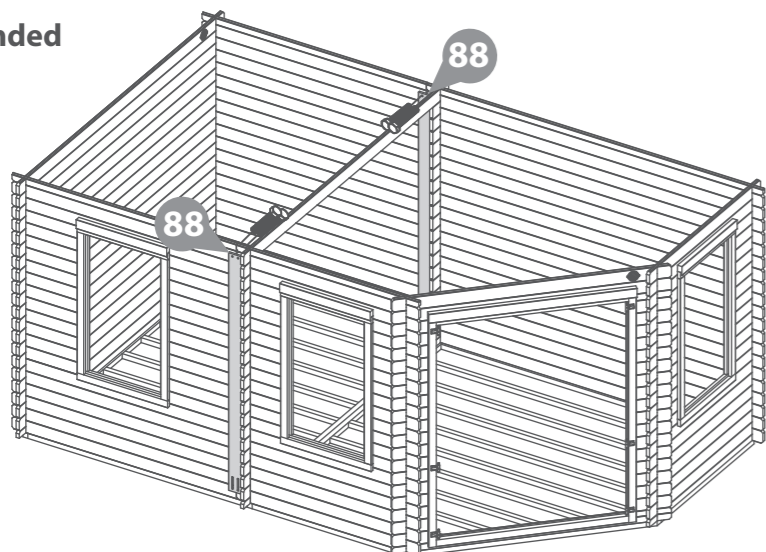


Step 24
Parts Needed - No. 26 QTY 2

Following the method shown in the illustration, locate the Gables (**No. 26**) onto the log cabin.


***Ensure that the boards are level and flush with each other as you lay each one.**

Fix the gables to the boards below by screwing through the notch using 1x120mm screw per corner, as shown in the illustration.



4x120mm Screws
Important: Pre-drill before fixing screws.



Left Handed

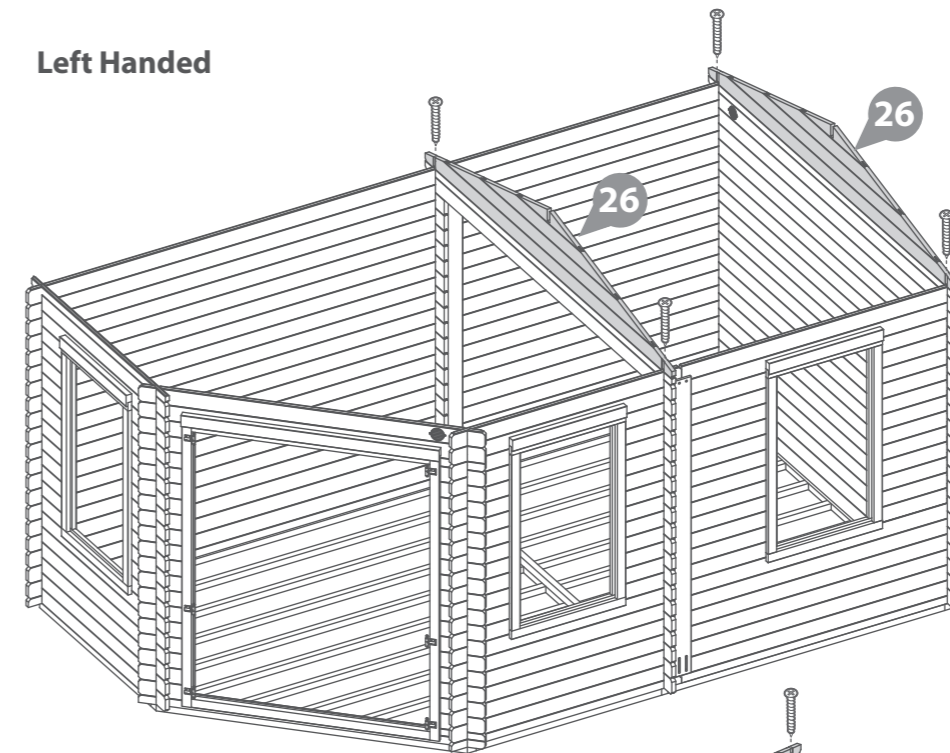

Right Handed

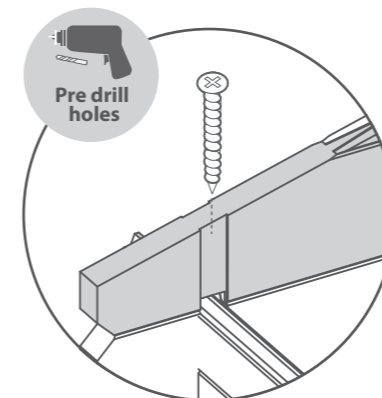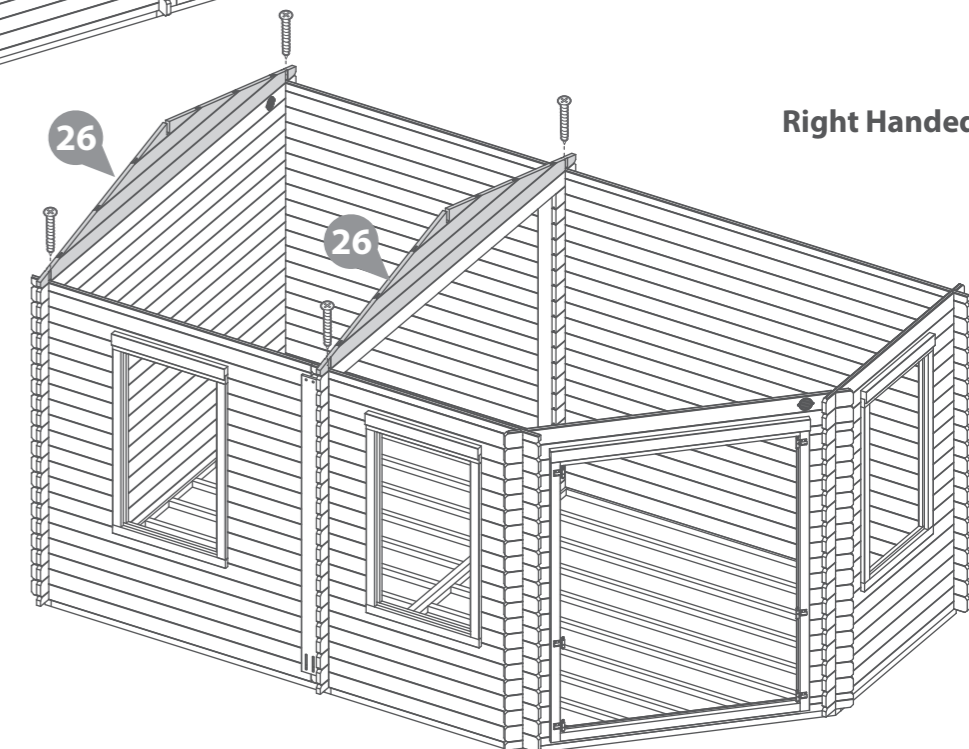

Step 25

Parts needed - No. 84 QTY 1

Align the Purlin (**No.84**) into the cut out notches on the Gables, ensuring they interlock.

Note: Use a mallet and a scrap piece of wood to gently fix the purlins into position.

Secure the Roof Purlins in place by screwing through the notches at an angle into the gable, using 2x90mm screws per notch, as shown.

4x90mm Screws.


Important: Pre-drill before fixing screws.





Rubber Mallet. Drill / Pre drill.

90mm screw

Left Handed

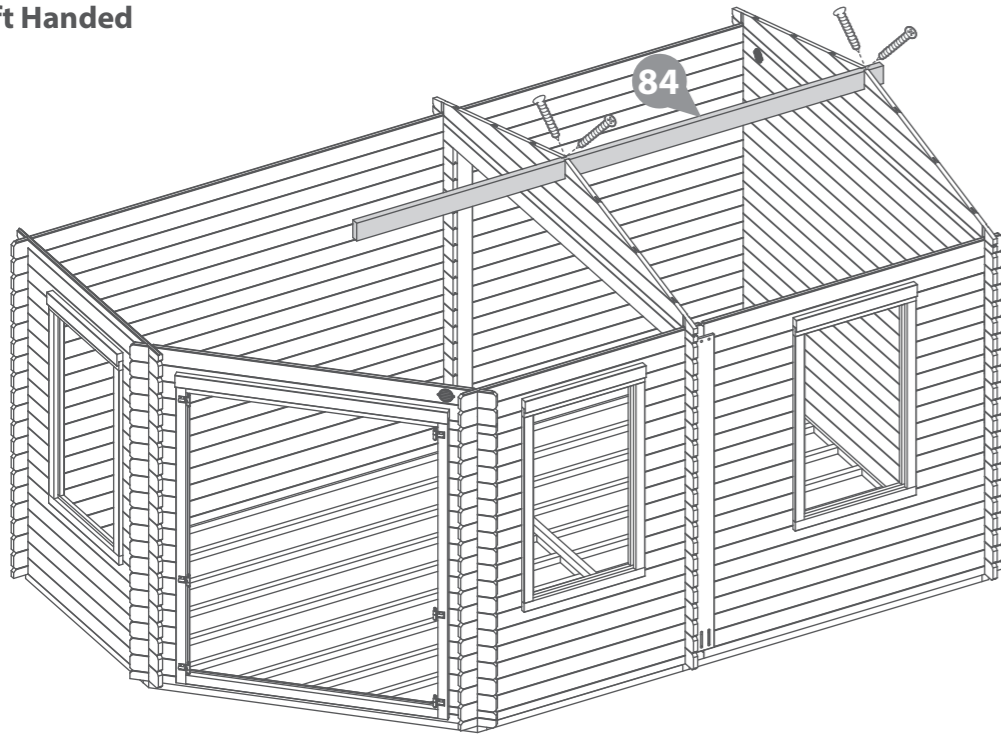

Right Handed

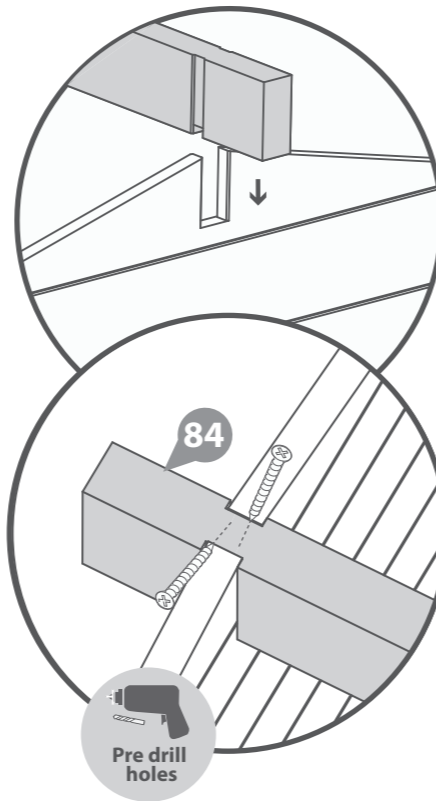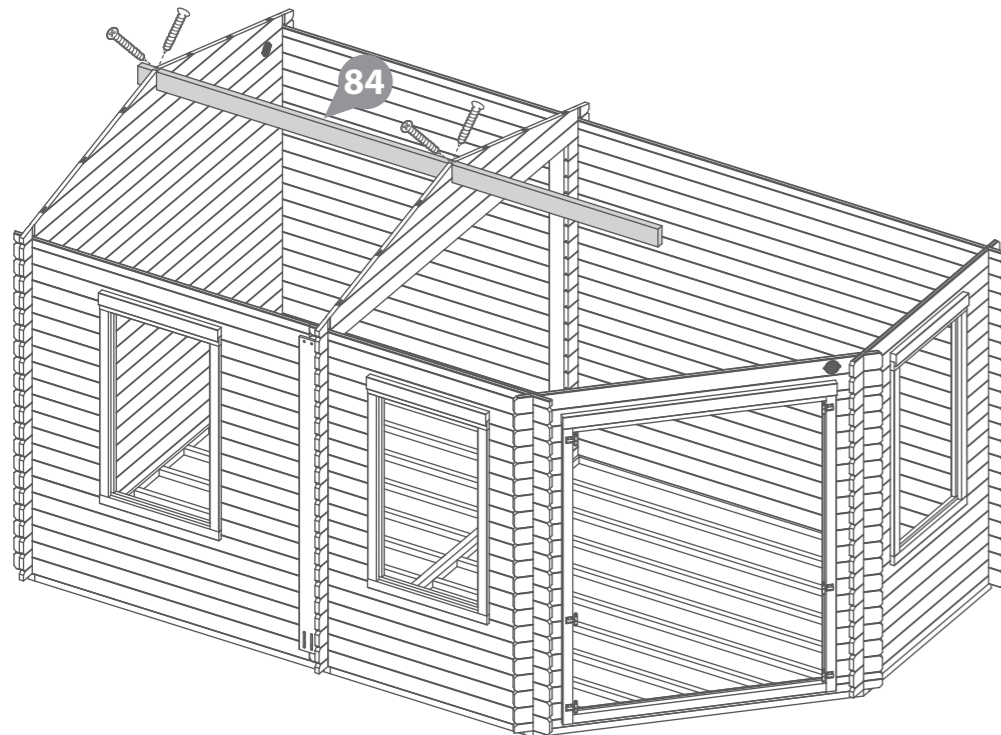

Step 26 - Left Handed

- Parts needed - No. 29 QTY 1
 No. 31 QTY 1
 No. 32 QTY 1

Place the Central roof Truss ' Roof Truss D (No.32) flush to the end of the Roof Purlin (No. 84).




Place Roof Truss C (No.31) and Roof Truss A (No.29) onto either side of the Roof Purlin (No.84) ensuring they sit flush to the end, creating a 'T' shape, as shown in the illustration.

Fix in place by screwing through the truss at an angle into the Purlin using 1x90mm screw per truss, as shown.

3x90mm Screws
Important: Pre-drill before fixing screws.



Left Handed

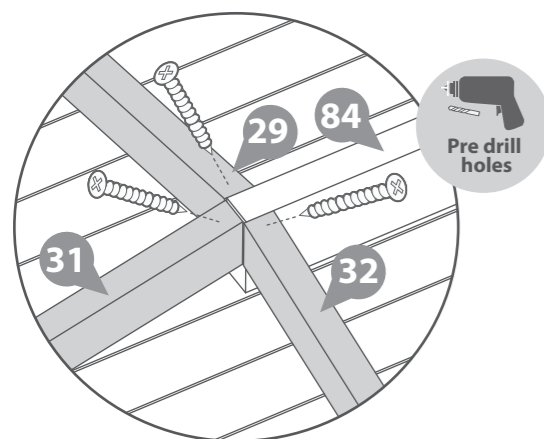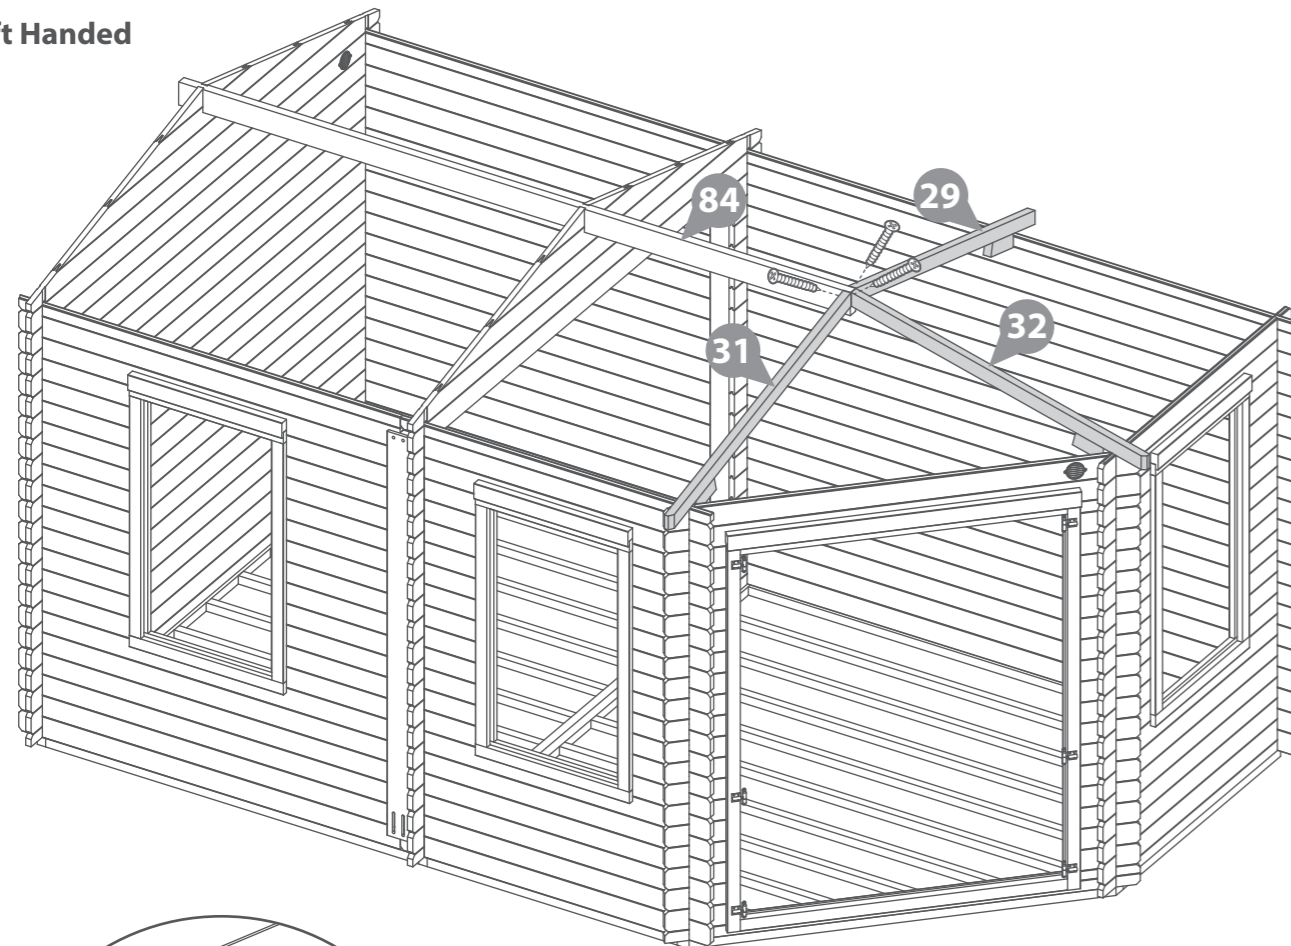

Please note: You can adjust the blocks attached to the roof truss' if necessary.

Step 26 - Right Handed

- Parts needed - No. 29 QTY 1
 No. 31 QTY 1
 No. 32 QTY 1

Place the Central roof Truss Roof Truss C (No.31) flush to the end of the Roof Purlin (No. 84).




Place Roof Truss D (No.32) and Roof Truss A (No.29) onto either side of the Roof Purlin (No.84) ensuring they sit flush to the end, creating a 'T' shape, as shown in the illustration.

Fix in place by screwing through the truss at an angle into the Purlin using 1x90mm screw per truss, as shown.

3x90mm Screws
Important: Pre-drill before fixing screws.



Right Handed

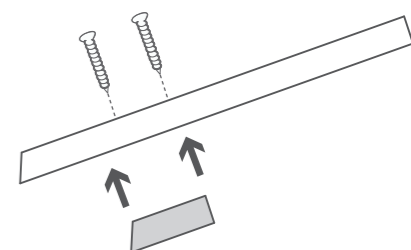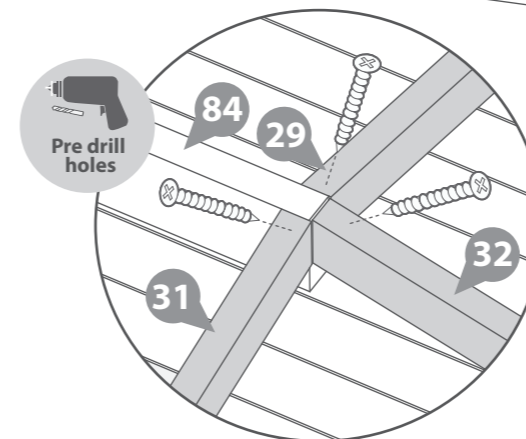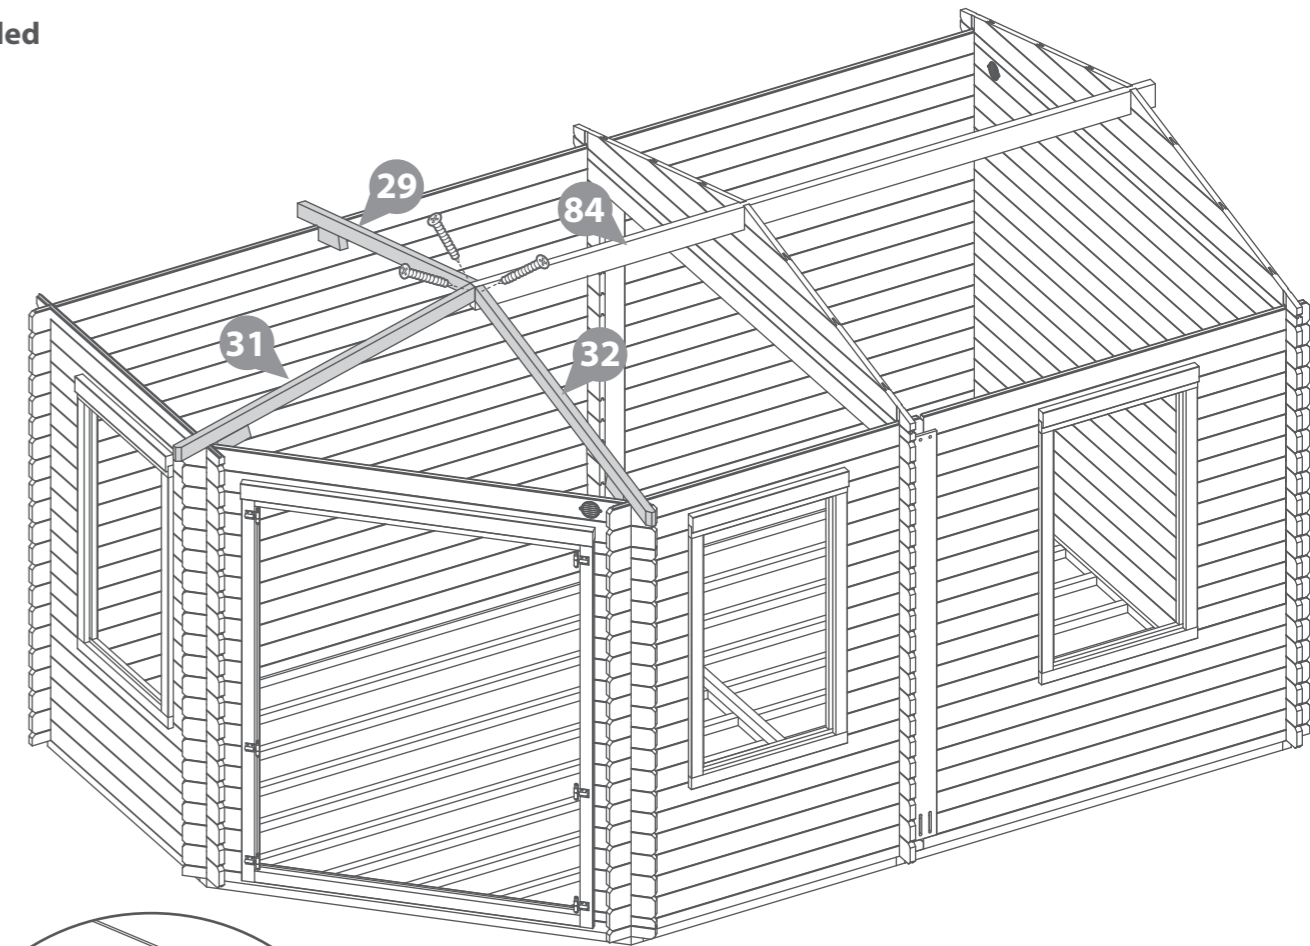

Please note: You can adjust the blocks attached to the roof truss' if necessary.

Step 27

Parts needed - No. 30 QTY 1

Place 'Roof Truss B' (**No. 30**) between Roof Truss A (**No.29**) and the Central Roof Truss (Truss D for Roof Assembly 1, and Truss C for Roof Assembly 2) as shown in the illustration.




Fix in place by screwing through the truss at an angle into the purlin using 1x90mm screws shown.

**Ensure to stagger screws to avoid screws colliding.*

1x90mm Screws
Important: Pre-drill before fixing screws.






Left Handed

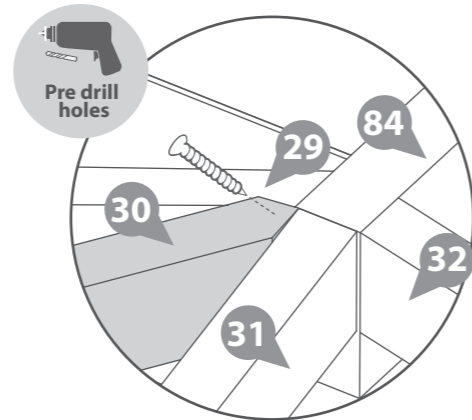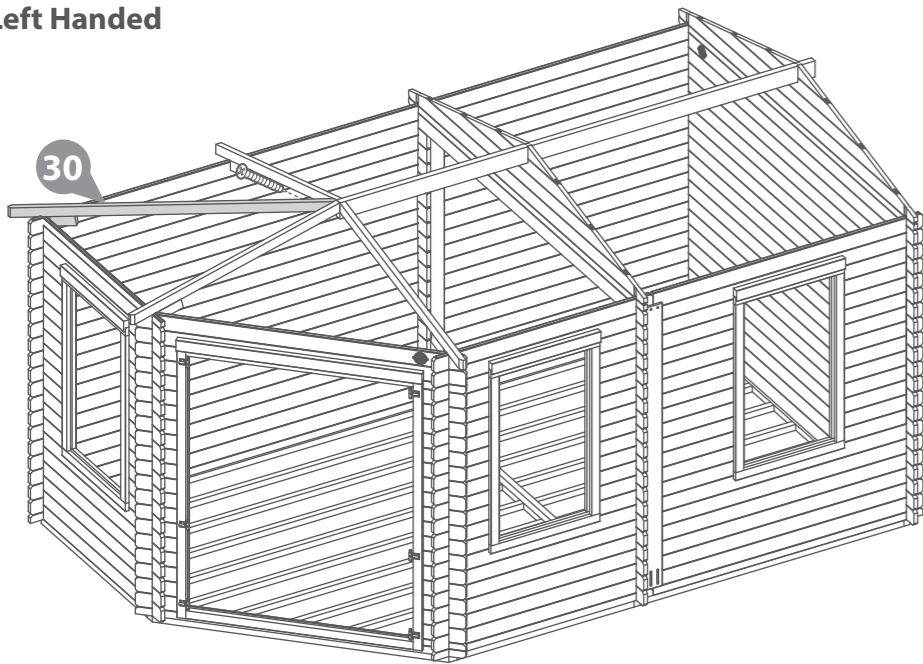

Please note: You can adjust the blocks attached to the roof truss' if necessary.

Right Handed

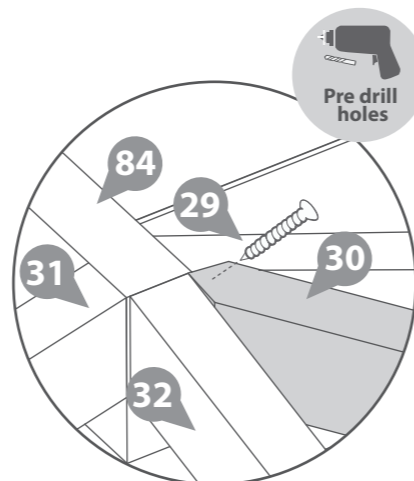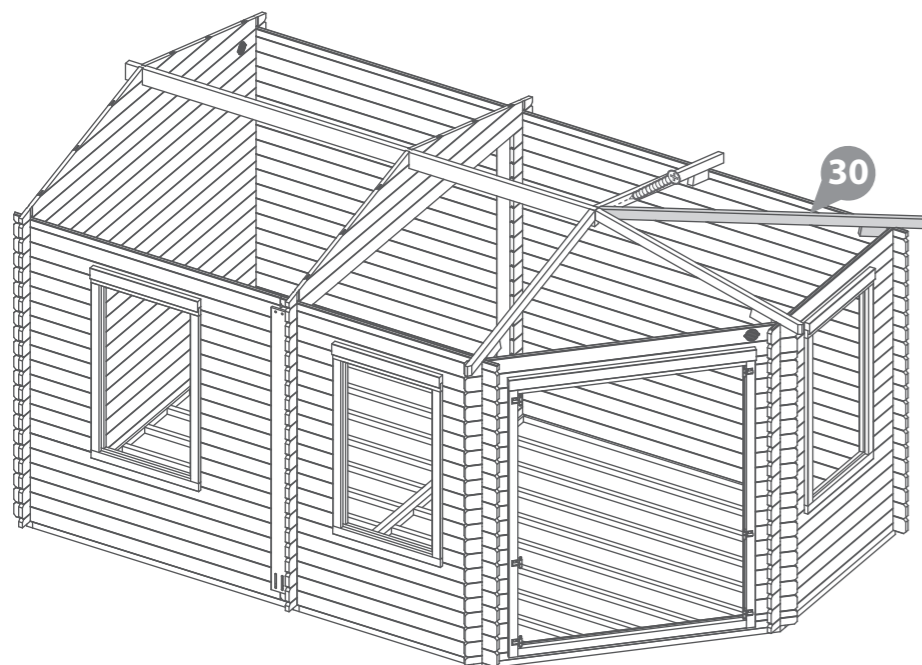

Please note: You can adjust the blocks attached to the roof truss' if necessary.

Step 28

Parts needed - No. 29 QTY 4

Place one 'Roof Truss A' (**No. 29**) flush to the inside of the gables on either side of the Purlin, as shown.



Fix in place by screwing through the truss at an angle into the purlin using 1x90mm screws shown.

**Ensure to stagger screws to avoid screws colliding.*


4x90mm Screws
Important: Pre-drill before fixing screws.



Left Handed

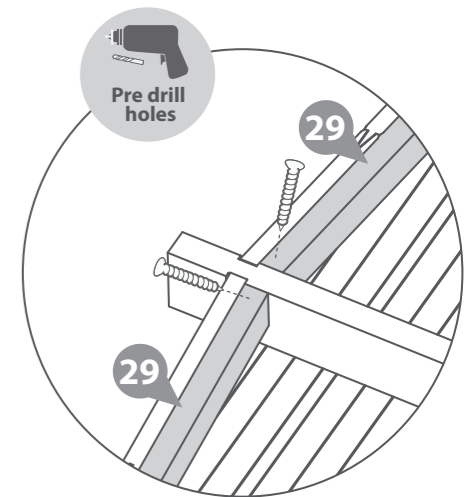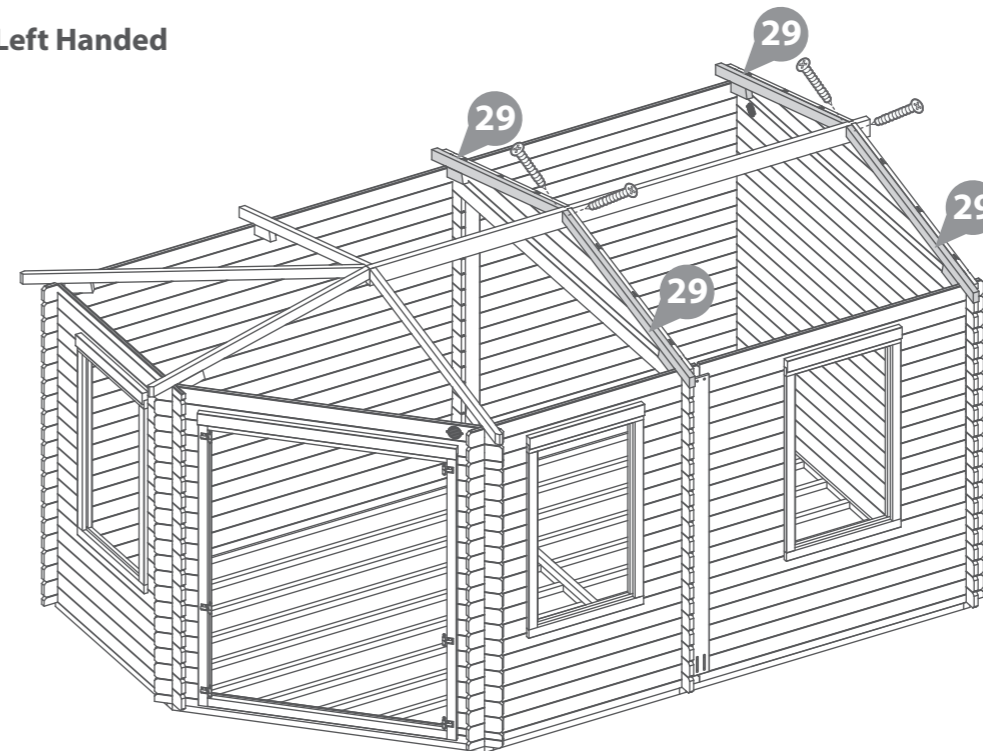

Right Handed

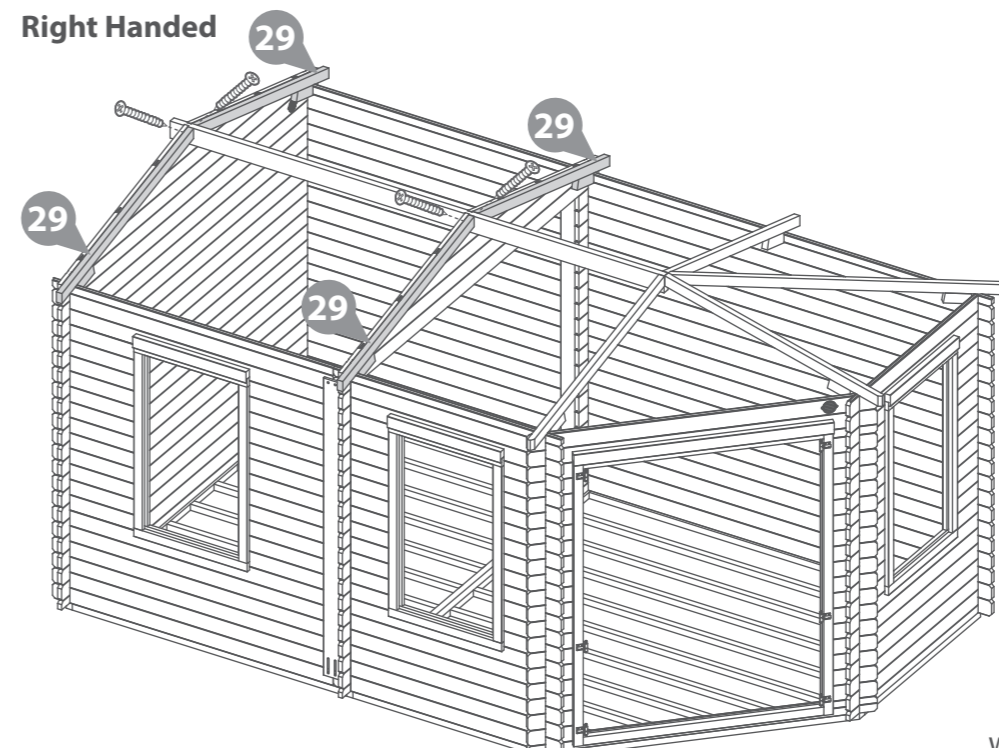

Step 29

**Parts needed - No. 27 QTY 1
No. 28 QTY 1**

Position the Left and Right Roof Truss' (No. 27 & 28) up against 'Roof Truss B' (No.30), ensuring the angled sides are flush to the long framing of Roof Truss B and that the block is flush against the cabin walls, as shown.



Secure the Left and Right Truss' (No. 27 & 28) to Truss B (No.30) using 1x90mm screws per truss.

**Ensure to stagger screws to avoid screws colliding.*



2x90mm Screws
Important: Pre-drill before fixing screws.



Left Handed

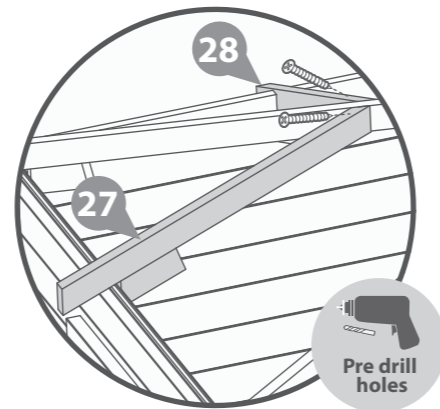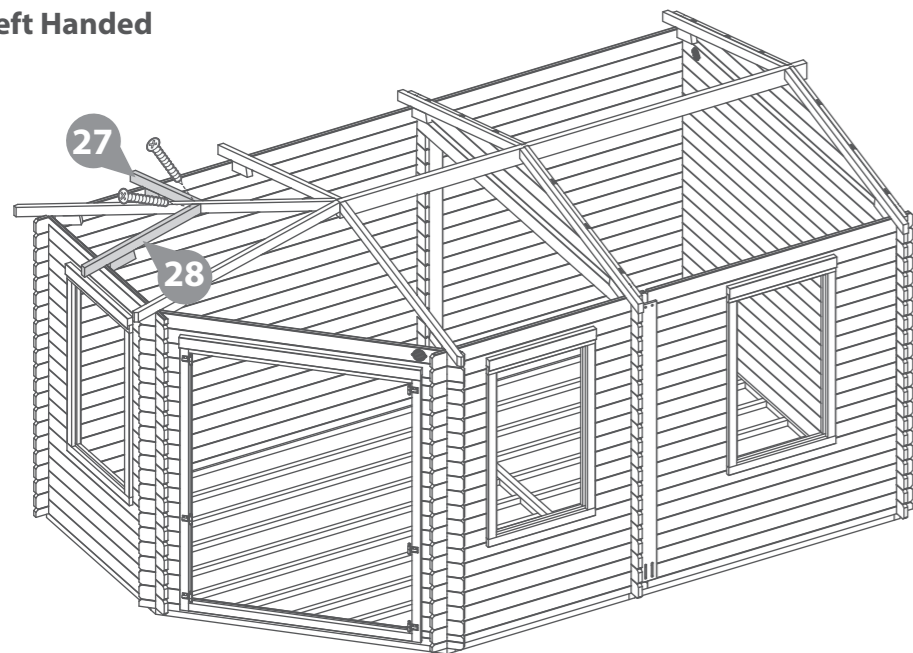

Right Handed

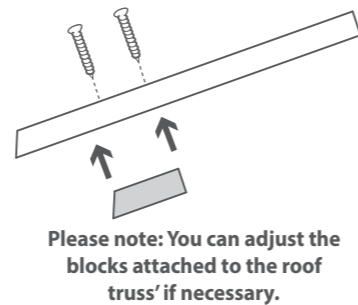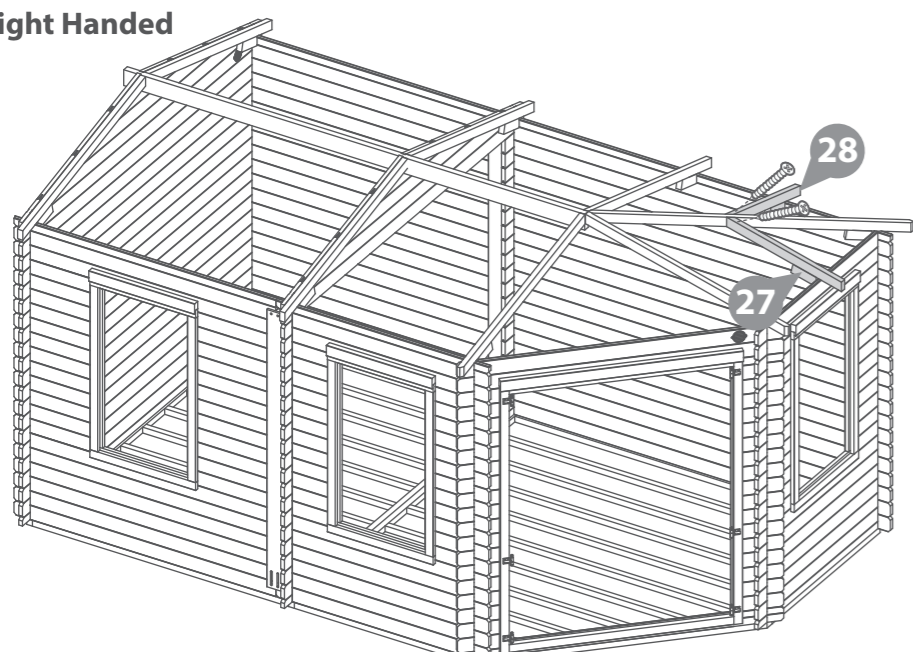

Step 30

**Parts needed - No. 22 QTY 1
No. 23 QTY 1
No. 24 QTY 1
No. 25 QTY 6**

Position the Finisher Boards (No. 22, 23, 24 & 25) around the building as shown, locating each board flush to the adjacent truss'. Ensure there is at least a 42mm gap between parts No. 25 on both sides of the log cabin.



Some adjustment may be required to ensure the roof structure rests correctly.

Secure each board in place by screwing through the board at an angle into the adjacent Roof Truss using 2x70mm screws per board, ensuring to stagger the screws to avoid them colliding.




14x70mm Screws
Important: Pre-drill before fixing screws.



Left Handed

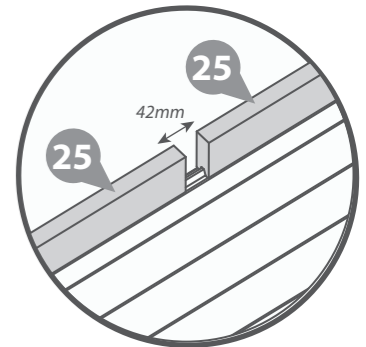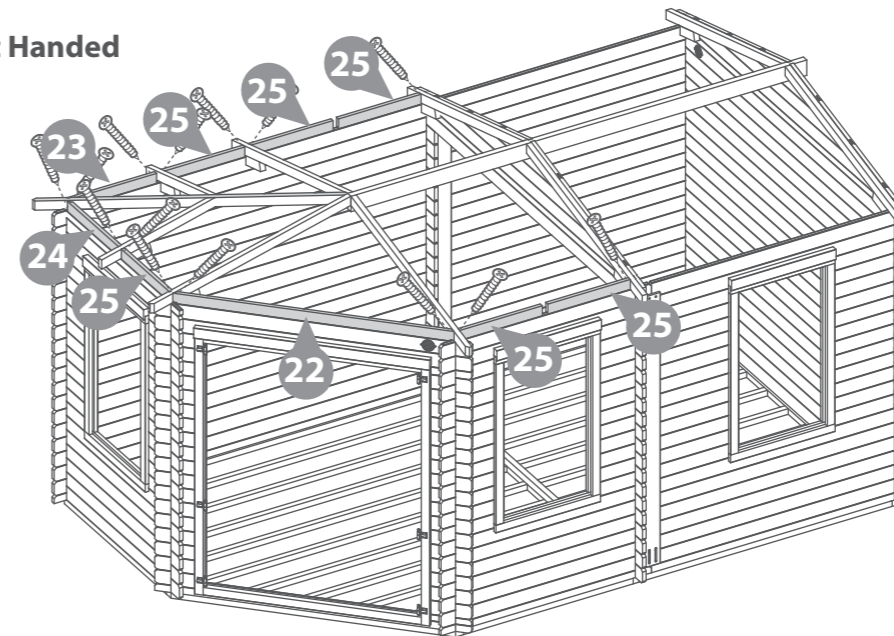

Right Handed

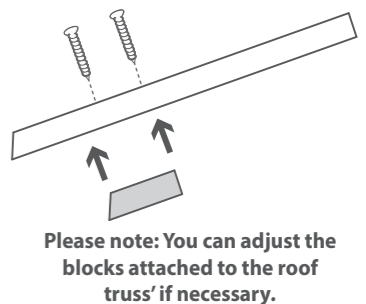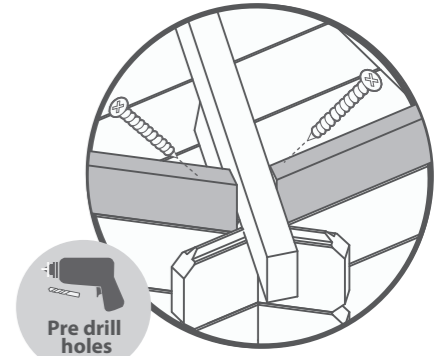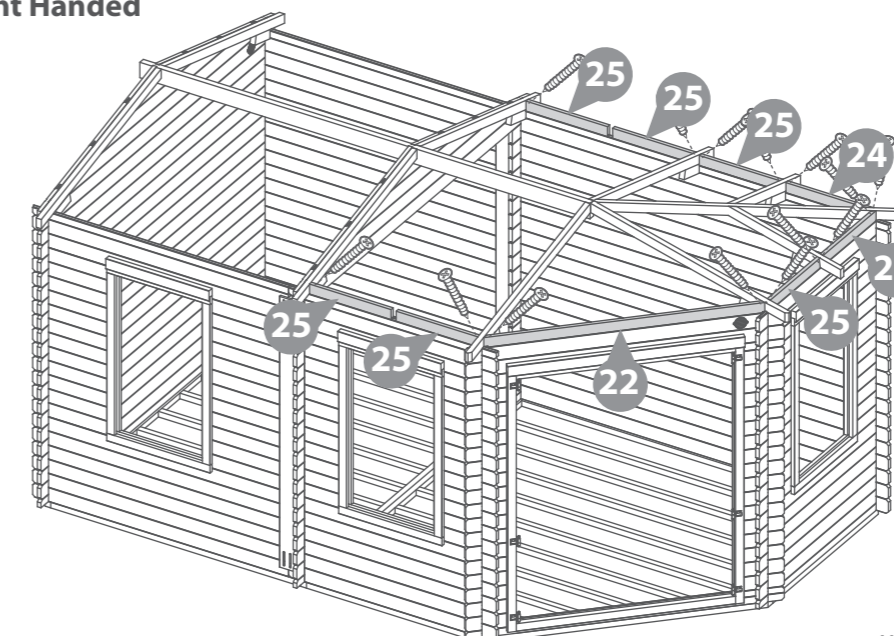

Step 31

Parts needed - No. 29 QTY 2

Locate the last two 'Roof Truss A' (**No. 29**) into the 42mm gaps between the Finisher boards (**No.25**) on either side of the cabin, as shown in the illustration.

Some adjustment may be required to ensure the roof structure rests correctly.

Fix the Roof Truss' (**No.29**) in place by screwing through the truss at an angle into the purlin using 1x90mm screw per Roof Truss, as shown in the illustration.

Secure the Finisher boards (**No. 25**) in place by screwing through the board at an angle into the Roof Truss using 2x70mm screws per board, ensuring to stagger the screws to avoid them colliding.

4x70mm Screws
2x90mm Screws

Important: Pre-drill before fixing screws.



Step 32

Parts needed - No. 29 QTY 2
No. 83 QTY 2

Place the Finisher boards (**No. 83**) either side of the log cabin, locating each board flush to the central gable. Locate two Roof Truss A's (**No. 29**) flush to the finisher boards on either side, as shown in the illustration.

Some adjustment may be required to ensure the roof structure rests correctly.

Fix the Truss (**No.29**) in place by screwing through the truss at an angle into the purlin using 1x90mm screw per Roof Truss.


Secure each Finisher board (**No.83**) in place by screwing through the board at an angle into the Roof Truss and gable using 2x70mm screws per board, ensuring to stagger the screws to avoid them colliding.

4x70mm Screws
2x90mm Screws


Important: Pre-drill before fixing screws.



Left Handed

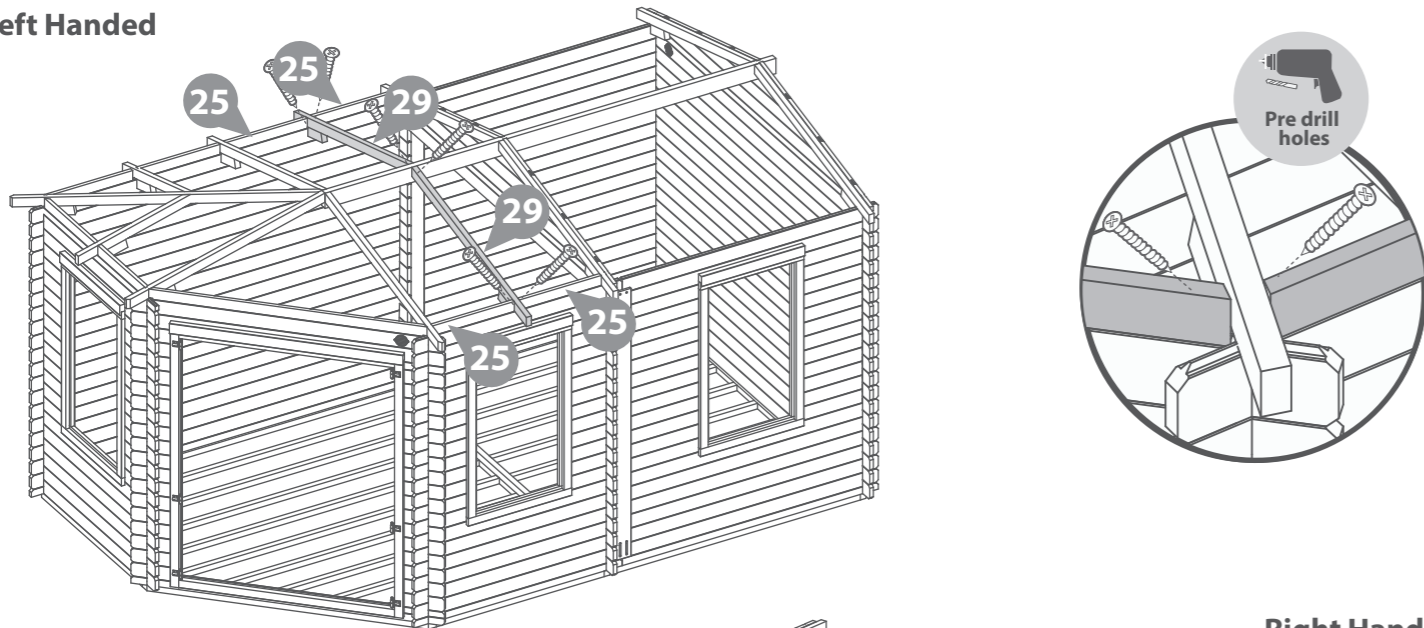


Right Handed

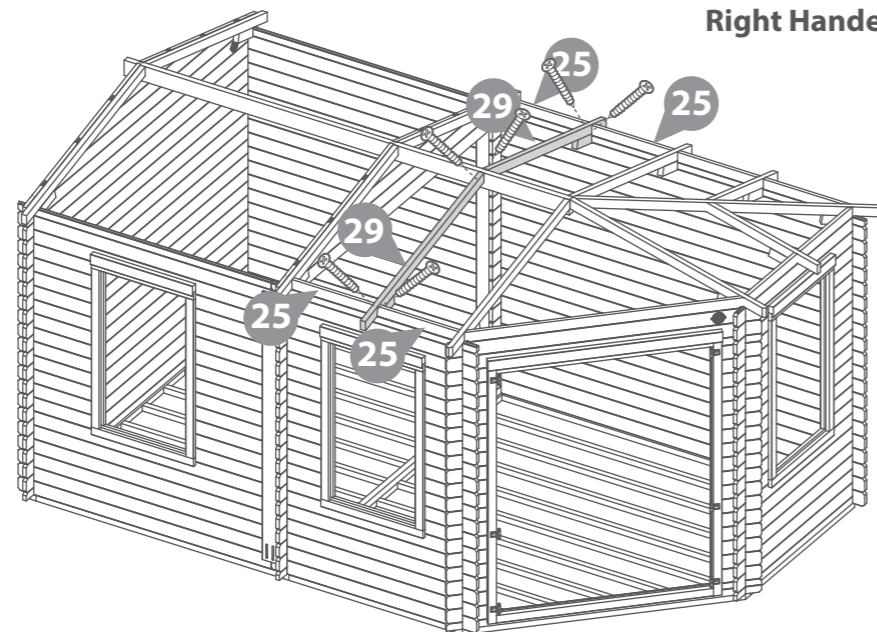


Please note: You can adjust the blocks attached to the roof truss' if necessary.

Left Handed

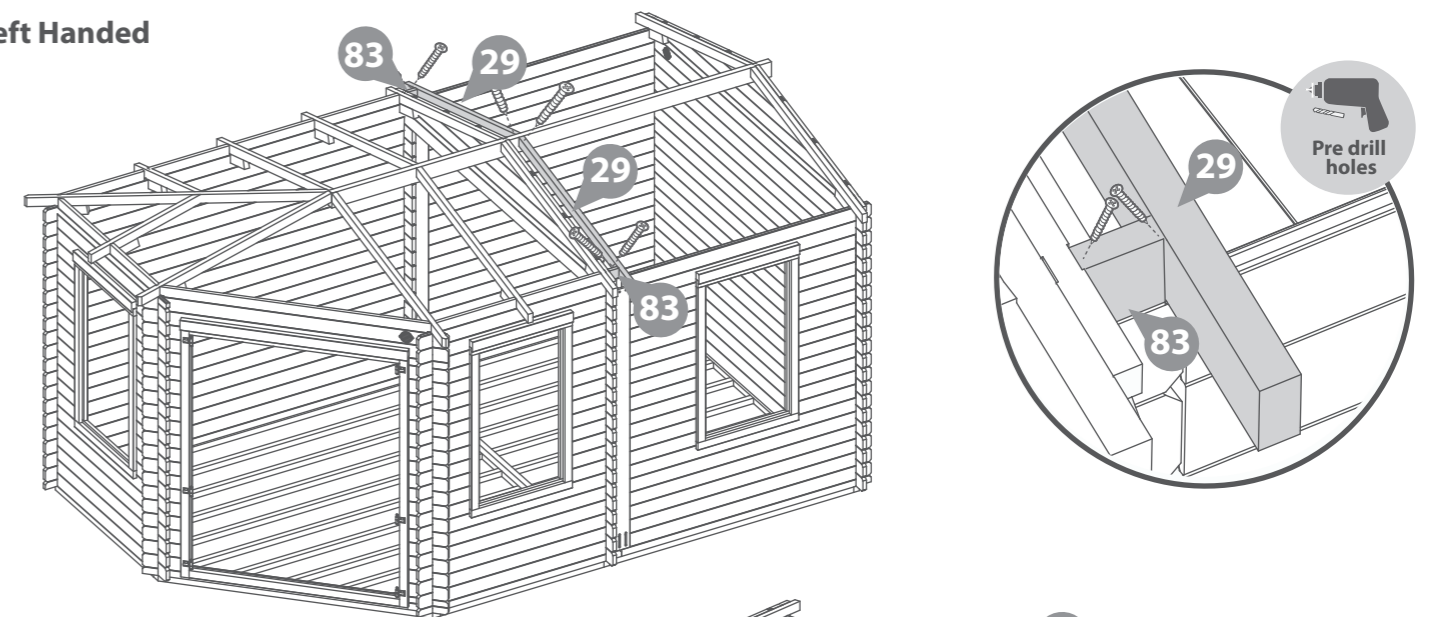

Right Handed

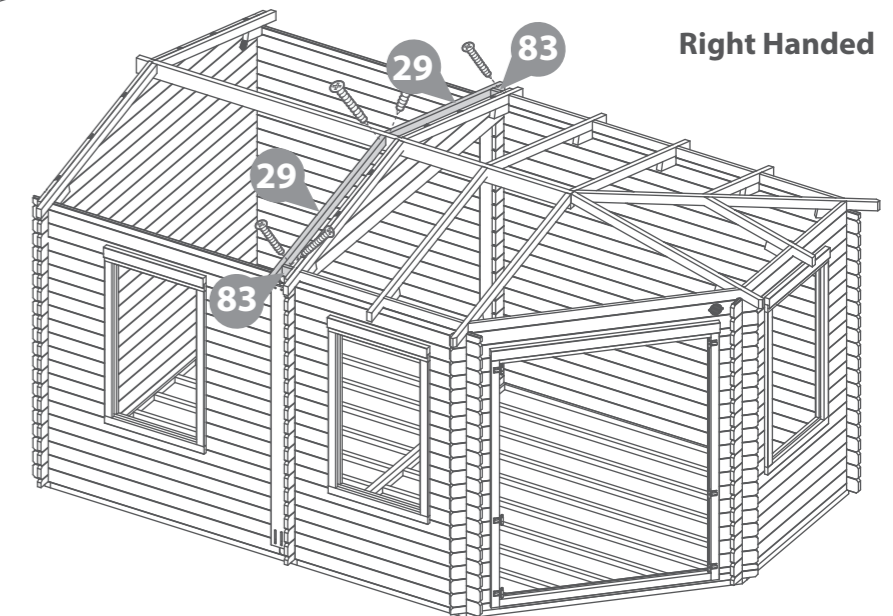

Please note: You can adjust the blocks attached to the roof truss' if necessary.

Step 33

Parts needed - No. 29 QTY 2
No. 82 QTY 4

Place the Finisher Boards (**No. 82**) around the back of the log cabin, locating each board flush to the truss'. Ensure there is a gap between the finisher boards and gables on either side of the log cabin, with enough space to locate a Roof Truss.

Locate the last two Roof Truss A's (**No. 29**) into the gaps between the finisher boards **No. 82** on either side of the log cabin, as shown in the illustration.

Some adjustment may be required to ensure the roof structure rests correctly.



Fix the Roof Truss' (**No.29**) in place by screwing through the truss at an angle into the purlin using 1x90mm screw per Roof Truss.

Secure the Finisher boards (**No. 82**) in place by screwing through the board at an angle into the Roof Truss using 2x70mm screws per board, ensuring to stagger the screws to avoid them colliding.



8x70mm Screws
2x90mm Screws
Important: Pre-drill before fixing screws.



Left Handed

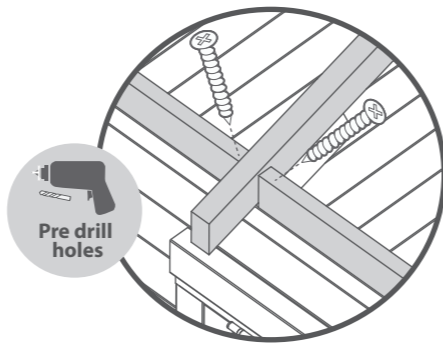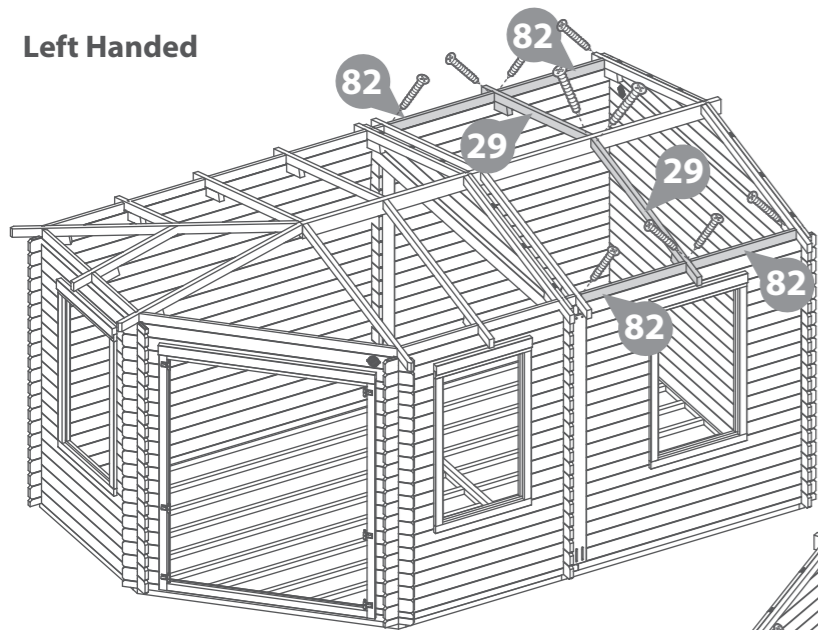

Right Handed

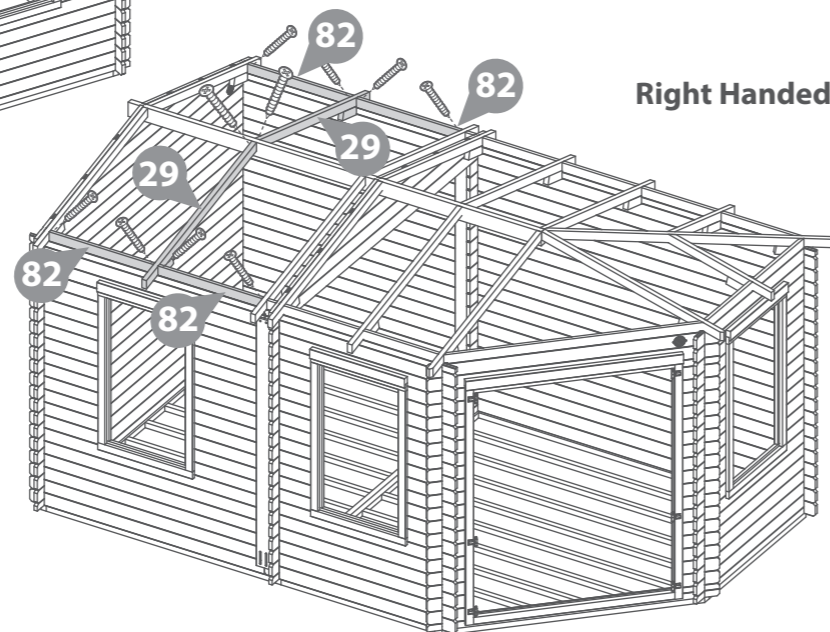

Please note: You can adjust the blocks attached to the roof truss' if necessary.

Step 34



You can now fix the assembled roof truss' and Roof Purlin to the log cabin, making sure the attached blocks sit inside the assembly. Some adjustment may be required to ensure the roof structure rests correctly.

Once in position fix the roof truss' to the log cabin by screwing down through the truss into the board below using 1x120mm screw per truss, as shown in the diagram. Ensure to stagger screws to avoid them colliding.



16x120mm Screws
Important: Pre-drill before fixing screws.



Left Handed

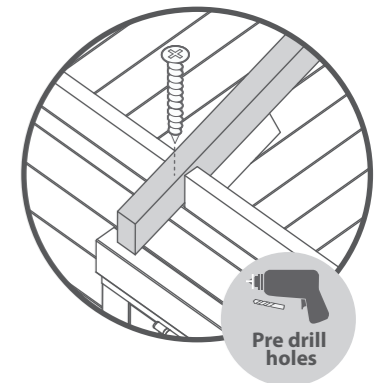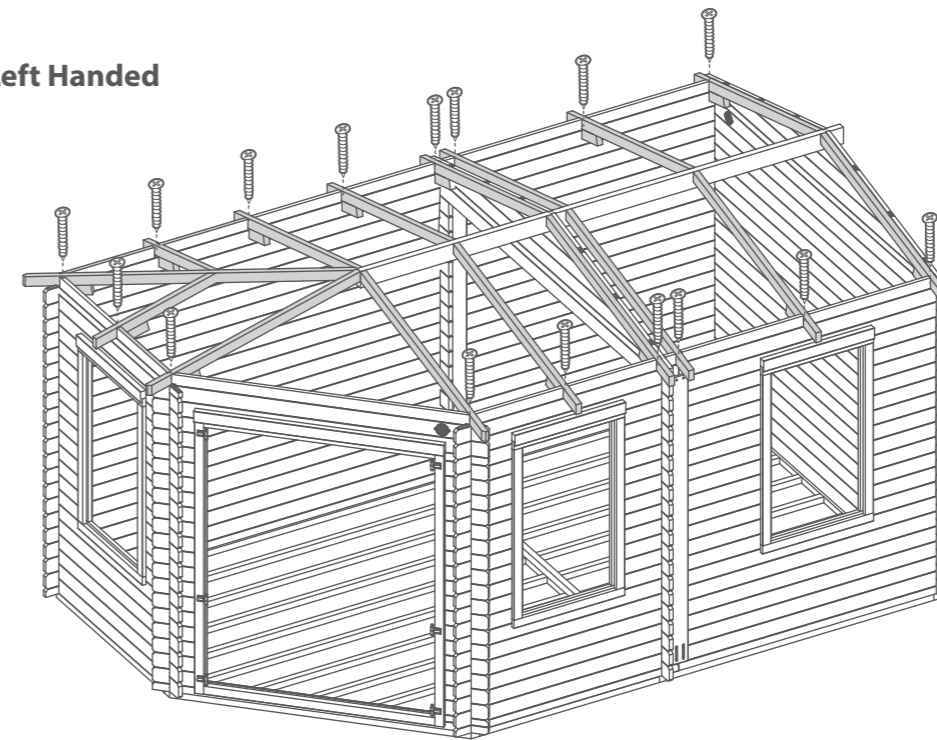

Right Handed

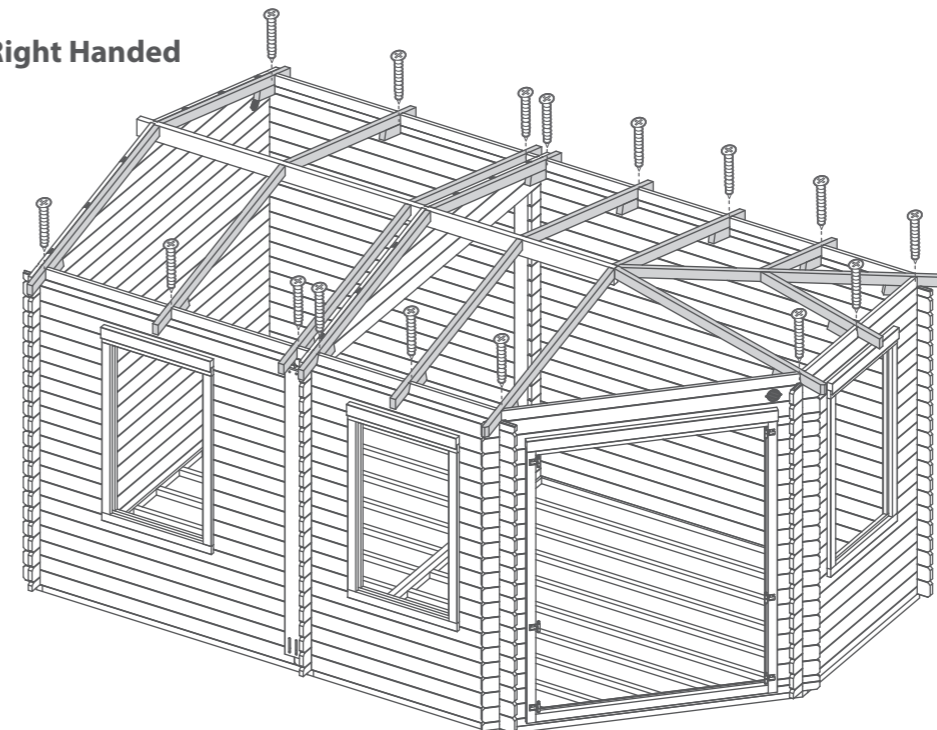

Please note: You can adjust the blocks attached to the roof truss' if necessary.

Step 35



- Parts needed - No. 34 QTY 1 Pack A**
No. 35 QTY 2 Pack B
No. 36 QTY 2 Pack C
No. 87 QTY 2 Pack D

***HINT: keep the individual roof board packs together to avoid mixing them up.**


Place the first board from each 'Roof Board Pack' (No. 34, 35, 36 & 87) onto the roof assembly, working around the structure, laying each roof board one by one.

Once you are happy with the fit of the roof boards, fix the boards into place using 40mm screws, ensuring to fix through the roof board into the truss below.


40x40mm screws
Important: Pre-drill before fixing screws.

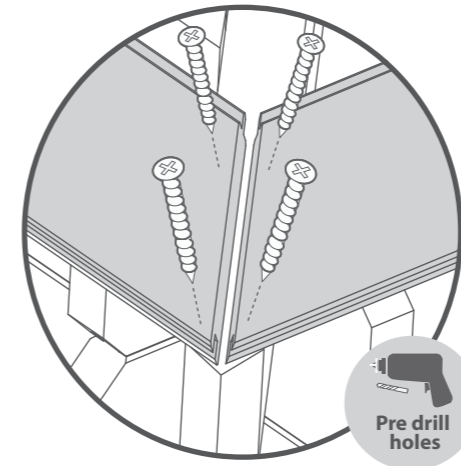

Left Handed

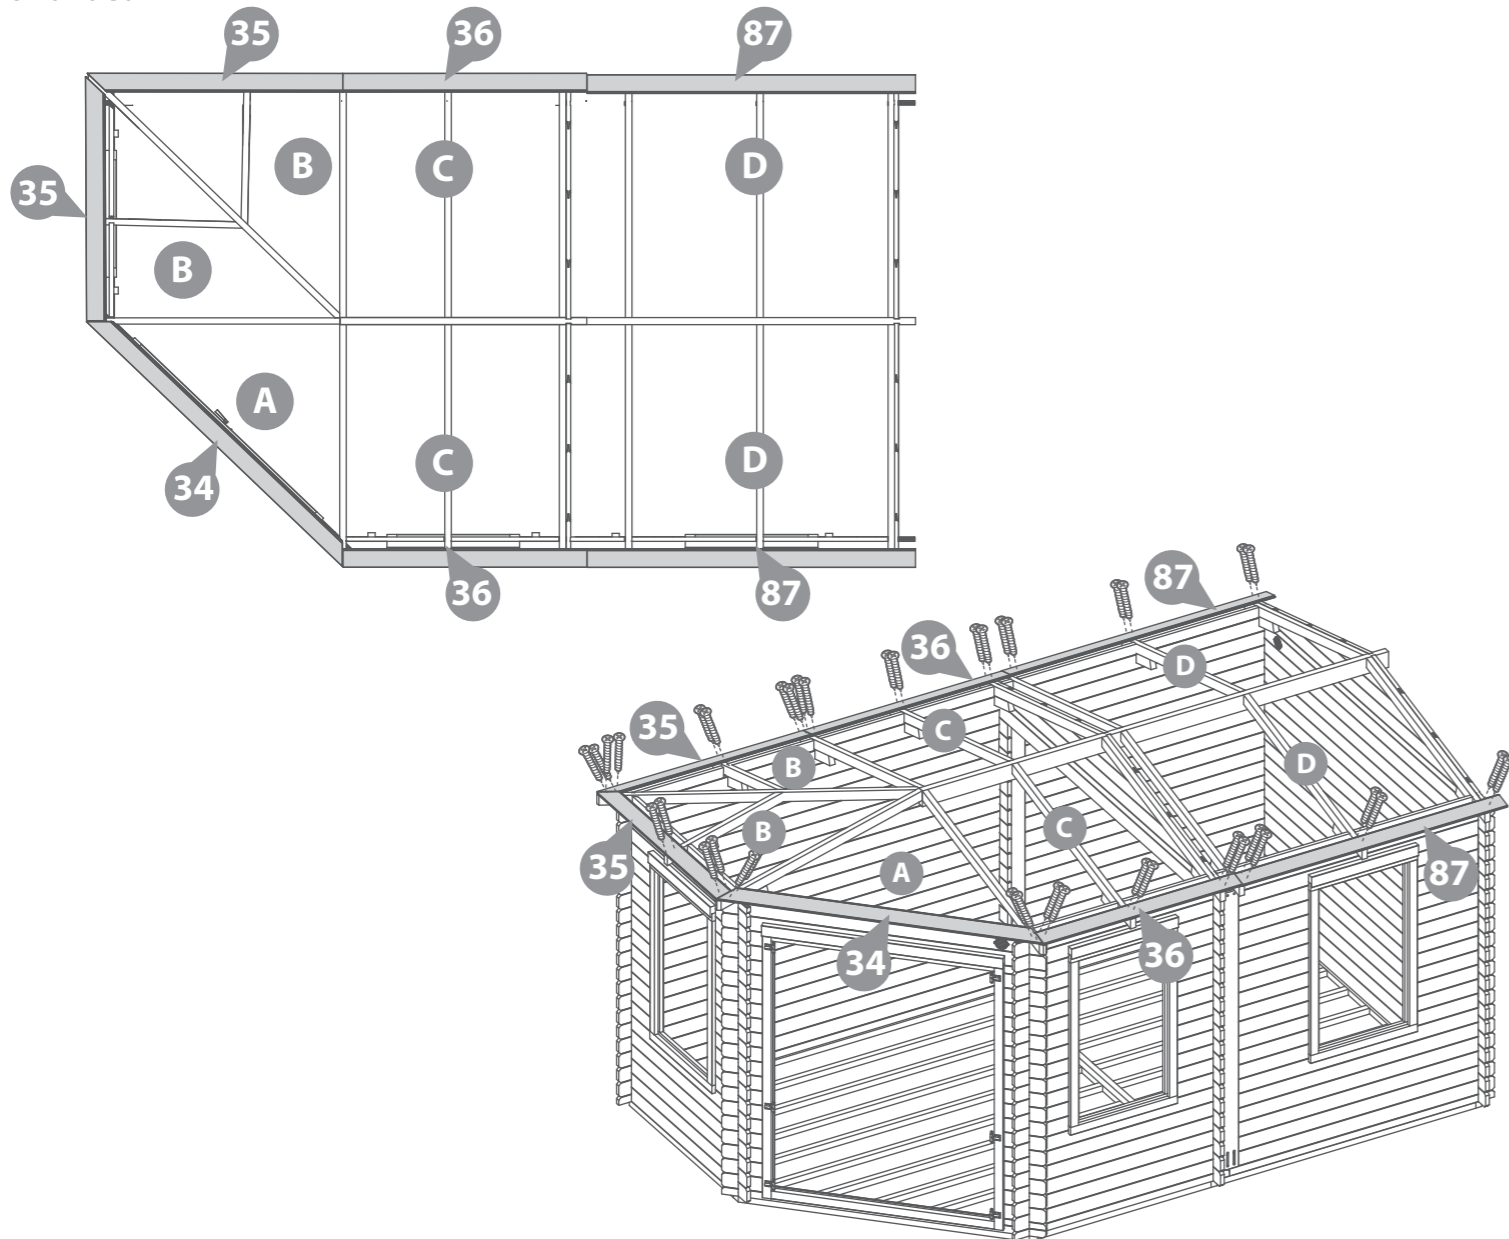

Right Handed

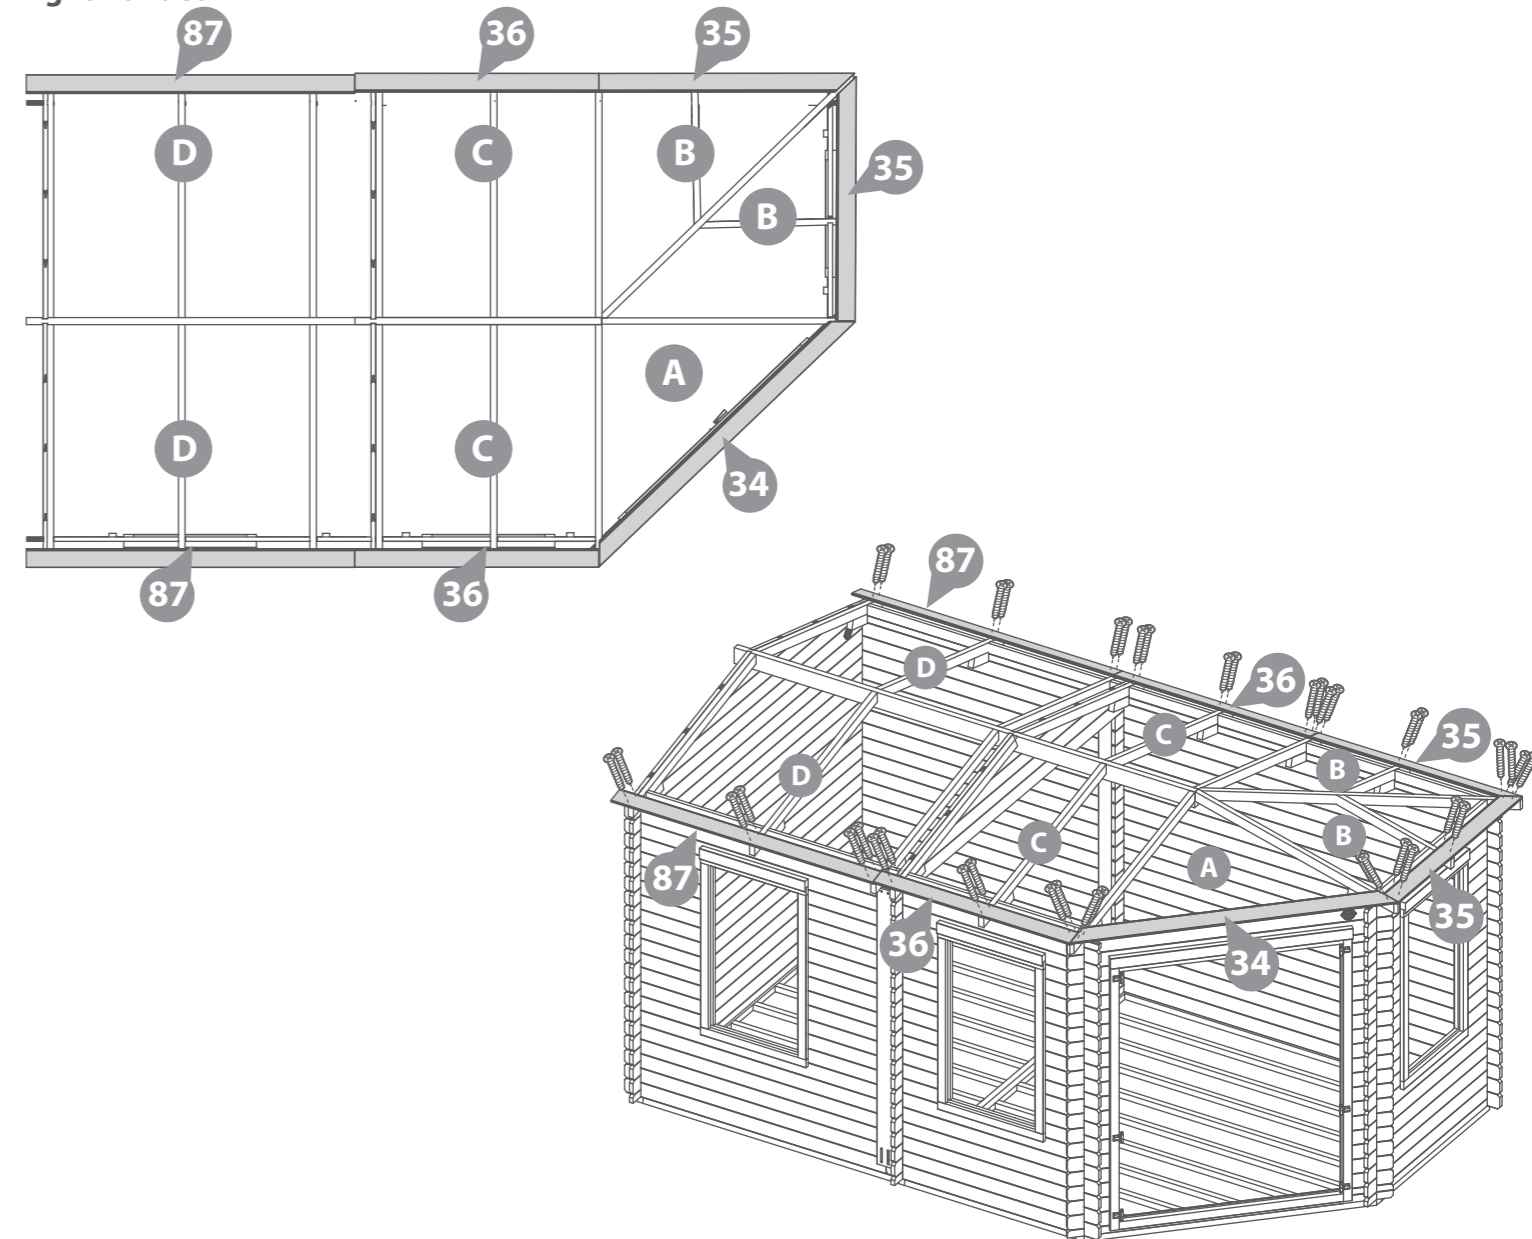

Step 36

- Parts needed - No. 34 QTY 1 Pack A**
No. 35 QTY 2 Pack B
No. 36 QTY 2 Pack C
No. 87 QTY 2 Pack D
No. 55 QTY 10

***HINT: keep the individual roof board packs together to avoid mixing them up.**

Continue arranging the Roof Board Packs (**No. 34, 35, 36 & 87**) onto the roof assembly, working around the structure, building up each layer of roof boards one by one.

To ensure the roof boards are not laid too close together, use the spacers (**No.55**) provided to create a 2mm gap. Adjusting the spacing between the boards allows the wood to swell in damp weather.

Once you are happy with the fit of the roof boards, fix the 2nd, 3rd & 4th boards into place using 40mm screws, ensuring the screws fix through the roof board into the truss below.



Repeat this so you have four boards screwed down in total on each of the sides and three on the front.

116x40mm Screws


Important: Pre-drill before fixing screws.



Left Handed

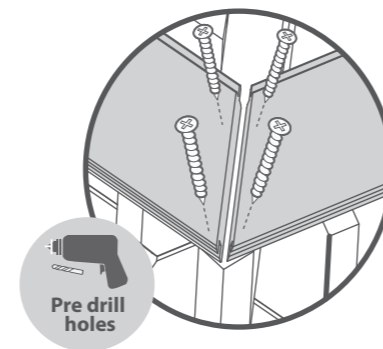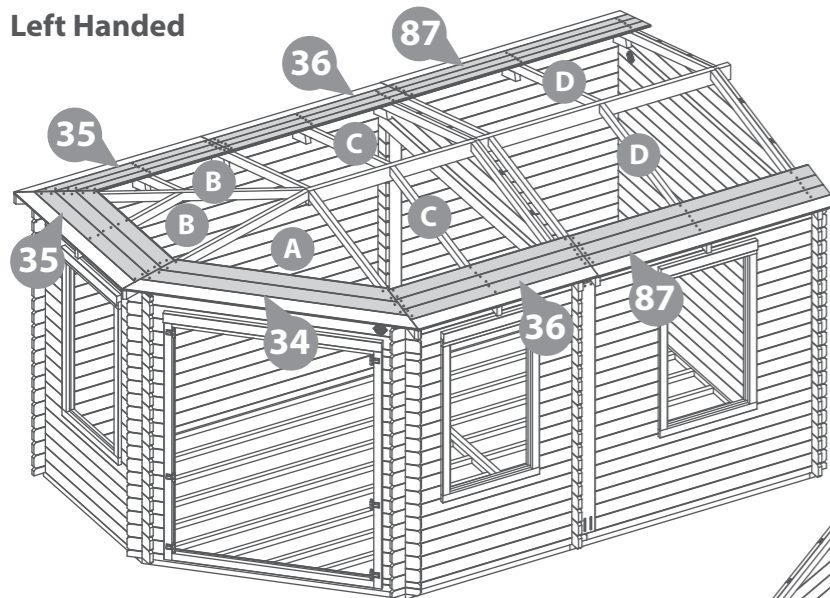

Right Handed

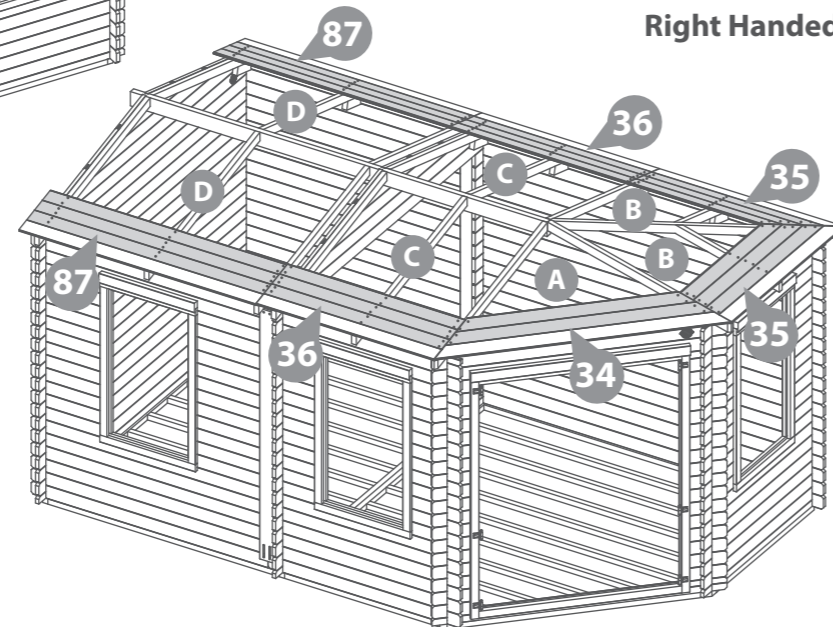

Step 37

- Parts needed - No. 34 QTY 1 Pack A**
No. 35 QTY 2 Pack B
No. 36 QTY 2 Pack C
No. 87 QTY 2 Pack D
No. 55 QTY 10

***HINT: keep the individual roof board packs together to avoid mixing them up.**

Continue arranging the Roof Board Packs (**No. 34, 35, 36 & 87**) onto the roof assembly, working around the structure, building up each layer of roof boards one by one.


To ensure the roof boards are not laid too close together, use the spacers (**No.55**) provided to create a 2mm gap. Adjusting the spacing between the boards allows the wood to swell in damp weather.

Once you are happy with the fit of the roof boards, fix the 5th, 6th & 7th boards into place using 40mm screws, ensuring the screws fix through the roof board into the truss below.



Repeat this so you have seven boards high screwed down in total on each of the sides and five on the front.

116x40mm Screws


Important: Pre-drill before fixing screws.



Left Handed

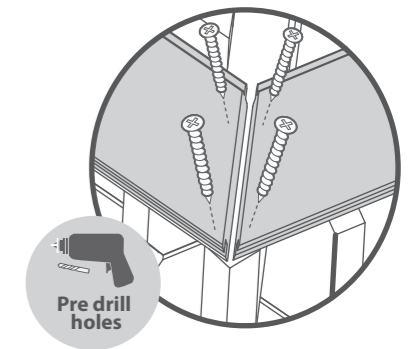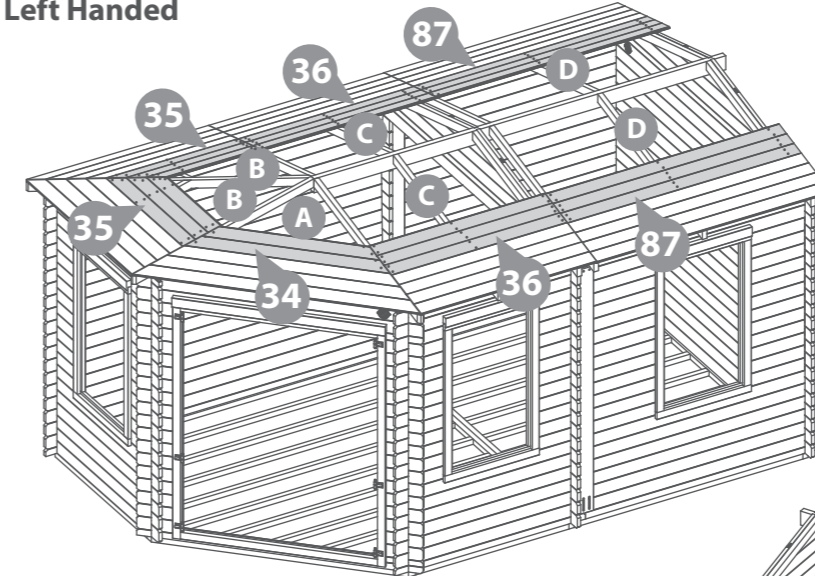

Right Handed

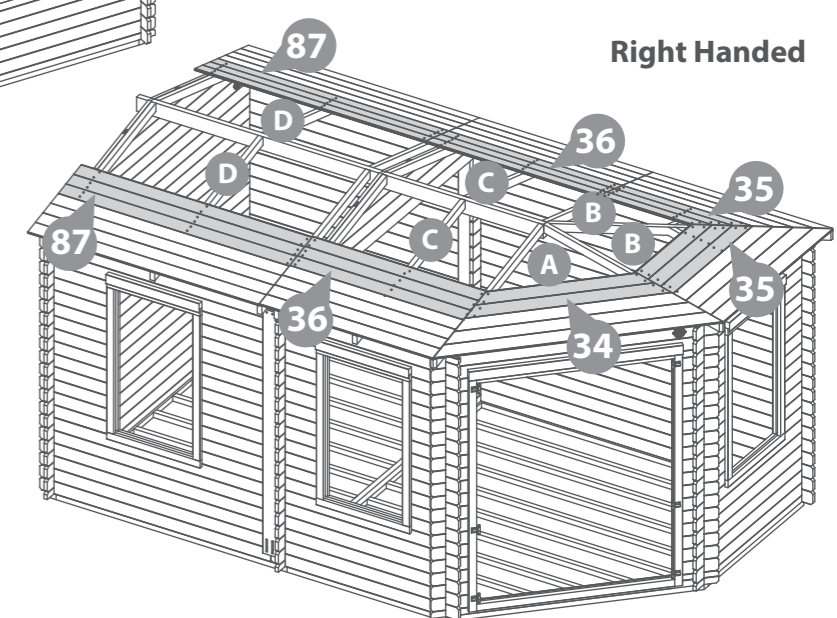

Step 38

- Parts needed - No. 34 QTY 1 Pack A**
No. 35 QTY 2 Pack B
No. 36 QTY 2 Pack C
No. 87 QTY 2 Pack D
No. 55 QTY 10

***HINT: keep the individual roof board packs together to avoid mixing them up.**

Continue arranging the Roof Board Packs (**No. 34, 35, 36 & 87**) onto the roof assembly, working around the structure, building up each layer of roof boards one by one.


To ensure the roof boards are not laid too close together, use the spacers (**No.55**) provided to create a 2mm gap. Adjusting the spacing between the boards allows the wood to swell in damp weather.

Once you are happy with the fit of the roof boards, fix the 8th, 9th & 10th boards into place using 40mm screws, ensuring the screws fix through the roof board into the truss below.

Repeat this so you have 10 boards high screwed down in total on each of the sides and seven on the front.

104x40mm Screws



Important: Pre-drill before fixing screws.



Drill / Pre drill.


40mm screw

Left Handed

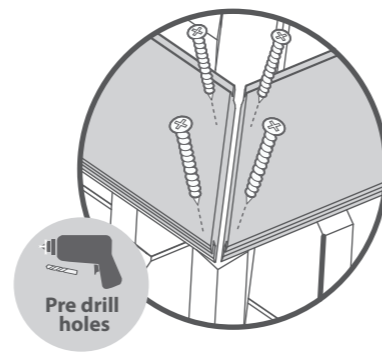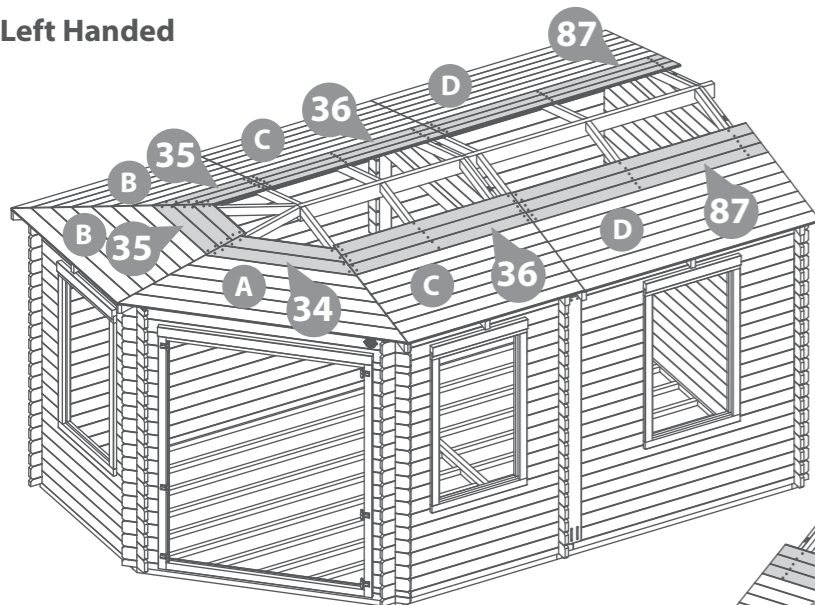

Pre drill holes

Right Handed

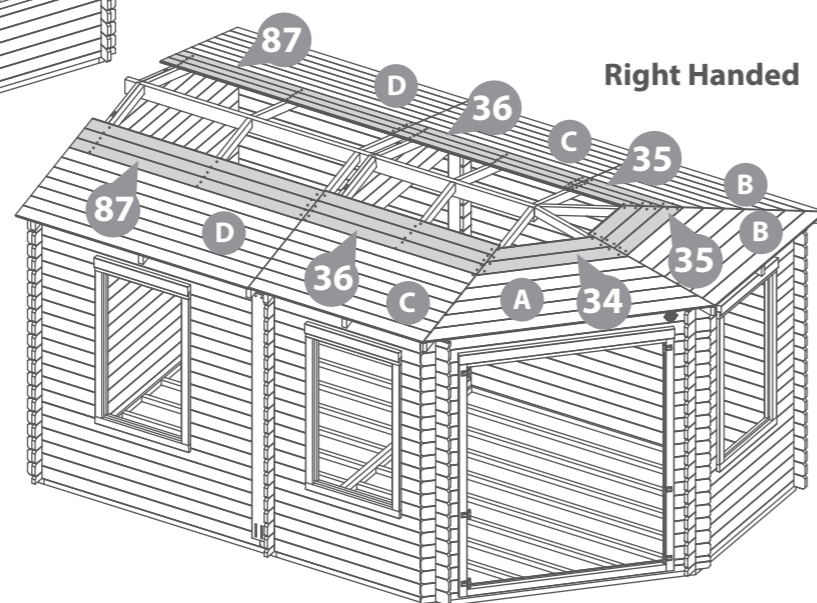

Step 39

- Parts needed - No. 34 QTY 1 Pack A**
No. 35 QTY 2 Pack B
No. 36 QTY 2 Pack C
No. 87 QTY 2 Pack D
No. 55 QTY 10

***HINT: keep the individual roof board packs together to avoid mixing them up.**

Continue arranging the Roof Board Packs (**No. 34, 35, 36 & 87**) onto the roof assembly, working around the structure, building up each layer of roof boards one by one. Use the spacers (**No.55**) provided to create a 2mm gap.

The last two boards from Pack C & D (**No. 36 & 87**) will overhang at the top. Using a pencil and a straight edge, mark out the excess with a line as a guide. Saw along the mark, remove the excess and place the cut down boards back onto the roof.

Once you are happy with the fit of the roof boards, fix the remaining boards into place using 40mm screws, ensuring the screws fix through the roof board into the truss below.

Repeat this so you have the rest of the boards high screwed down on each of the 7 sides.

140x40mm Screws

Important: Pre-drill before fixing screws.





Saw.


Drill / Pre drill.

40mm screw


Left Handed

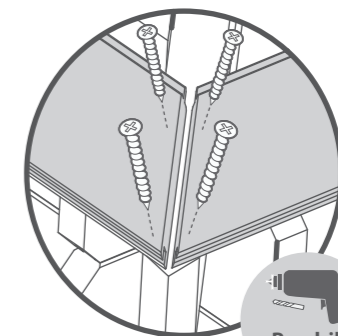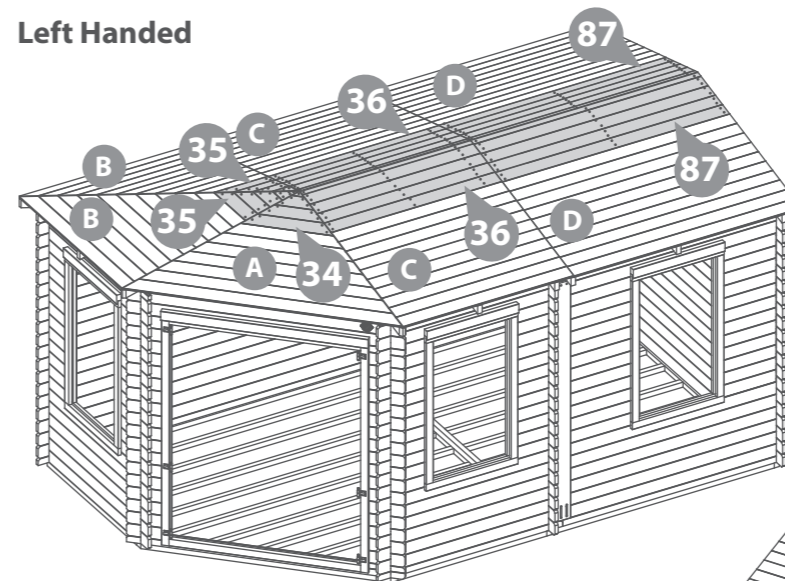

Pre drill holes

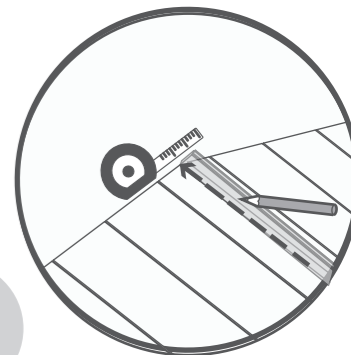

Right Handed

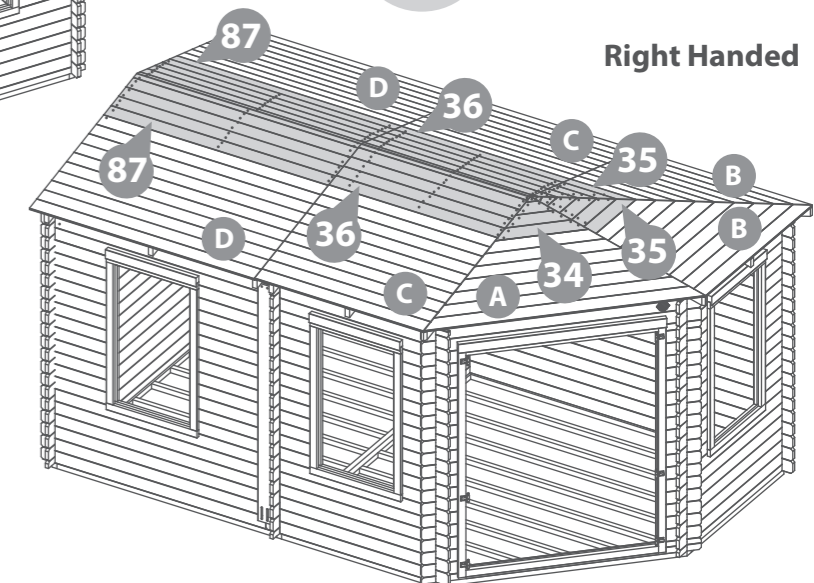

Step 40
Parts Needed - No. 68 QTY 3



Once the Roof is secured, open the window hinges and re-position the Window (**No. 68**) onto the hinges (as previously done in step 15) and fix in place using the same 3x30mm screws per hinge.

Ensure the window is able to open and close freely without getting stuck on the frame.

Use this method to fix all three windows into the frames.

****Please note:** This image is for illustrative purposes and may differ from the assembly you have constructed, however the process of fitting the windows is the same.

Important: Pre-drill before fixing screws.

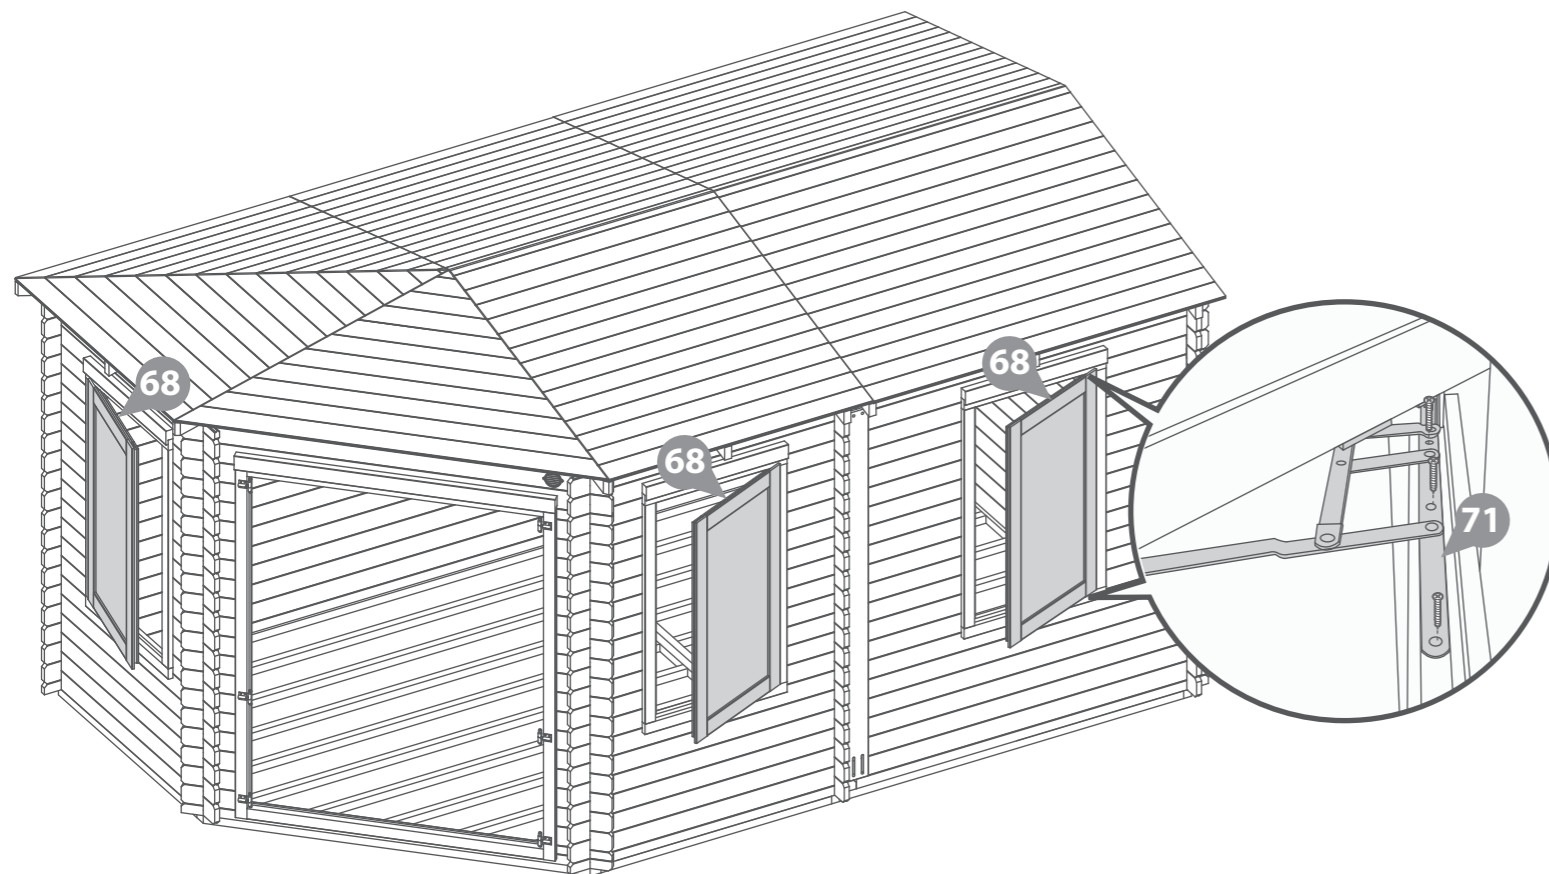

Step 41
Parts Needed - No. 72 QTY 3


With the window (**No.68**) shut tight, from the inside locate the Window Handle (**No.72**) onto the window and the window casement pin onto the inside of the window frame, as shown.

Ensuring the two parts locate together and shut correctly, fix the handle in place using 2x30mm screws, and secure the pin in place using 2x30mm screws.


Check that when locked, the window is as tight to the frame as possible. This will ensure a tight seal when the window is shut.

Use this method to locate and fix a handle to all three windows.

12x30mm screws.
Important: Pre-drill before fixing screws.



Internal view of window

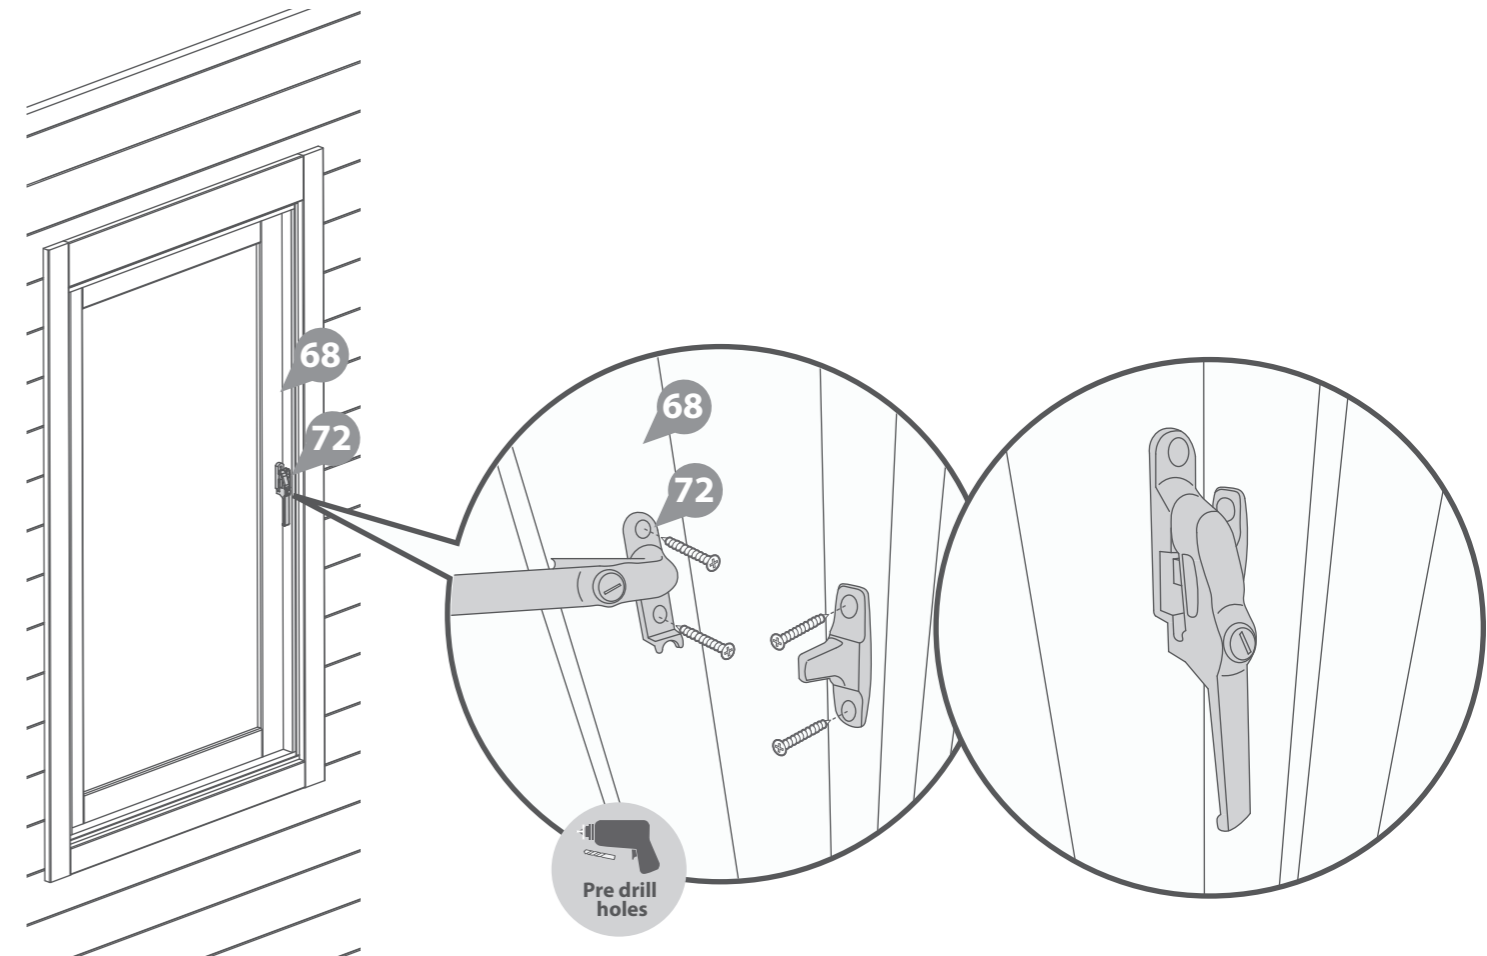


Step 42

Lift each Door onto the already existing hooks on the door frame, ensuring the hook and bands connect.

Tip: The adjustable hinges on the frames are loose and tend to spin when knocked. To aid in locating your Doors back onto the hinges, tape the loose hinges to the door frame to temporarily hold them in place.

***Some adjustment may be required to align properly. To adjust and align your Doors:**

1. Lift up the Doors to separate the two parts of the hinge.
2. Turn the rotating barrel (No. 64a) in / out to move the position of the Doors either in or away from each other.
3. You can then place the Door(s) back on to the hinge and check whether they require more / less adjustments, if further adjustments are required repeat number 2.

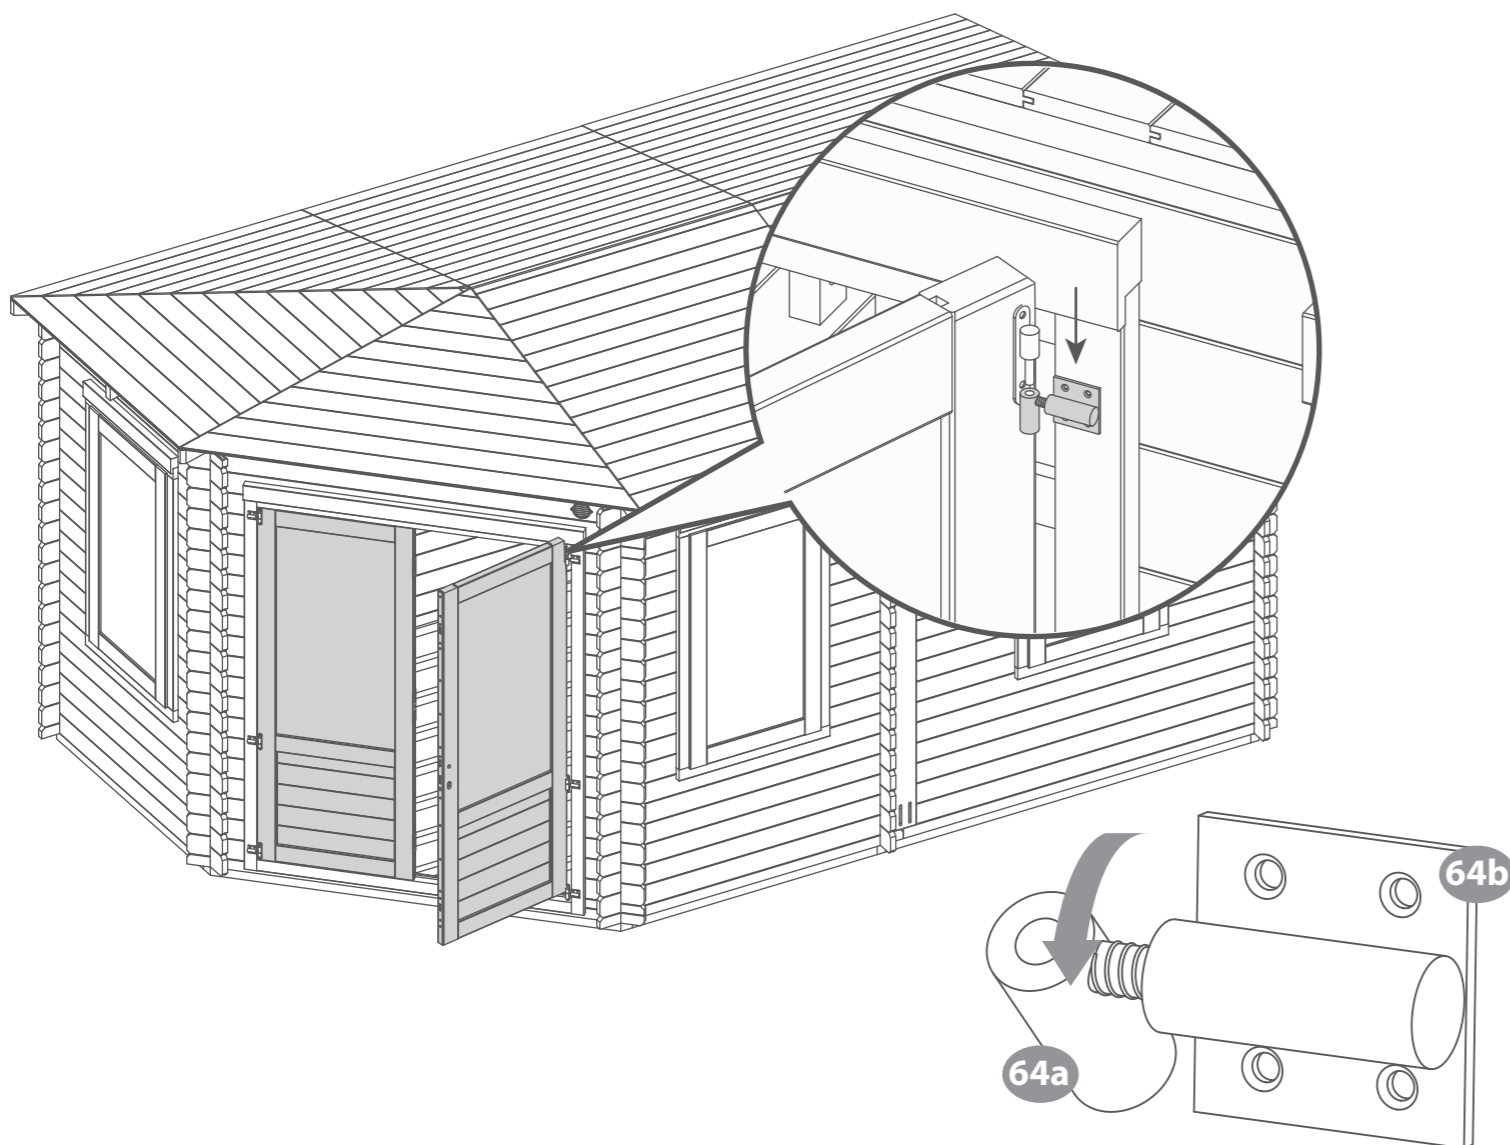

Adjusting the door hinges

Step 43


Parts Needed - No. 38 QTY 1

Open the Master Door (No. 56) and locate the Cylinder Lock (No. 66) into the lock shaped hole in the Central Lock. Ensure the Cylinder is positioned centrally in the door stile, as shown.



Drill / Pre drill.

Fix the Cylinder lock in place using the screw provided.

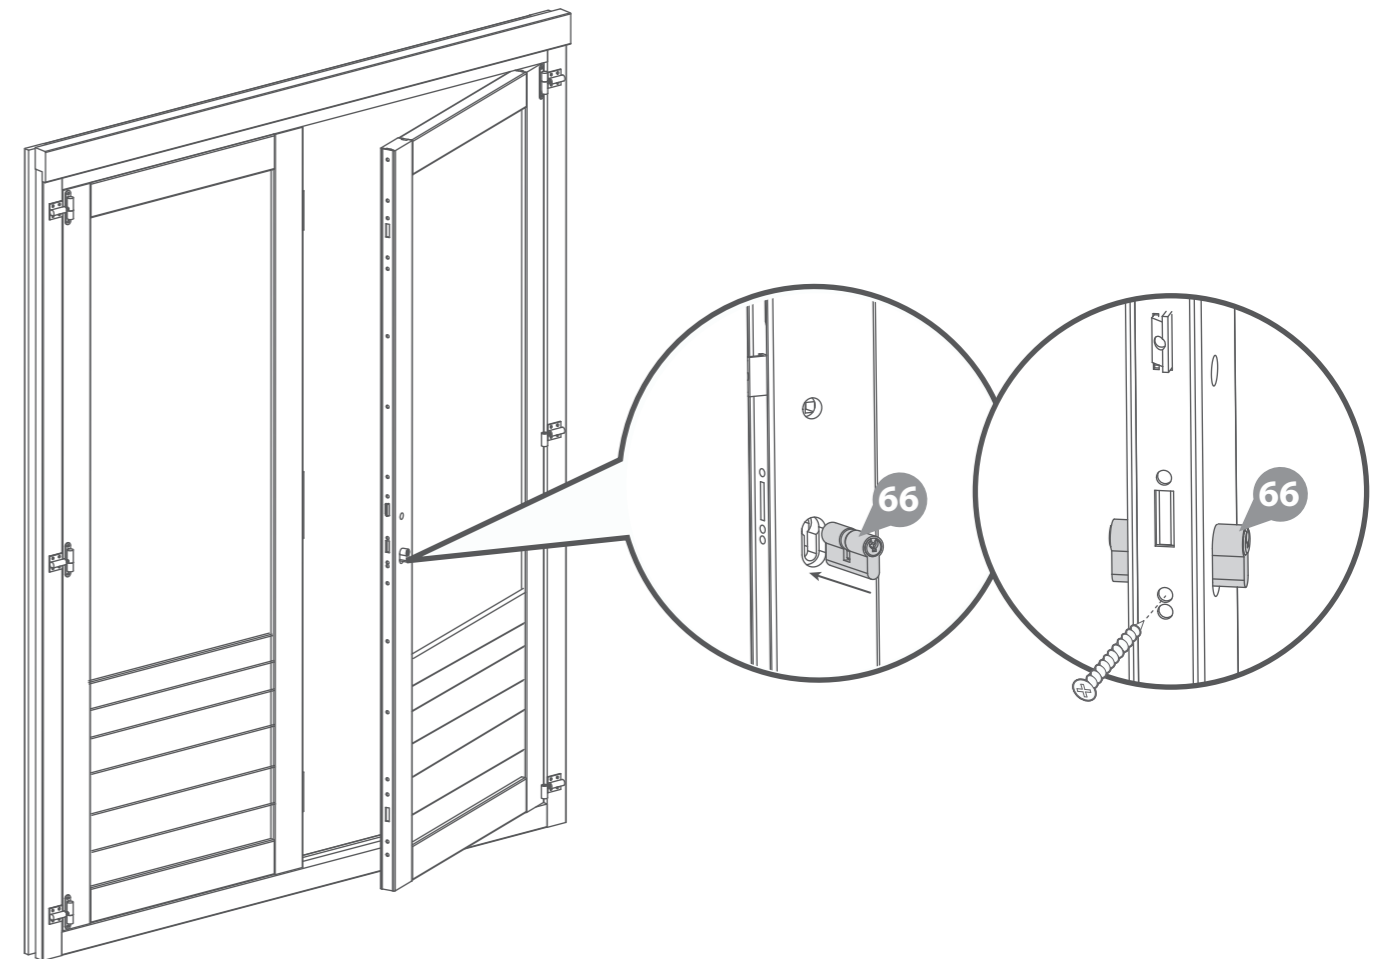

Step 44
Parts Needed - No. 65 QTY 1

From the Handle set (No. 65) position the Metal bar through the central lock and connect one handle onto either side, as shown. Ensure the handle with the screw holes sits on the inside of the Master door.

Fix the Handles in place using the two screws provided in the set.

Ensure the top and bottom Hook bolts work correctly and lock into the secondary door by lifting the handles. If not, your hinges may need adjusting, please refer to step 42 for a guide. Also make sure the cylinder lock locates properly into the secondary door when locked using the key, if not, then unscrew and re-adjust.

***Please note:** Once the components have been fitted, try closing doors to ensure the doors can be closed and the lock works. If your doors do need adjusting, please refer to step 42.

Important: Pre-drill before fixing screws.



Drill / Pre drill.

Step 45
Parts Needed - No. 62 QTY 1
No. 67 QTY 2

a Attach the Door Strip (No. 62) to the back of the Secondary Door (No. 57) using 4x40mm screws, as shown.

b Once fixed, place the Tower Bolts (No. 67) roughly into position at the top/bottom of the door strip. With a pencil mark around the bolt.

After marking the bolt onto the frame, drill a hole for the barrel bolt to locate into.

c Following the hole being drilled, place the tower bolts into position and secure using the screws provided.

4x40mm Screws



Important: Pre-drill before fixing screws.



Drill / Pre drill.



40mm screw

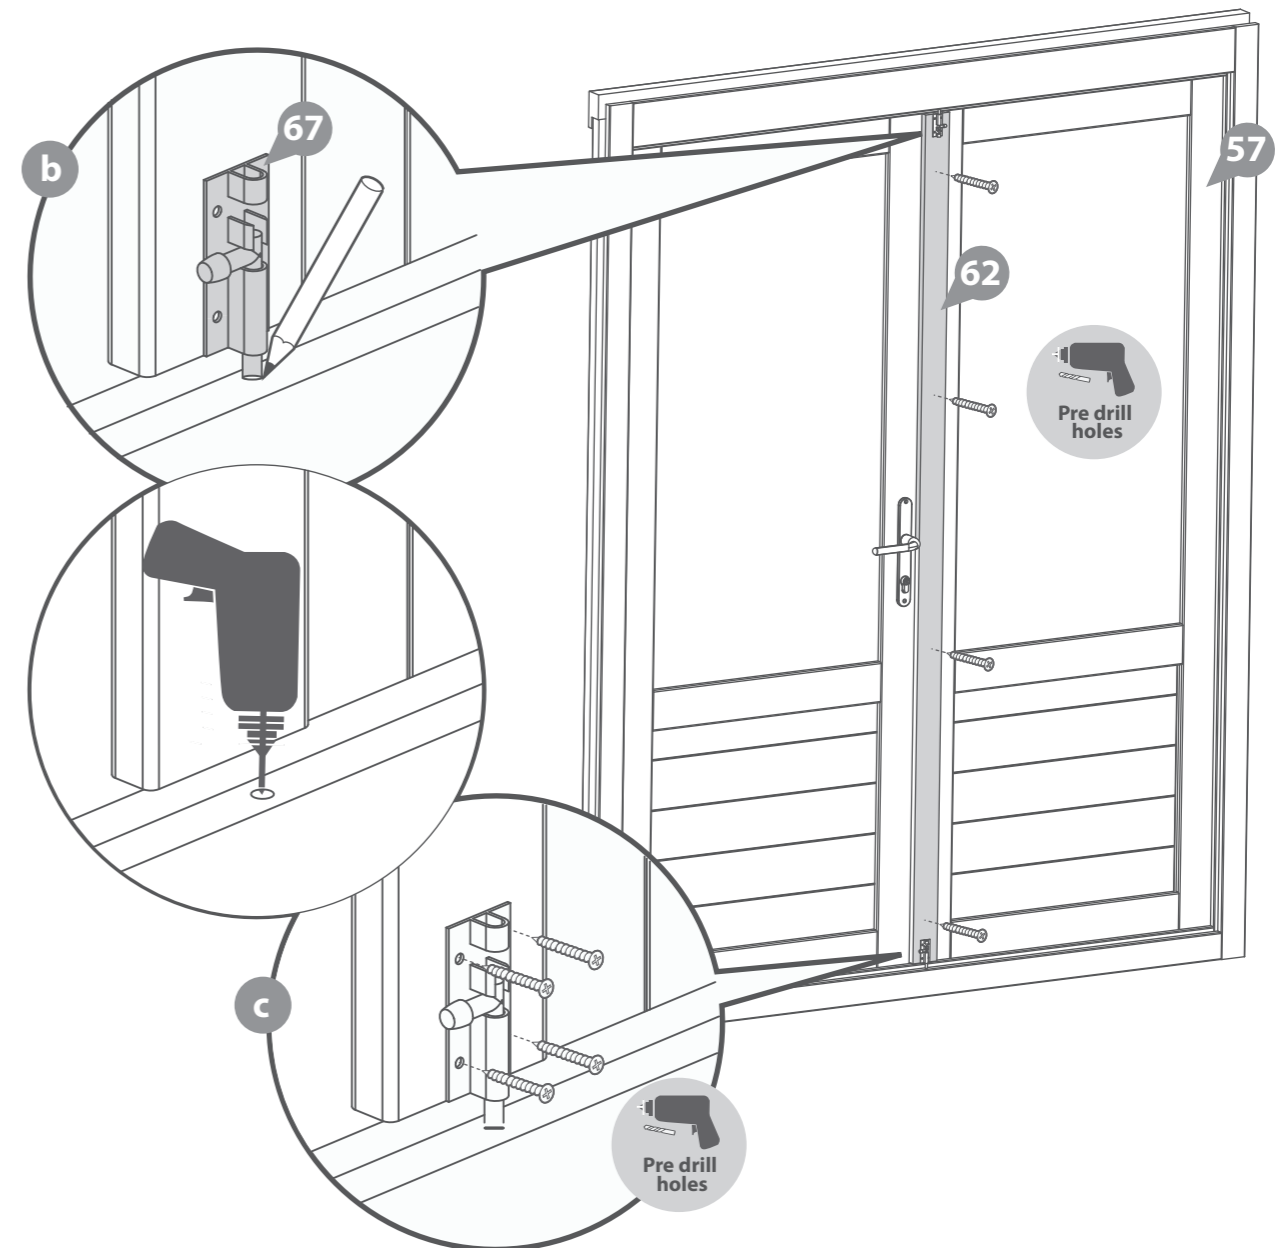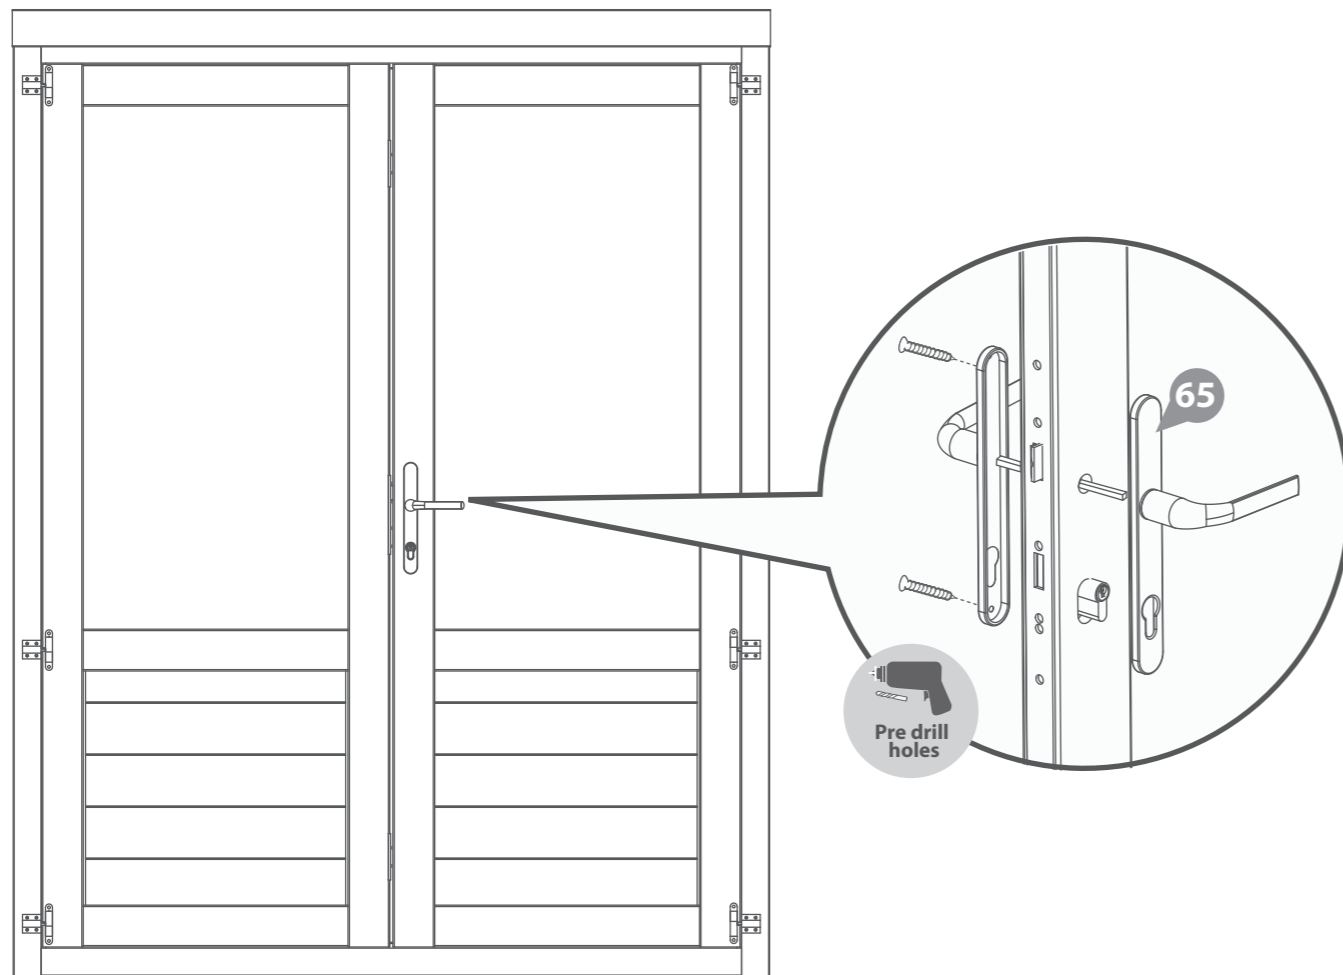

Step 46

**Parts Needed - No. 50 QTY 1
No. 86 QTY 19**

a Place the first floor board (**No. 50**) inside the building flush to the log board on one side. Continue adding the floor boards (**No. 50 & 86**) (*internally*) making sure to interlock each individual board.

***Do NOT secure the boards until the last board has been measured and cut.**

b Once a full board can no longer fit, measure the gap between the bottom of the tongue (*on the last board placed*) and the log board. Ensure to measure at multiple points along the board for added accuracy.


Using a straight edge, mark out the measurement onto the last floor board (**No. 86**), saw along the length and remove the excess. *Mark the final board 2mm under the measurement; This will allow the timber to expand and contract correctly.*

The floor boards either side of the central 'mini wall' will also need to be notched to fit. Measure around the protruding log boards as shown in the illustration and mark onto the floor boards. Once marked, cut into the floor boards to create the desired notch and place the boards back into position.

Once all the floor boards are in position, secure each board into position using 9x40mm screws per board.

*****Please Note:** *Ensure to screw through each of the floor boards into the floor bearers.*

405x40mm Screws
Important: *Pre-drill before fixing screws.*

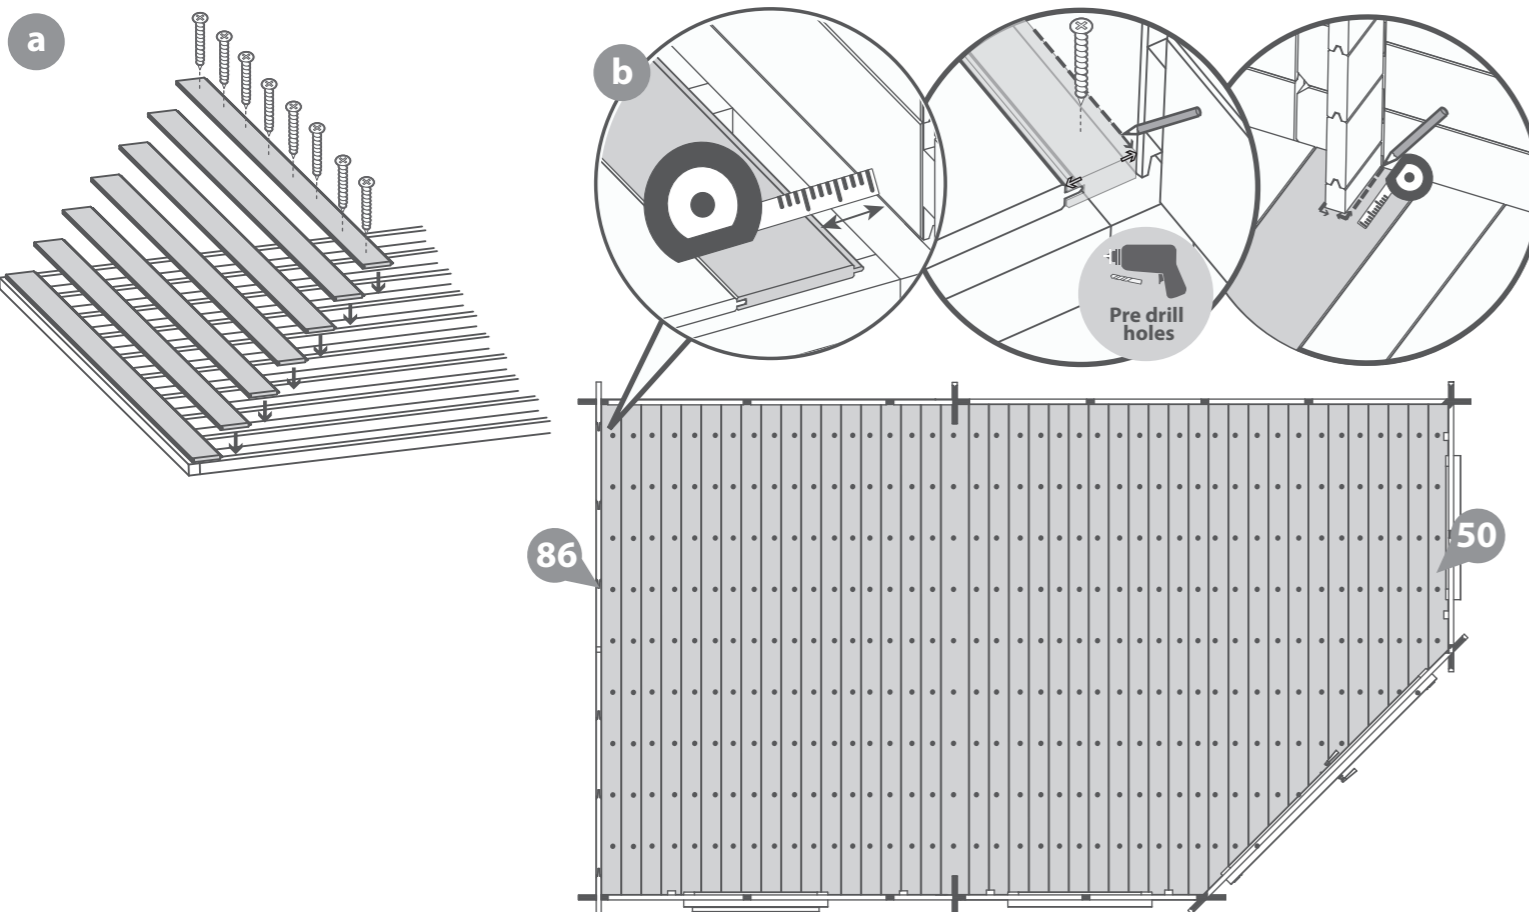

Step 47


Parts needed - No. 51 QTY 7

Inside the building place the closure trim (**No. 51**) against the boarding and align with the roof as shown in the illustration.

***Measure and cut the closure trims to fit the internal space.**

Once in position fix each trim into place by pre drilling a pilot hole and using 6x30mm screws per trim, equally spacing them along the face of the board.

42x30mm Screws
Important: *Pre-drill before fixing screws.*

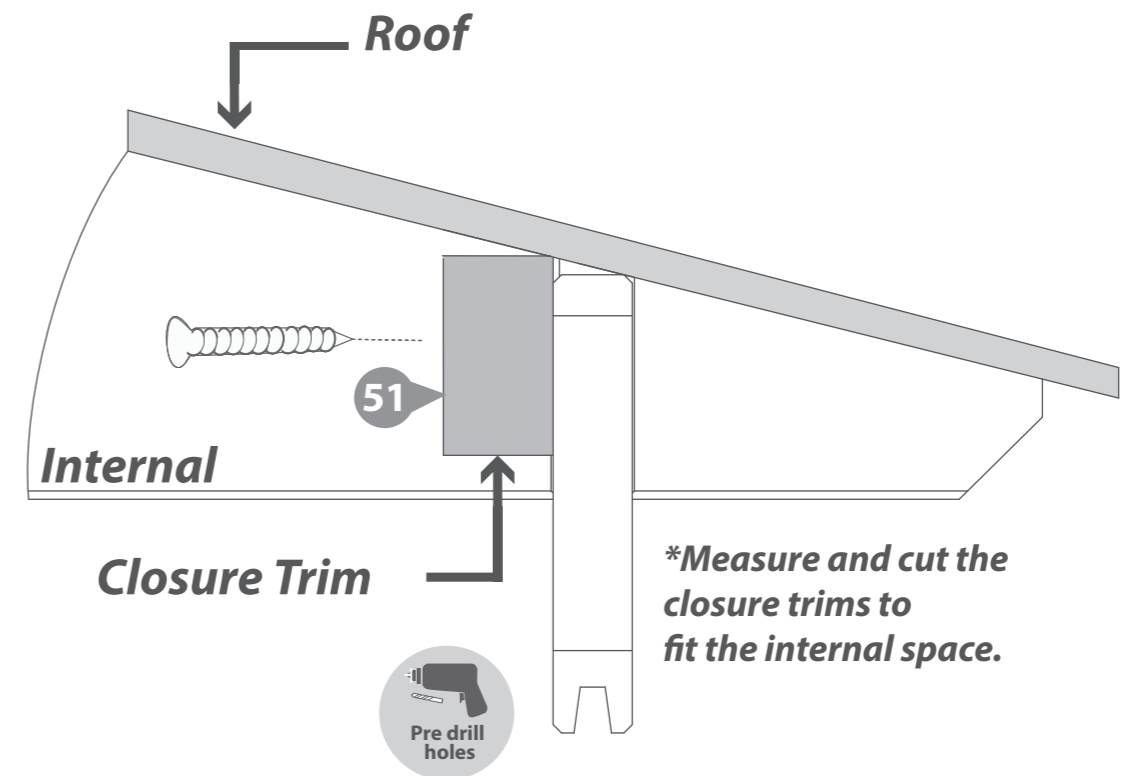

Step 48

Parts needed - No. 51 QTY 7

Once the floor has been laid, arrange the closure trim (**No. 51**) around the outside edge of the floor (**internally**), measure and cut down accordingly to best match the internal space.

Secure each trim section into place using 6x30mm screws spaced equally along the board as shown in the illustration.

***Do NOT fix the closure trim to the floor boards.**

42x30mm Screws


Important: Pre-drill before fixing screws.




Saw.



Drill / Pre drill.



30mm screw

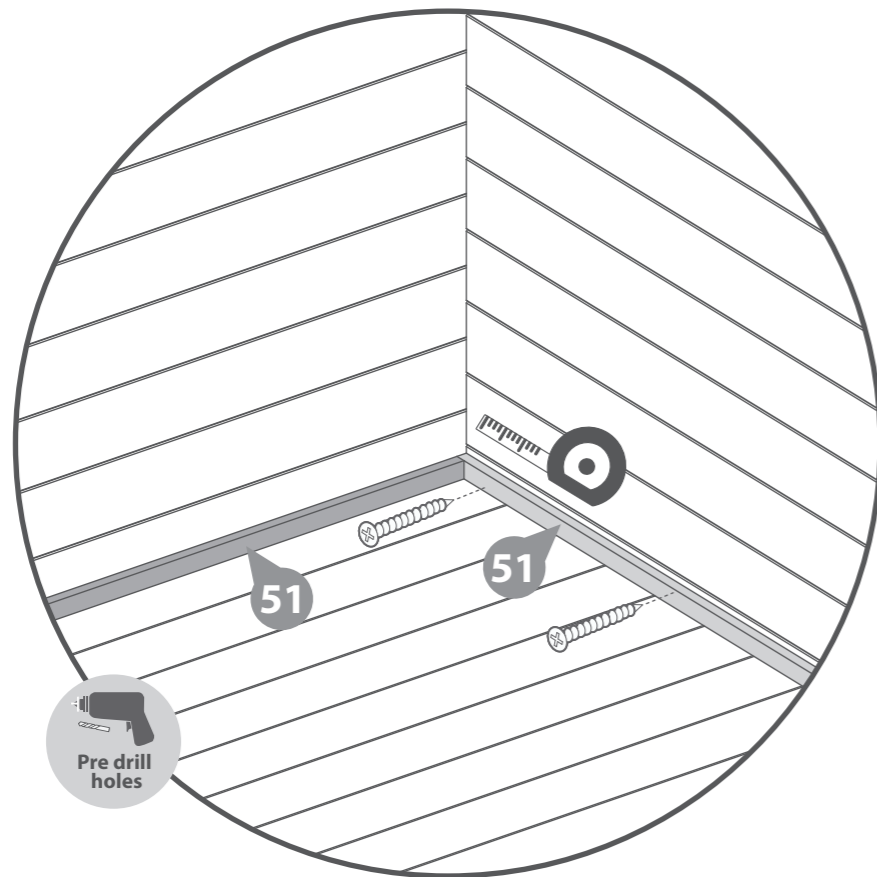

Step 49
Parts needed - No. 54

Measure and cut the felt (No.54) into eight sheets using the dimensions given below:

- 1 - 3600mm (L) x 1000mm (W)
- 2 - 2300mm (L) x 1000mm (W)
- 3 - 1660mm (L) x 1000mm (W)
- 4 - 5160mm (L) x 1000mm (W)
- 5 - 3600mm (L) x 1000mm (W)
- 6 - 820mm (L) x 1000mm (W)
- 7 - 700mm (L) x 1000mm (W)
- 8 - 4300mm (L) x 1000mm (W)



Lay the first piece of felt (1-3600mm (L) x 1000mm (W)) onto the roof as shown (1) and cut down to the individual shape of the roof.

Continue this method to lay and shape each piece of felt (2-8) in the order as shown.



Ensure each sheet overlaps by 5100m and that the felt overhangs the edge of the roof by at least 50mm on each side.

Secure the felt in place using felt tacks spaced out at 100mm intervals.



350 x Felt Tacks

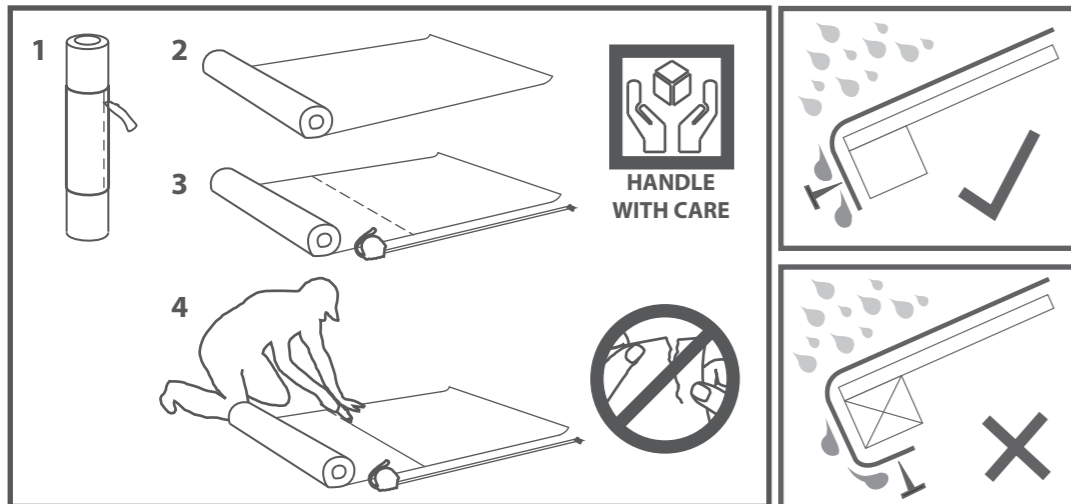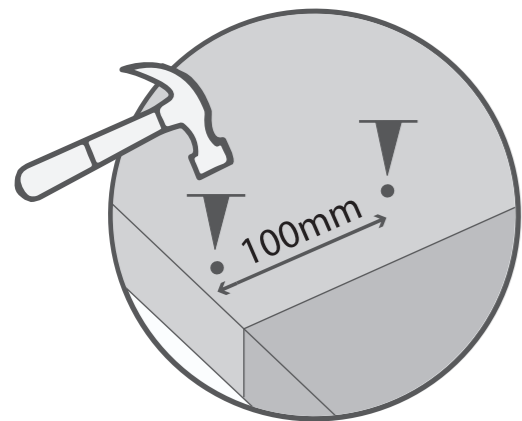

Left Handed

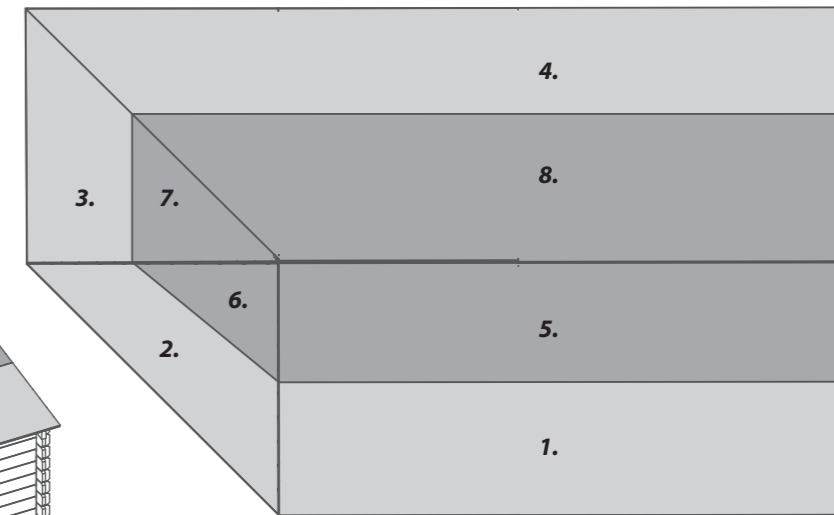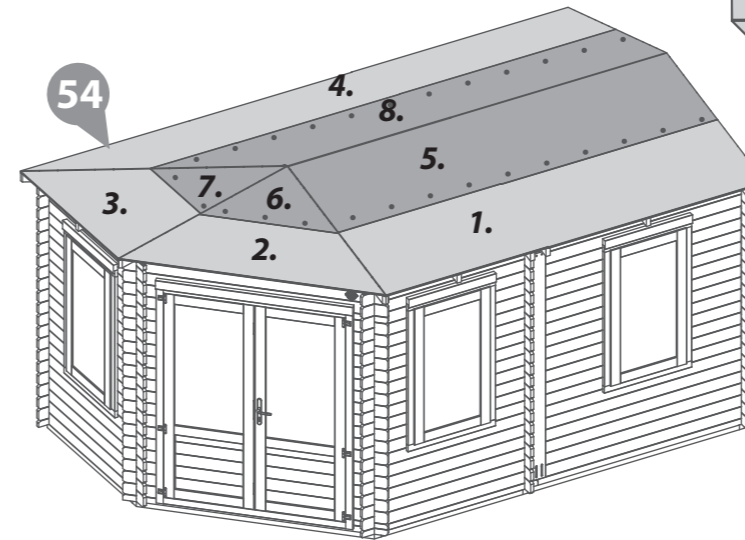

Right Handed

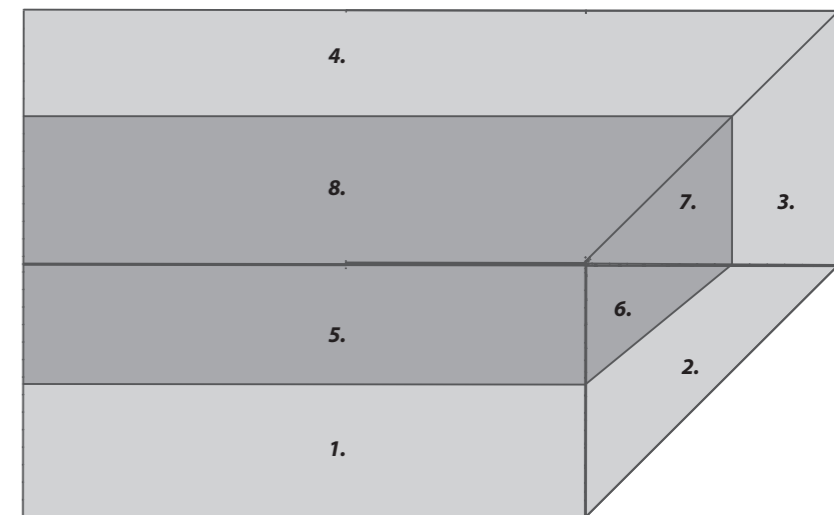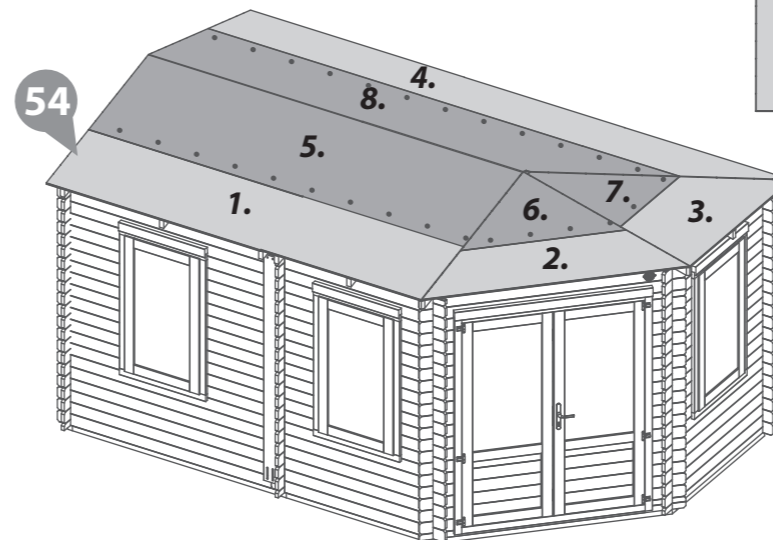

Step 50
Parts needed - No. 54

Measure and cut the remaining felt (No.54) into four strips using the dimensions given below:



- 1 - 3600mm (L) x 200mm (W)
- 2 - 2340mm (L) x 200mm (W)
- 3 - 1700mm (L) x 200mm (W)
- 4 - 1720mm (L) x 200mm (W)

Lay the first strip (1-3600mm (L) x 200mm (W)) onto the roof as shown (1), ensuring it is overlapping the previously placed sheets.



Continue to lay each of the felt strips (2-4) onto the roof in the order shown.

Secure along the outer edge of each felt section using felt tacks spaced out at 100mm intervals.



200 x Felt Tacks

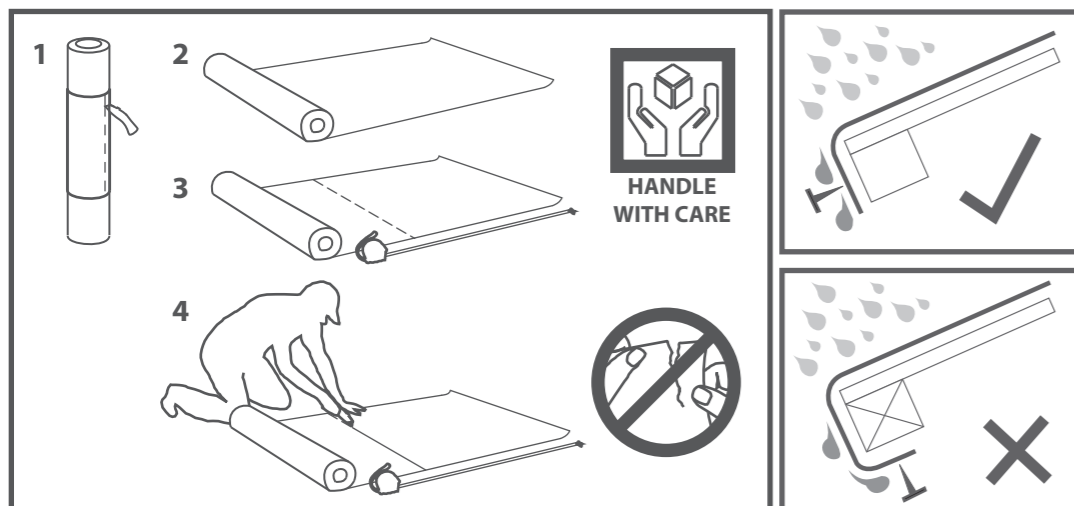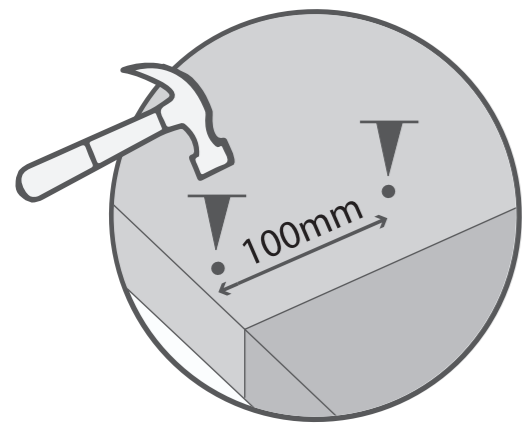

Left Handed

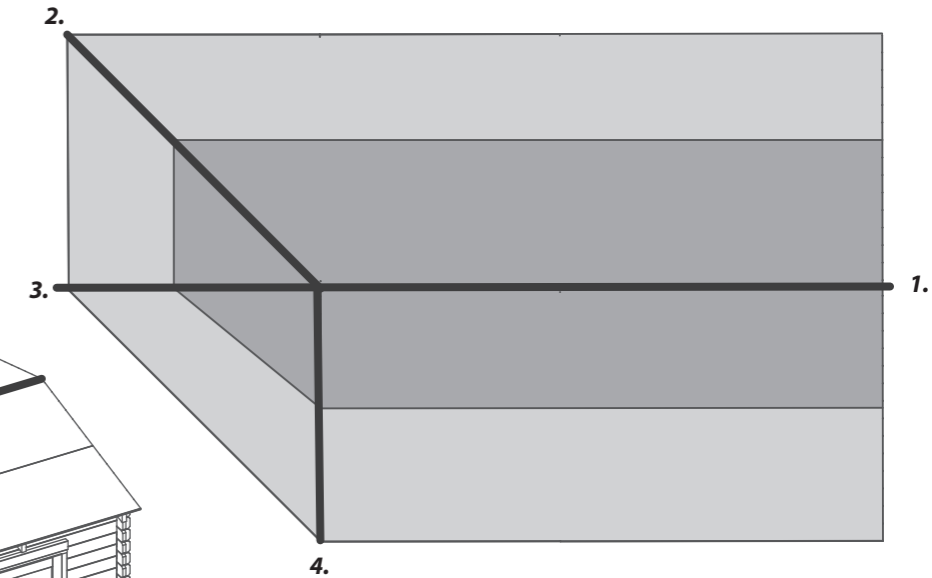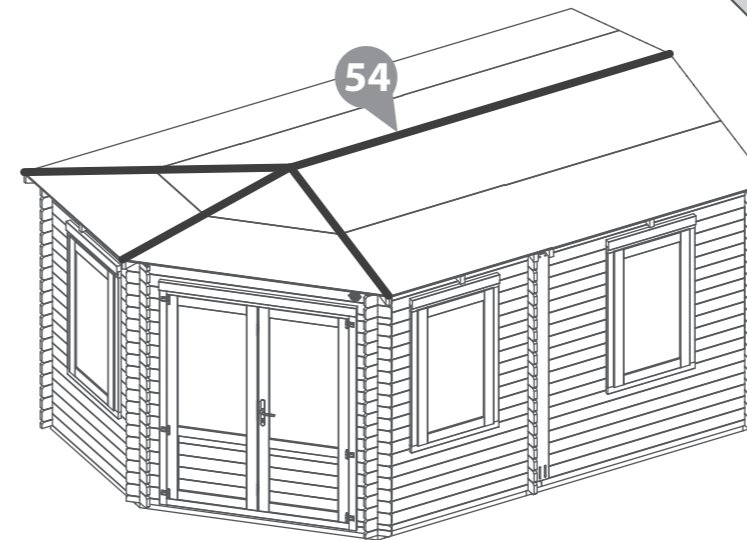

Right Handed

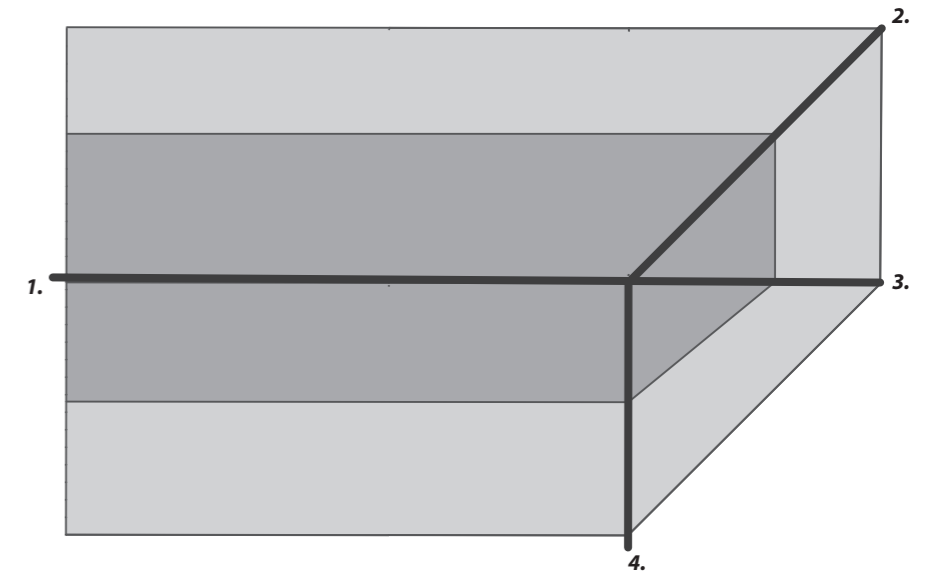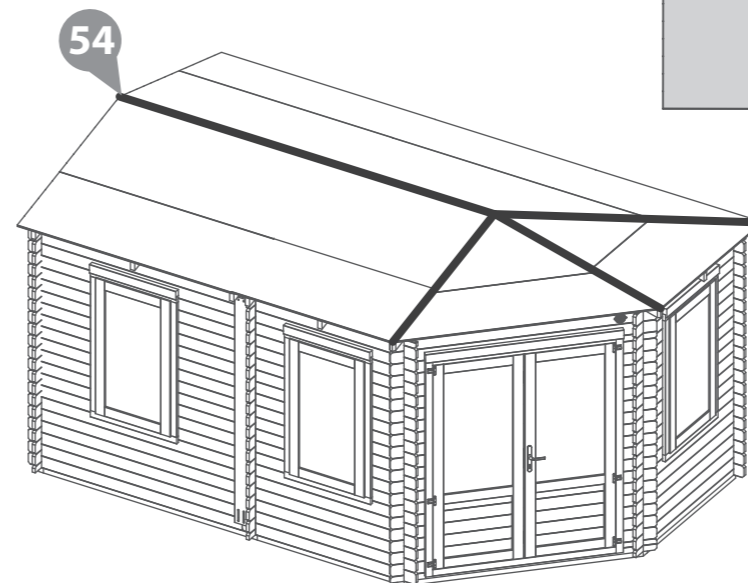

Step 51

- Parts Needed - No. 46 QTY 1**
No. 47 QTY 1
No. 48 QTY 4
No. 49 QTY 2

a Attach the Fascias (**No. 46, 48 & 49**) to the back sides of the log cabin (*ensuring to trap the felt in between the fascias*) securing (**No. 48**) in place using 6x40mm screws per Fascia, and (**No. 46 & 49**) using 8x40mm screws per Fascia, screwing through the Fascia into the Purlin, Roof Truss or Log board behind

Once in place mark the excess Fascia with a pencil and trim the Fascias to follow the shape of the building as shown in the illustration.


b Locate the Fascias (**No. 47 & 48**) to the front sides of the log cabin (*ensuring to trap the felt in between the fascias*) and secure (**No. 48**) in place using 6x40mm screws per fascia, and (**No. 47**) in place using 4x40mm screws, screwing through the Fascia in to the Roof Truss behind.

Once in place, repeat the above method to trim the fascias to follow the shape of the building.

Ensure the fascias sit level or lower than the felt to allow water to run off.

****Please note:** This image is for illustrative purposes and may differ from the assembly you have constructed, however the process of fitting the fascias is the same.

52x40mm Screws
Important: Pre-drill before fixing screws.

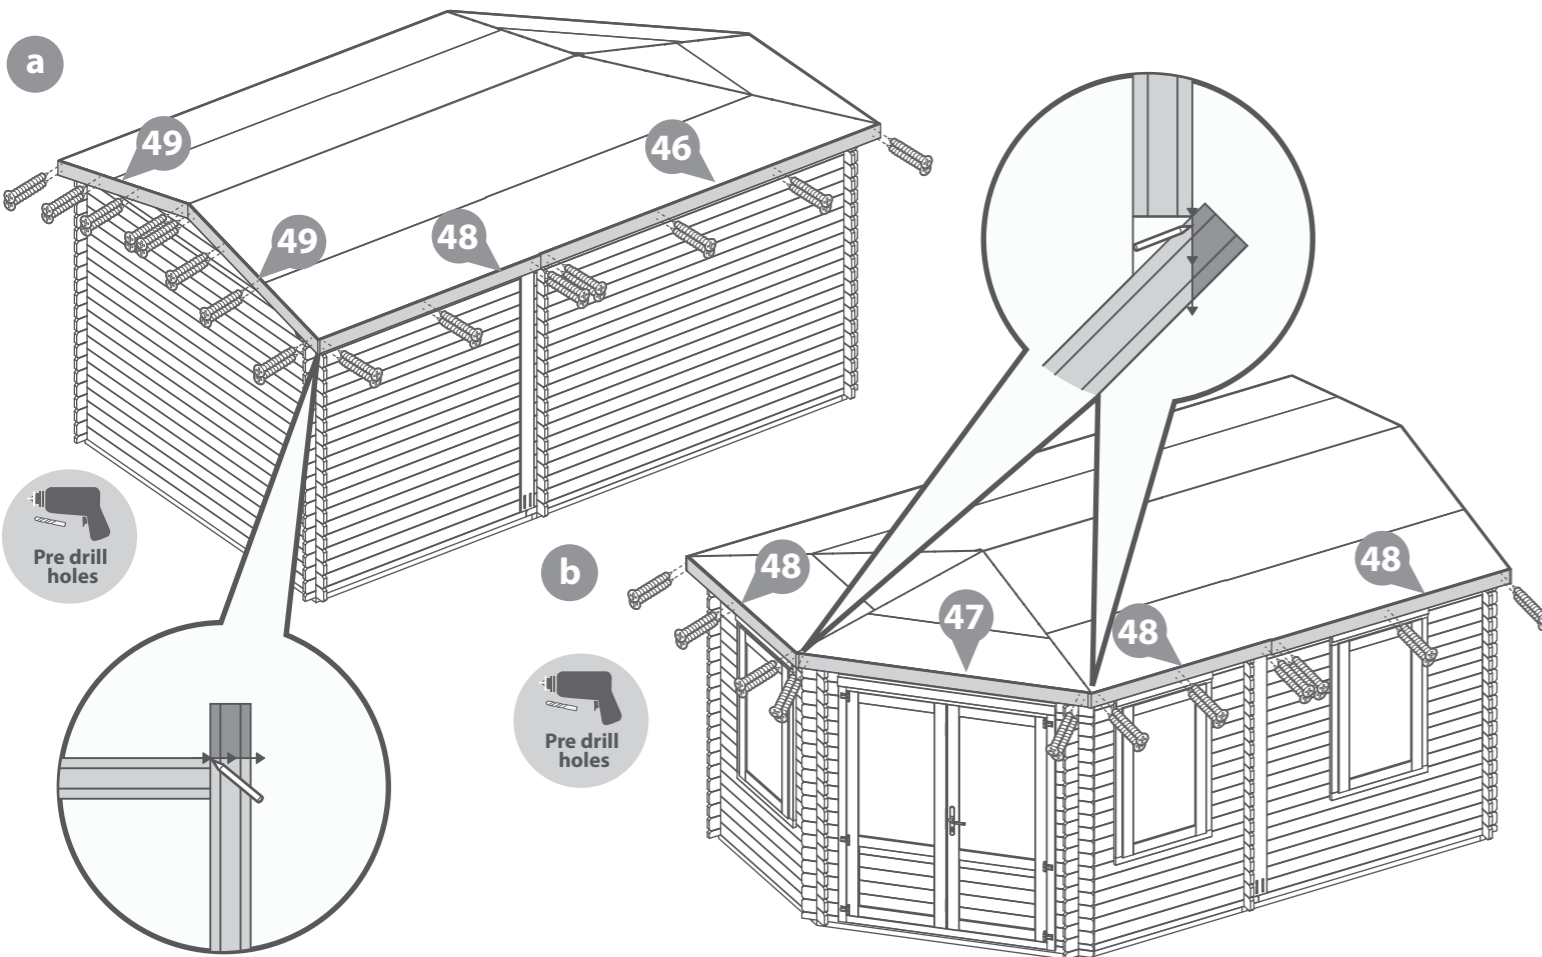

Step 52



- Parts Needed - No. 63 QTY 1**
No. 70 QTY 3

Attach the Rain Guards (**No. 70**) to the Window frames, ensuring to position the rain guards directly above the windows, flush to the underside of the top framing, as shown. Make sure the rain guards are positioned centrally. Fix in place using 3x70mm screws per rain guard.

Attach the Rain Guard (**No. 63**) to the Door frame, fixing in place onto the framing above the Door using 4x70mm screws.

****Please note:** This image is for illustrative purposes and may differ from the assembly you have constructed, however the process of fitting the rain guards is the same.

13x70mm Screws.
Important: Pre-drill before fixing screws.

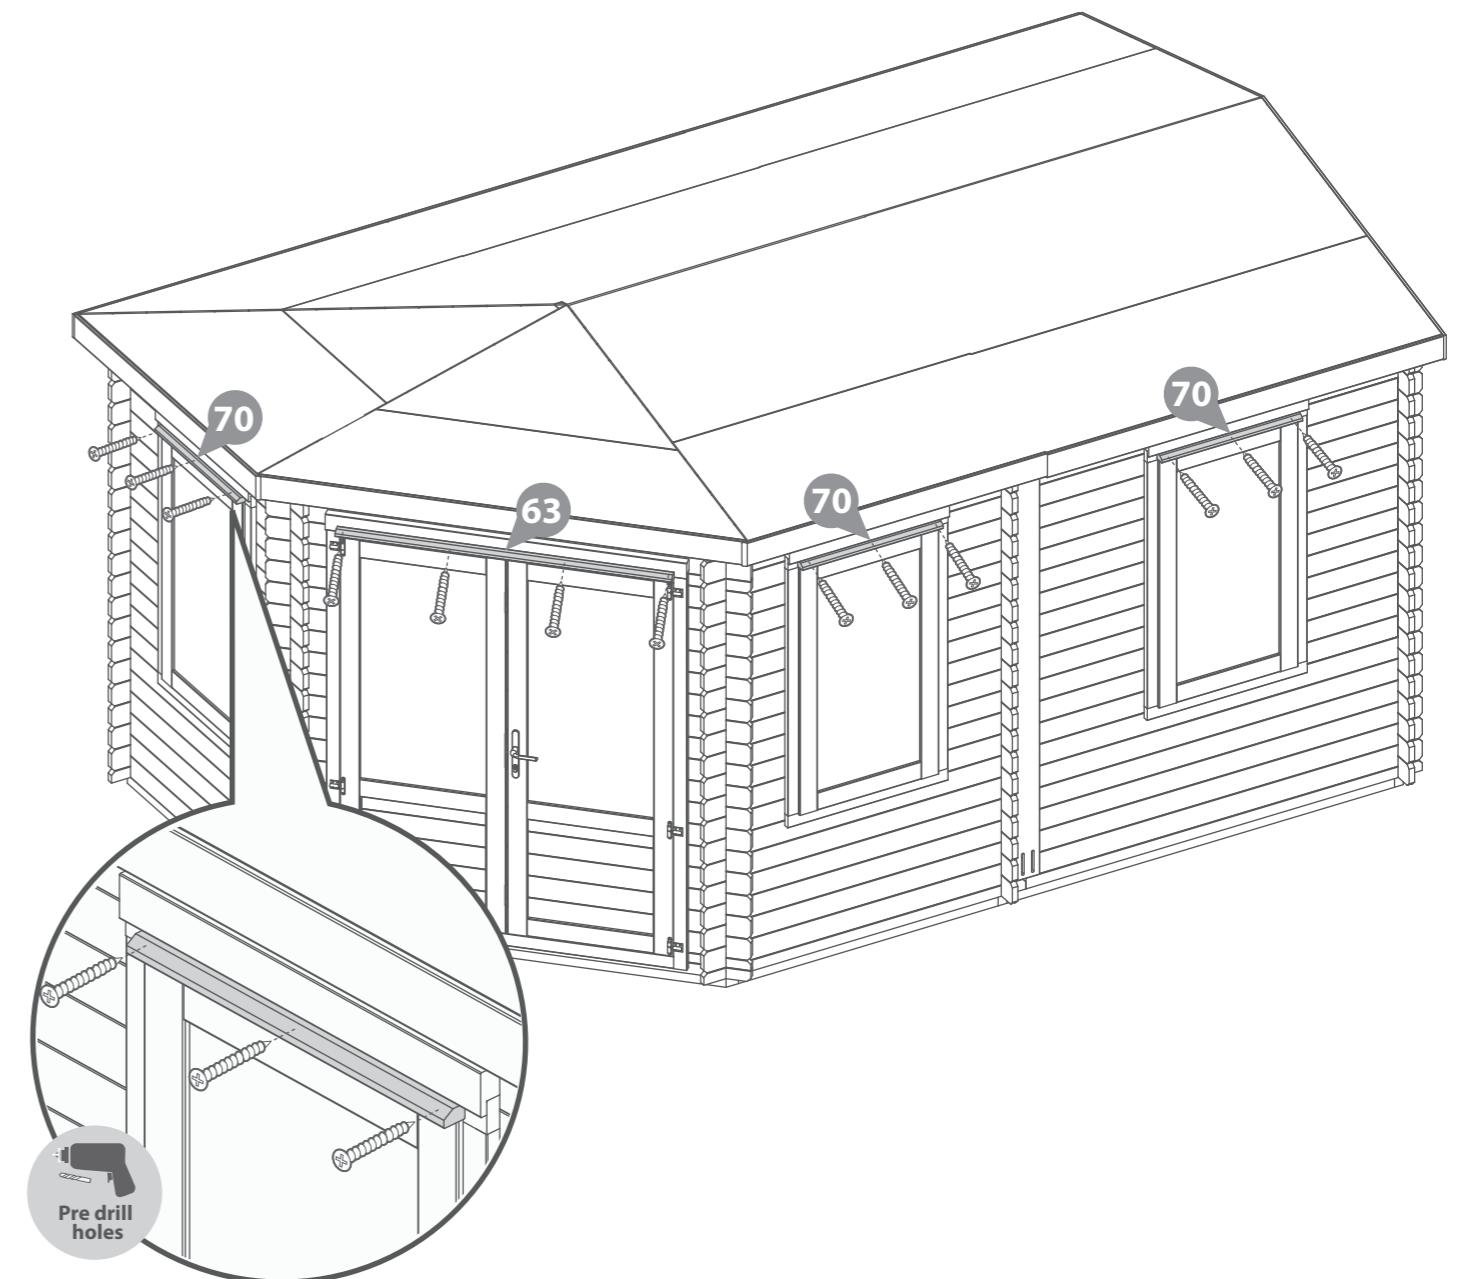

Step 53

Parts needed - No. 52 QTY 12

Arrange the storm braces (**No.52**) around the building (*internally*), placing two storm braces per wall.

***Ensure the storm braces are secured at the highest point possible on each side.**

Fix in place using 2x80mm bolts per brace, making sure the washer & nut are tightened from the outside of the building.

The storm braces will need to be altered during the buildings life as the moisture content within the log boards changes. The boards will expand during periods of high moisture (Winter) and shrink during periods of low moisture (Summer.)



****Storm braces are required to be adjusted during changes in humidity to allow the building to expand and contract. To do this, periodically loosen the bolts, adjust the storm brace position and re-tighten.**

*****Important: Ensure each bolt is tightened using a washer so as not to damage the log boards.***

***Please note:** This image is for illustrative purposes and may differ from the assembly you have constructed, however the process of fitting the storm braces is the same.

24x80mm Bolt Sets

Important: Pre-drill before fixing screws.

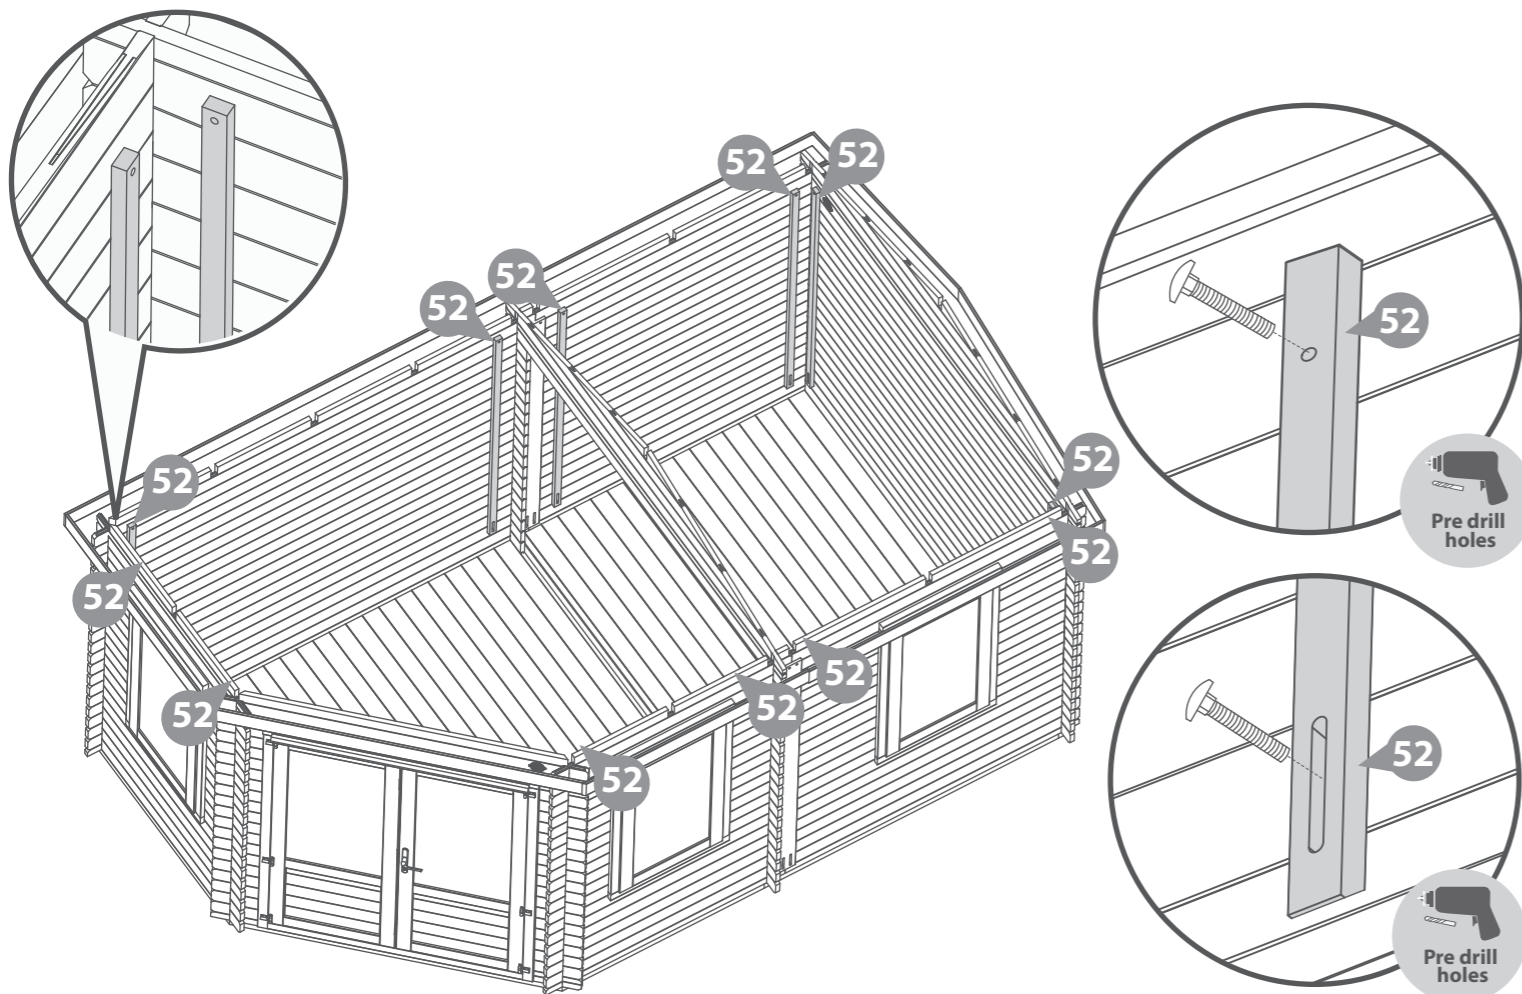


Step 54

Once constructed, apply a preserving and a waterproofing treatment to your garden building as soon as possible. This will help to protect your building and prevent decay.

See page 41 for a full guide and instructions.

****Please note:** This image is for illustrative purposes and may differ from the assembly you have constructed, however the process of treating the building is the same.

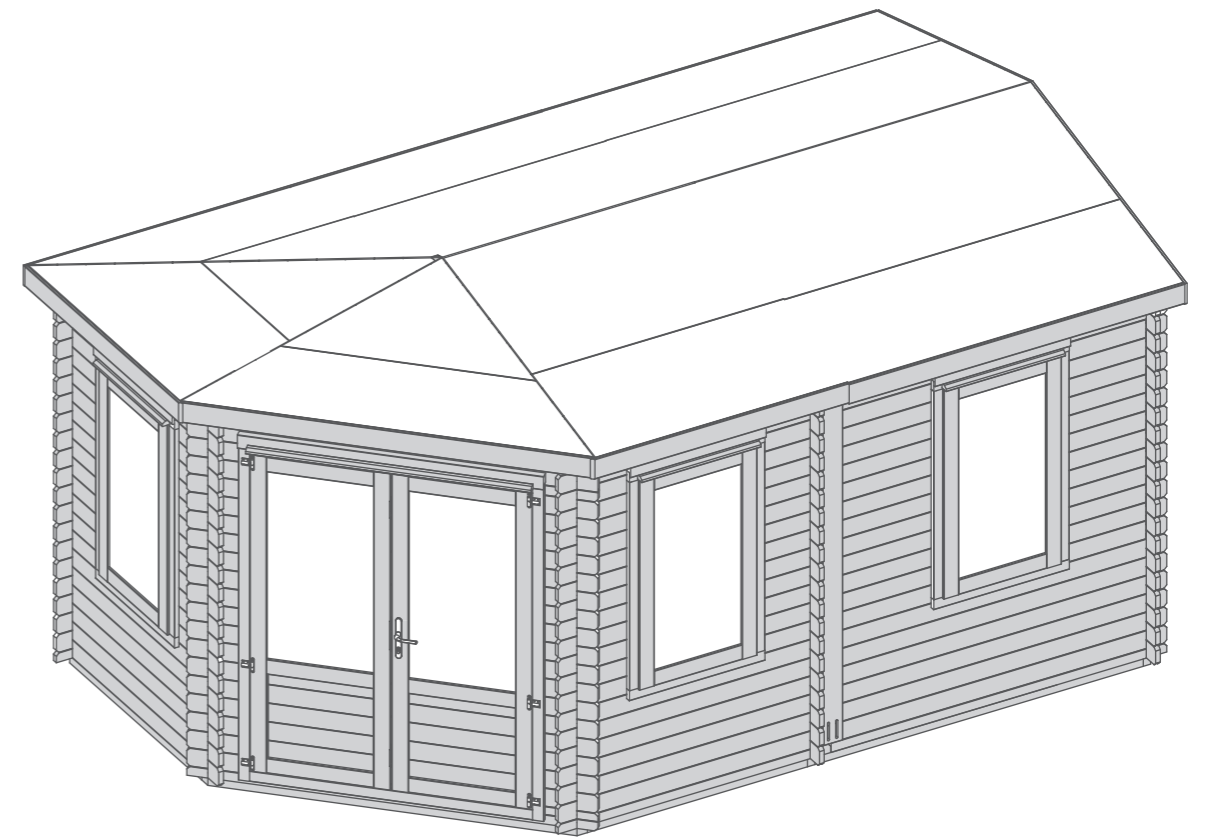

LEAVE US A REVIEW...

Want to share your experience with us? Leave us a review on Feefo, TrustPilot or Google.

Your reviews help other people find and trust our business, as well as helping to play an important role in our growth and improvement!

TREATING YOUR GARDEN BUILDING

Preservation of wood that's outdoors is vital. A little early care will help protect your garden building, improve its appearance and ensure maximum longevity. Insects, moisture, salt, and changing weather can have dramatic effects on the stability and appearance of your garden building. Once your building is installed, you've checked it over and you're happy with it, you can take a few basic precautions to prepare it for the elements. Treating your garden building helps prevent decay and, by repelling water, discourages the growth of moulds and fungi that could jeopardise the structural integrity of the wood.

Dip Treated buildings - Require a preservative treatment to protect against rot and decay and a waterproof treatment to prevent water ingress

Pressure Treated buildings - Require a waterproof treatment to prevent water ingress

Log Cabins/Insulated Garden Rooms - Are supplied untreated and require a preservative and waterproofing treatment.



ANY QUESTIONS?

Scan the QR code to contact us via our customer portal.

To apply a preservative and water proofing treatment (pressure treated products do not require a preserver), follow the manufacturer's instructions but in principle, stick to the following steps:

- ✓ Weather permitting, ensure to treat your garden building within 14 days of installation.
- ✓ Wear latex or rubber gloves, eye protection and (if spraying) a mask.
- ✓ Prepare the wood, by sanding down any ridges or inconsistencies in the wood, smoothing out knots and end-cuts.
- ✓ Choose a dry day to treat your garden building. If you're spraying rather than brushing paint on, avoid a windy day.
- ✓ Be sure you can safely reach all the sections you need to paint - and if you need a ladder, make sure it's safely positioned before climbing. Lay dust sheets around to avoid paint splatters on your base or surrounding plants.

- ✓ Tape around windowpanes to avoid smears when you're painting the frames.
- ✓ Keep pets and small children out of the way. The last thing you want is to have fur on your garden building paint, or little painted footprints all over your garden and home.
- ✓ Fill any gaps in the building's body with caulk or wood filler to prevent water and draughts getting in. Silicone based caulk is flexible and will move with the timber when temperature and humidity change. Allow to dry completely before treating. A handy tip for finding gaps is to go into your garden building and look for light leaking through joints and frames. If light gets in, then so will water.
- ✓ Liberally apply at least two coats of the treatment products with a brush or spray, taking care to allow the first coat to completely dry before applying the second.
- ✓ Make sure the solution permeates the whole of the surface area, especially around natural cracks, end cuts and nail/screw holes.



APPLY WOOD TREATMENT
IMMEDIATELY
AFTER ASSEMBLY

PLEASE SCAN HERE TO
SEE TREATMENT VIDEO:



1 Perimeter

Check around the perimeter of your product to ensure there are not trees or plants that are in contact with or overhanging the building. This can affect airflow and overhanging trees, or branches can damage the roof, it is advised to keep plants at a distance.

2 Repair

Inspect the interior and exterior of the product to look for splits, cracks, and holes. Although this is a natural occurrence it can be prevented. A wood filler can be used to close the splits, cracks, and holes.

3 Roof

Check your roof regularly for tears, splits, damaged wood and fallen debris. If you notice any of this immediate repair is critical.

4 Doors & Windows

Expansion and contraction can cause doors and windows to stick or become difficult to open. Small adjustments to the hinge position can be made to the doors and windows to allow free movement.

5 Oil

Hinges can seize up over time, apply lubricant to the hinges and locks annually.

6 Screws & Bolts

It is advised to check all screws and bolts and tighten any loose you might find. For log cabins specifically the storm braces will require loosening. During humidity and temperature changes (seasons) to allow expansion and contraction to prevent gaping, twisting, popping, and warping.

7 Wash

At least once a year, give the outside of you building a good wash, to remove cobwebs, leaves, or any other dirt that may accumulate on the exterior.

8 Airing

Airing your product regularly prevents the build up of condensation which can cause the timber to warp, bow, boards to pop, distortion, rot and mould. Condensation can build up over time or daily, it is caused by a rise and fall in temperature.

Excessive moisture levels within your building can cause water to collect on the roofs, walls and floors internally. Leaving doors and windows open regularly can help combat the natural moisture build up.

9 Storm Braces

The storm braces will need to be altered during the buildings life as the moisture content within the log boards changes, altering the braces will help your building expand and contract properly. The boards will expand during periods of high moisture (Winter) and shrink during periods of low moisture (Summer).

Ensure each bolt is tightened using a washer so as not to damage the log boards.

10 Clean & Tidy

It is good practice to clean the inside and outside of your product regularly. Clear out the contents, sweep the floor, remove dirt and cobwebs. Check for areas of damp and investigate the cause to remove and prevent future occurrences. Check the ground around your product for build up of debris such as leaves, remove and ensure there is clear ventilation underneath the floor.

Additional Playhouse Maintenance:

It is recommended that the following checks and maintenance are carried out at the beginning of each season as well as at regular intervals during the usage season.

- Check all nuts /bolts/ screws for tightness and tighten when required.
- Check for movement / opening of wood giving rise to protrusion of nail heads and tips.
- Check hinges.
- Replace defective parts in accordance with the manufacturers instructions.
- Check any crossbeams, suspensions and anchors.
- If a swing is included; check the swing seat, chains and ropes.

IF THESE CHECKS ARE NOT CARRIED OUT THE ACTIVITY TOY COULD BECOME A HAZARD

All our garden buildings have been designed and manufactured with care and attention to be the perfect addition to your outdoor space. To ensure you do get the best out of your new garden building and to increase the longevity we advise that you follow the product instructions and our manufacturer's recommendations as detailed below. Thank you for choosing a Mercia Garden product!

1 Choosing the most suitable location for your garden building...

A minimum of 60cm should be left around the perimeter of your garden building to allow access for maintenance, annual treatment and to allow air flow around the building.

Where possible you should avoid placing your garden building underneath large trees to prevent the tree causing damage to the building.

2 Preparing the base for your garden building...

All our buildings must be built on a firm, level base to ensure the longevity of the building and prevent the wood from distorting. We recommend either concrete, concrete slabs or a wooden base, such as our 'Portabase'.

The base should be slightly smaller than the external measurement of the building, i.e. the cladding should overlap the base, creating a run off for water and preventing water from pooling underneath the building.

We also recommend that the floor of the garden building is a minimum of 25mm above the surrounding ground level to avoid flooding.

3 After installation...

Once your garden building has been installed, it will need to be treated within 14 days (weather permitting) and annually to prevent the timber from deteriorating and to waterproof it. This is required to maintain the anti-rot guarantee.

Dip Treated buildings - Require a preservative treatment to protect against rot and decay and a waterproof treatment to prevent water ingress.

Pressure Treated buildings - Require a waterproof treatment to prevent water ingress.

Log Cabins/Insulated Garden Rooms - Are supplied untreated and require a preservative and waterproofing treatment.

We also recommend using a silicon sealant on the inside and outside of the windows as soon as possible after assembly and treatment to fully seal the windows.

Roofing felt/covering should be checked annually and replaced or fixed accordingly.

4 General maintenance and wood characteristics

As wood is a natural material it may be affected by the following:

Shrinkage and warping - The timber used in the construction of your garden building will have retained some of its natural moisture content. The moisture content of the timber will vary, depending upon prevailing environmental conditions, which will result in the components either naturally expanding or contracting. As the components dry out, shrinkage may occur. A good waterproofing treatment from the start is the best protection to minimise the effect of moisture loss/intake.

In extended periods of very warm weather getting some moisture to the building will help the overall balance. You can do this by spraying it down lightly with a garden hose. In contrast, after snow fall try to remove the snow as best as possible from the roof to prevent moisture intake and to remove the extra weight.

Top tip - using a garden brush will help you to reach the highest part of the building to remove snow and any debris left from bad weather.

Damp and mould - During the winter months, cold and damp conditions can result in an increased amount of moisture within your garden building, especially when used infrequently. Condensation can form on the timber and other items stored within your garden building. If left this moisture is likely to cause mould and mildew.

To prevent the build-up of moisture, we recommend leaving the door or windows of your building open from time to time, to allow the fresh air to circulate. We also advise against storing wet or damp items in your garden building as this will also increase the level of moisture in the building. If mould or mildew does start to form within your building we recommend using an anti-mould cleaner to remove it and to prevent it spreading, which if left untreated could permanently damage your garden building.

Splits, cracks and knots - You may notice small splits and cracks in some components or holes may appear where knots shrink and fall out. This will not affect the structure of your Garden building however, if you wish to fill them this can be easily done using any good quality wood filler.

Sap - is naturally occurring in wood and may appear in some boards of your garden building. If you wish to remove the sap, we advise waiting until it is dry and then using a sharp knife to carefully remove it. If the removal of the sap causes a hole in the timber, we recommend using a good quality wood filler to fill it.

For more handy hints and tips on how to care and maintain your garden building please refer to the MGP Customer Portal at www.mgplogistics.co.uk

Any further questions?

Contact our
Customer Service Team via the MGP
Customer Portal at:
www.mgplogistics.co.uk

1 Manufacturer's Warranty

All Mercia Garden Products are supplied with a 1 year warranty on all parts against manufacturing defects.

This warranty does not cover movement, warping or splitting of timber products over time.

This warranty will be voided if any of the following occur:

1. The building has been customised or modified/adapted in any way.
2. The person claiming is not the original purchaser of the building.
3. Any damage has been caused by or as a result of misuse.
4. The building has not been maintained and cared for in accordance to our advisories and manufacturer's recommendations.
5. The building has not been treated annually or as per the manufacturer's recommendations, please ensure receipts are kept to validate this claim.
6. The building has not been erected, fitted or installed as per the supplier instructions.
7. The building has not been erected on a suitable sized firm flat, solid level concrete/slab base or placed on pressure treated bearers.
8. The building is or has been placed with 2 feet (600mm) of any obstructions (walls, trees, plants, fences etc.) which can allow moisture to penetrate the timber.
9. The roofing felt has been incorrectly fitted or damaged, allowing water ingress, or has not been properly maintained.
10. Any windows and joints have not been sealed, inside and out, with silicone or other watertight sealant.
11. Any timber has been cut, pierced or drilled without subsequent application of approved cut-end treatment.

2 Anti-rot Guarantee


Mercia Garden Products offer a 10 year anti-rot guarantee on all dip treated (a preparatory treatment) and 15 years on all pressure treated products. This guarantee covers solid timber against rot, decay, blue stain and insect attacks.

To validate the guarantee the building must be treated (as detailed within manufacturer's recommendations) within 14 days (weather permitting) of assembly and annually thereafter.

This guarantee does not cover movement, warping or splitting of timber products over time.

This guarantee will be voided if any of the following occur:

1. The building has been customised or modified/adapted in any way.
2. The person claiming is not the original purchaser of the building.
3. Any damage is caused by or as a result of misuse.
4. The building has not been maintained and cared for in accordance to our advisories and manufacturer's recommendations.
5. The building has not been treated annually or as per the manufacturer's recommendations, please ensure receipts are kept to validate this claim.
6. The building has not been erected, fitted or installed as per the supplier instructions.
7. The building has not been erected on a suitable sized firm flat, solid level concrete/slab base or placed on pressure treated bearers.
8. The building is or has been placed with 600mm of any obstructions (walls, trees, plants, fences etc.) which can allow moisture to penetrate the timber.
9. The roofing felt has been incorrectly fitted or damaged allowing water ingress, or has not been properly maintained.
10. Any windows and joints have not been sealed, inside and out, with silicone or other watertight sealant.
11. Any timber has been cut, pierced or drilled without subsequent application of approved cut-end treatment.



REGISTER FOR YOUR
ANTI-ROT
GUARANTEE TODAY

PLEASE SCAN HERE:

